


Q1

Please confirm the base plate and anchor bolt details for the green-clouded column, as shown in Snap #01.

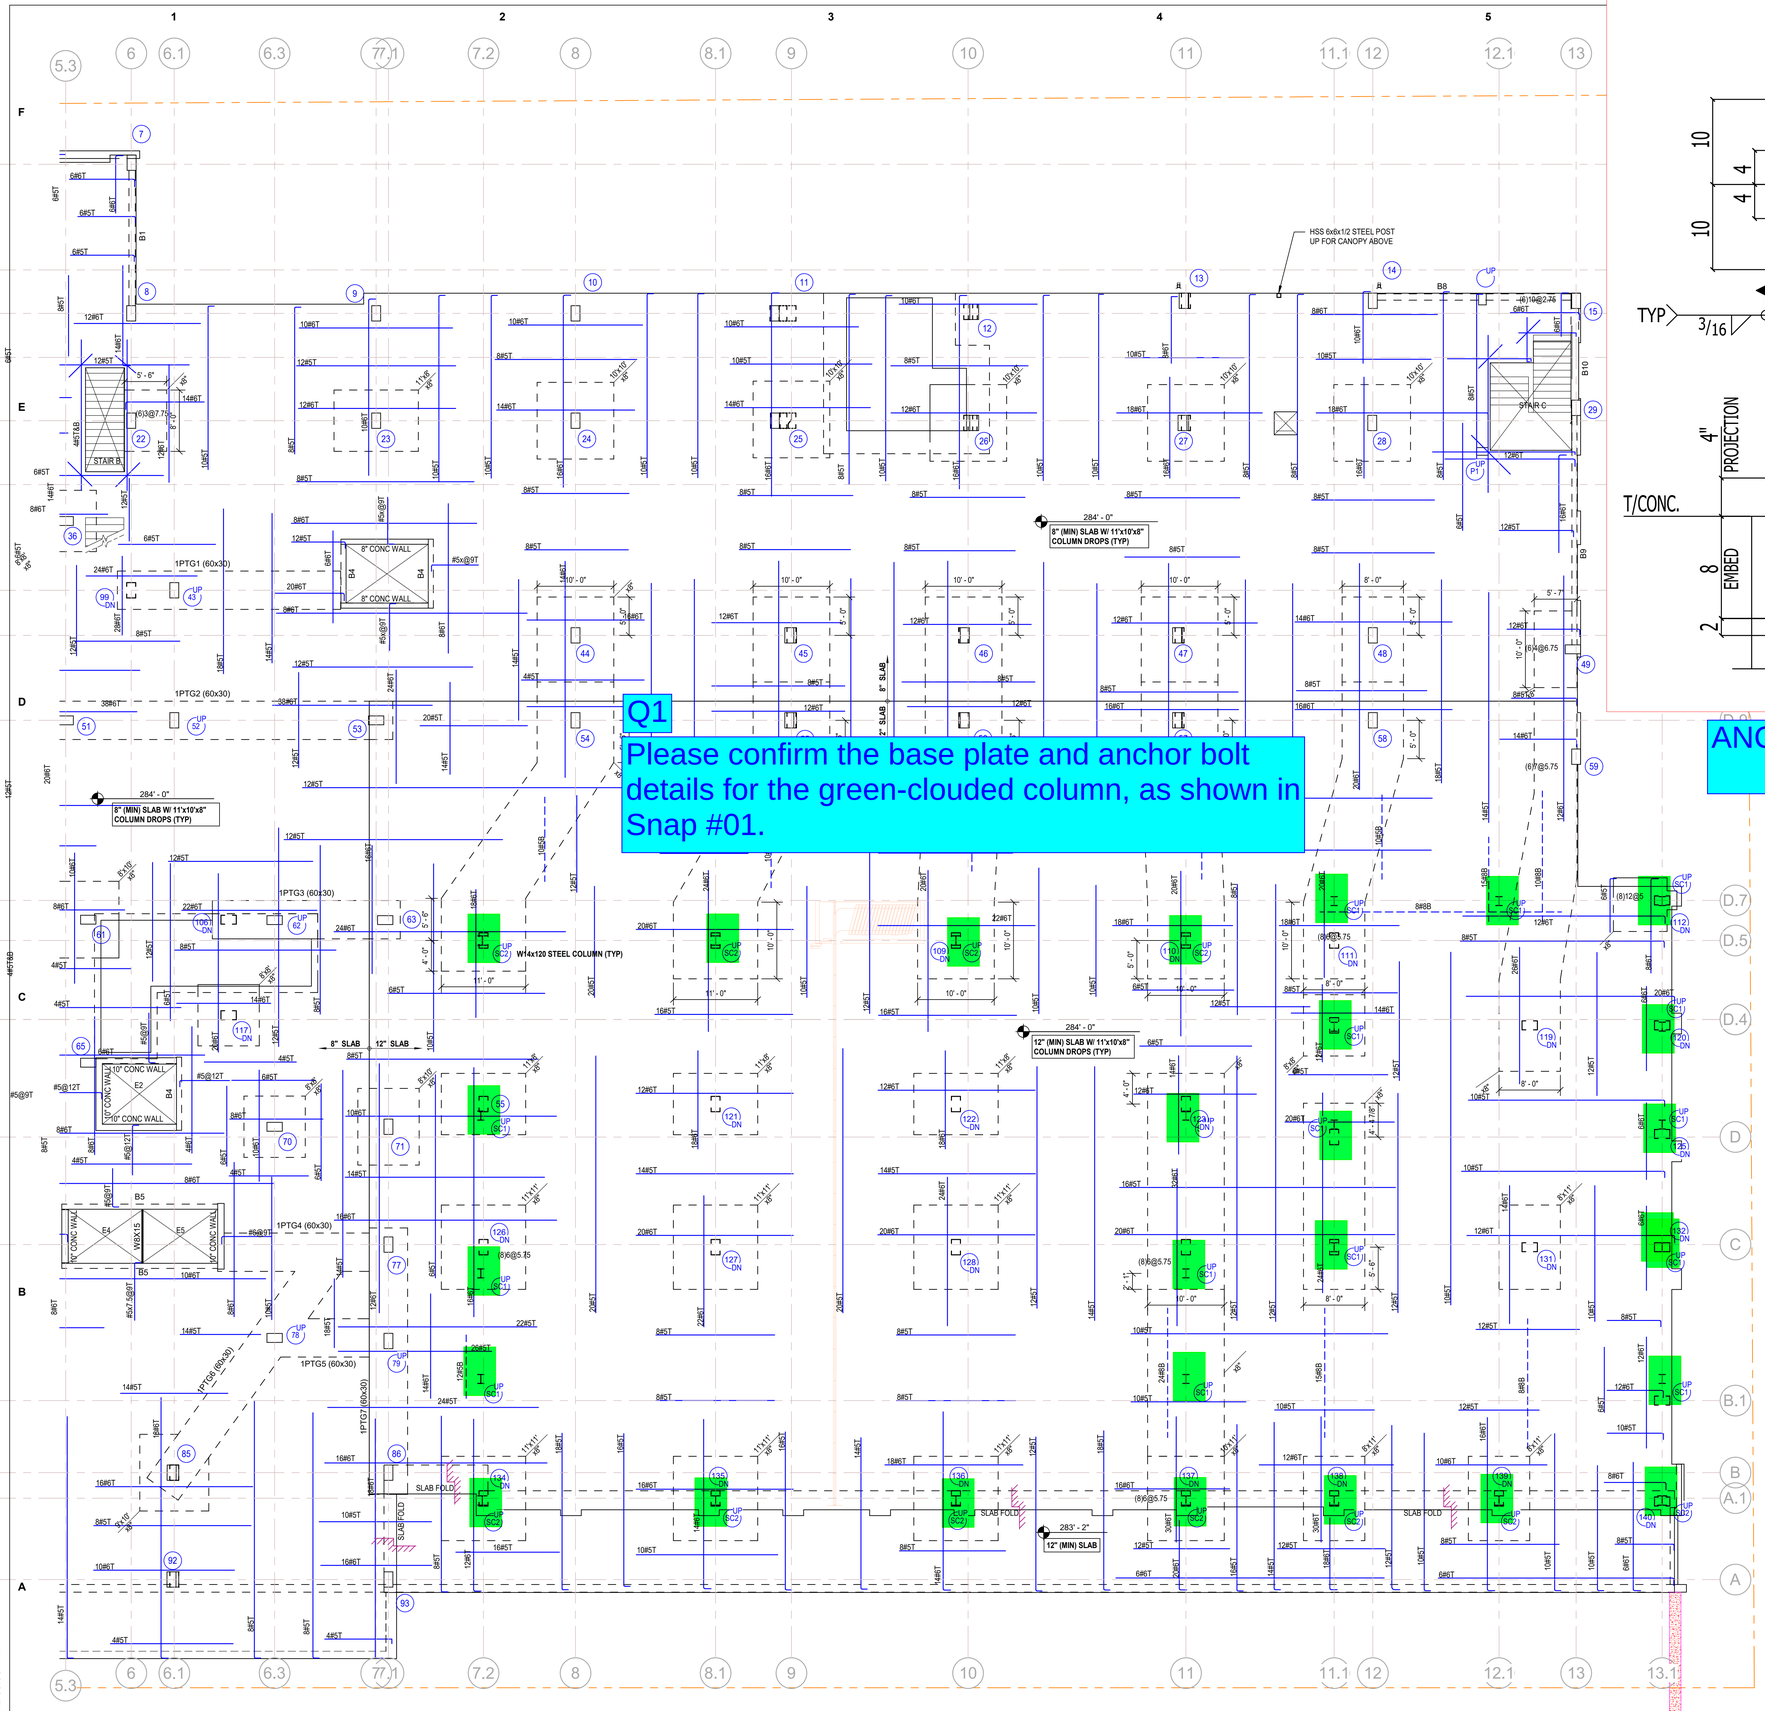


ANCHOR BOLT DETAILS
SNAP#01

1 LEVEL 1 PLAN - PART B
1/8" = 1'-0"

**SLAB NOTES**

1. TOP OF SLAB ELEVATION SEE PLAN & ARCH DWGS.
2. FLOOR SLAB TO BE 8" (MIN) CONCRETE SLAB REINF W/ #5@10" BOT EACH WAY (GENERAL REINF) & 12" (MIN) CONCRETE SLAB REINF W/ #6@10" BOT EACH WAY (GENERAL REINF).
3. "T" DENOTES TOP BARS; "B" DENOTES BOTTOM BARS.
4. ALL REINF SHOWN ON PLAN SHALL BE IN ADDITION TO GENERAL REINF (U.N.O.)
5. PROVIDE 3/4" CONCRETE COVER FOR TOP & BOTTOM BARS IN SLAB (U.N.O.)
6. ALL REINF STEEL (TOP & BOTTOM) IN THE SLABS EXPOSED TO WEATHER (i.e. BALCONIES) TO BE EPOXY COATED AND SHALL HAVE 1 1/2" CONCRETE COVER FOR TOP BARS (U.N.O.)
7. 28 DAY CONCRETE STRENGTH OF SLAB, f'c= 5000 psi (NWC). TYPICAL (U.N.O.)
8. [(3)#SR] DENOTES SHEAR HEAD REINFORCING EACH WAY SEE TYPICAL DETAILS.
9. DESIGN LIVE LOAD = 100 psf AT LOBBIES, RESTAURANT, BALL ROOMS, OFFICE AND AMENITY
   = 450 psf AT FIRE ENGINE ACCESS
10. DO NOT REMOVE SHORING BELOW THE HANGING FLOOR SLAB WHICH ARE SUPPORTED BY THE HANGERS UNTIL THE FLOOR SLAB ABOVE ACHIEVE 28 DAYS STRENGTH.
11. ► DENOTES SLOPING COLUMN, SEE COLUMN SCHEDULE
12. DROP PANELS EXTEND 8" MINIMUM BELOW THE LOWEST SLAB ELEVATION AT EACH COLUMN U.N.O.

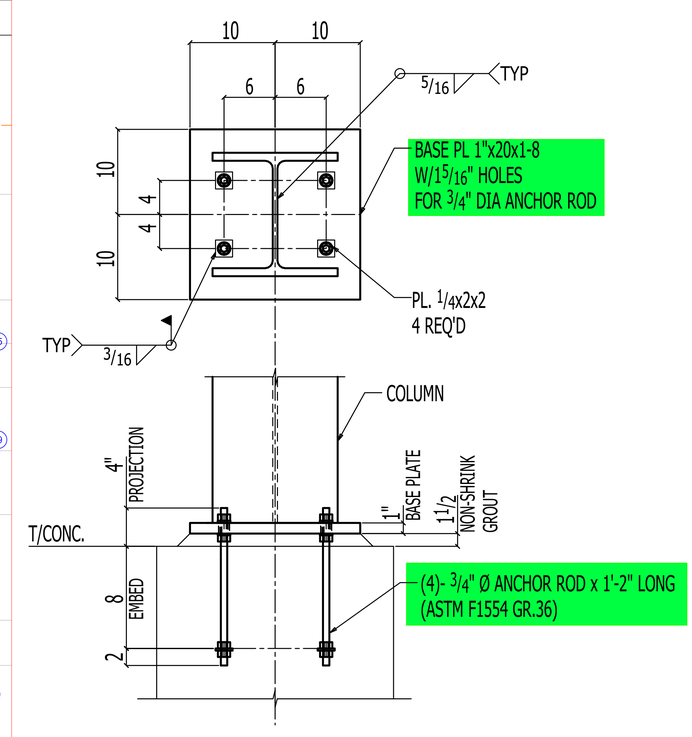OUTERMOST LAYER

SK#06
01 pages
01-Queries
Date: 01-19-2026


FILLAT+ ARCHITECTURE
400 E. PRATT | SUITE 502 | BALTIMORE MD | 21202
Ph: 410.576.9310 | PFARC.COM

STRUCTURAL ENGINEER
TADJER-COHEN-EDELSON ASSOCIATES ,INC.
1109 SILVER SPRING ST., SUITE 510
SILVER SPRING, MD 20910
(301) 587-1820
12402000

MEP ENGINEER
ALLEN & SHARIFF ENGINEERING, LLC
7061 DEEPAGE DRIVE
COLUMBIA, MD 21045
(443) 545-7100

CIVIL ENGINEER
BOHLER
901 DULANEY VALLEY ROAD, SUITE 801
TOWSON, MD 21204
(410) 821-7900

INTERIOR DESIGNER
LOONEY & ASSOCIATES
20 N WACKER DR. SUITE 2010
CHICAGO, ILLINOIS 60606
(312) 329-0464

LANDSCAPE
EDSA
400 E. PRATT STREET, SUITE 502
BALTIMORE, MARYLAND 21202
(443)539-3350

TEHNOLOGY
MICHAEL RAISER ASSOCIATES, INC.
500 VALLEY ROAD SUITE 106
WAYNE, NJ 07470
(973)305-0011


# FREDERICK CONFERENCE CENTER HOTEL
20 SOUTH CARROLL STREET
FREDERICK, MARYLAND, 21701

Copyright © 2025 Fillat + Partners Inc. All rights reserved

IFC SET

**LEVEL 1 PLAN - PART II**

| | |
|---|---|
| PROJECT NO.: | 13013 |
| SCALE: | 1/8" = 1'-0" |
| DATE: | 12.19.2025 |

REVISIONS:

| | | |
|---|---|---|
| 1 | PRE-GMP | 06.09.25 |
| 2 | IFC SET | 12.19.25 |

**S103B**

12/19/2025 12:56:56 PM
