Q1

Please review the yellow clouded note and advise.

G.C. VERIFY LOCATION WITH OWNER IS ACCEPTABLE. ONLY ONE PERSON CAN TIE OFF TO POST AT ANY GIVEN TIME.

APPROVER,
PLEASE CONFIRM CLOUDED TIE OFF POINT POST LOCATION IS OK TO PROCEED?

PROVIDE W12x65 BEAM BELOW SLAB BETWEEN W16x31 FLOOR BEAMS TO CONNECT TIE OFF POST. PROVIDE THRU-BOLTS FROM POST BASE PLATE TO TOP FLANGE OF BEAM OR WELD POST DIRECTLY TO TOP OF BEAM

PROVIDE 3 PAIRS OF 3/8" THICK FULL DEPTH FITTED STIFFENERS BELOW POST. USE DOUBLE ANGLE CONNECTIONS EACH END OF BEAM - 2L3x3x3/8 x 8" LONG WITH 3-SIDED 1/4" FILLET WELDS ON EACH LEG. COPE TOP FLANGE AS REQUIRED.

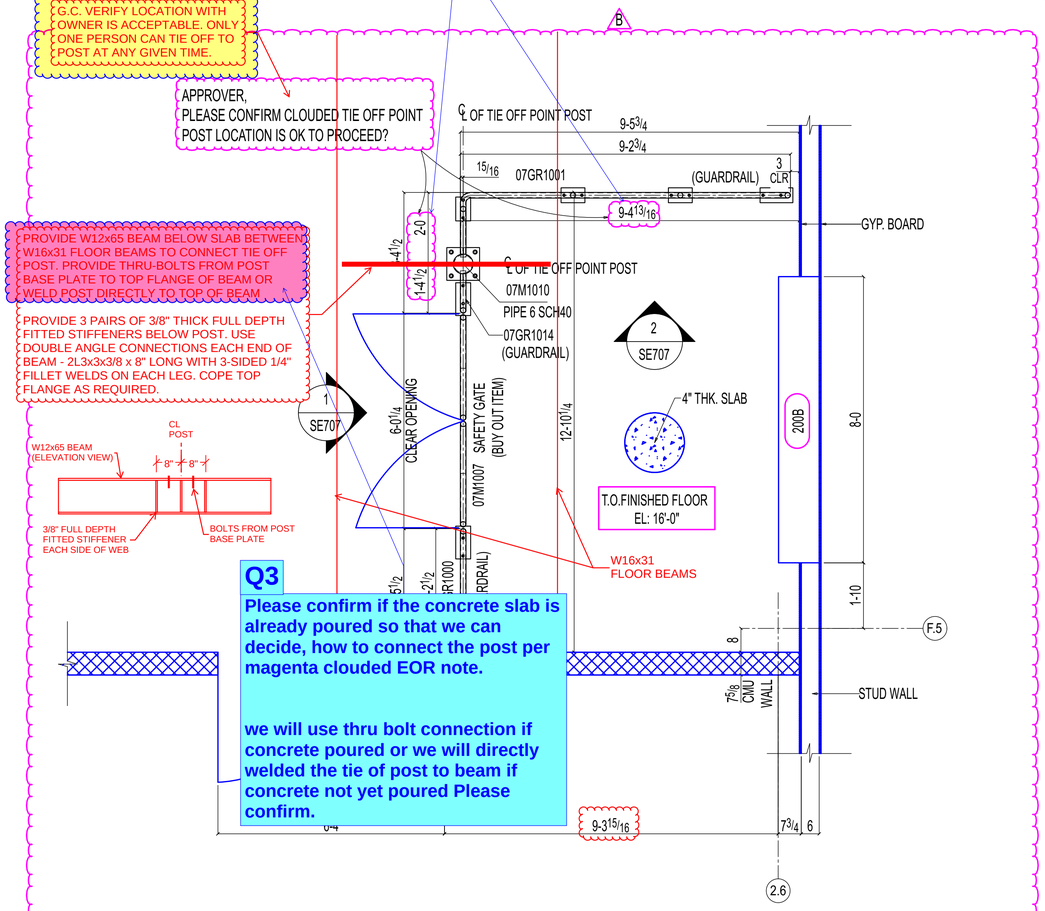

Q3

Please confirm if the concrete slab is already poured so that we can decide, how to connect the post per magenta clouded EOR note.

we will use thru bolt connection if concrete poured or we will directly welded the tie of post to beam if concrete not yet poured Please confirm.

1 / E703 MEZZANINE GUARDRAIL PLAN

(REF:1/A380)

TRUE NORTH PROJECT NORTH

NOTE:
1. ALL ELEVATION ARE REFERENCED FROM THE FINISHED FLOOR EL: [0'-0"] = DATUM EL: 100'-0" (U.N.O).
2. ALL GUARDRAILS ARE PIPE 1 1/2 SCH40 (U.N.O)

VERIFY CLOUDED DIMENSIONS - THEY ARE DIFFERENT THAN PREVIOUS SUBMITTAL AND DO NOT MATCH ARCH DRAWINGS

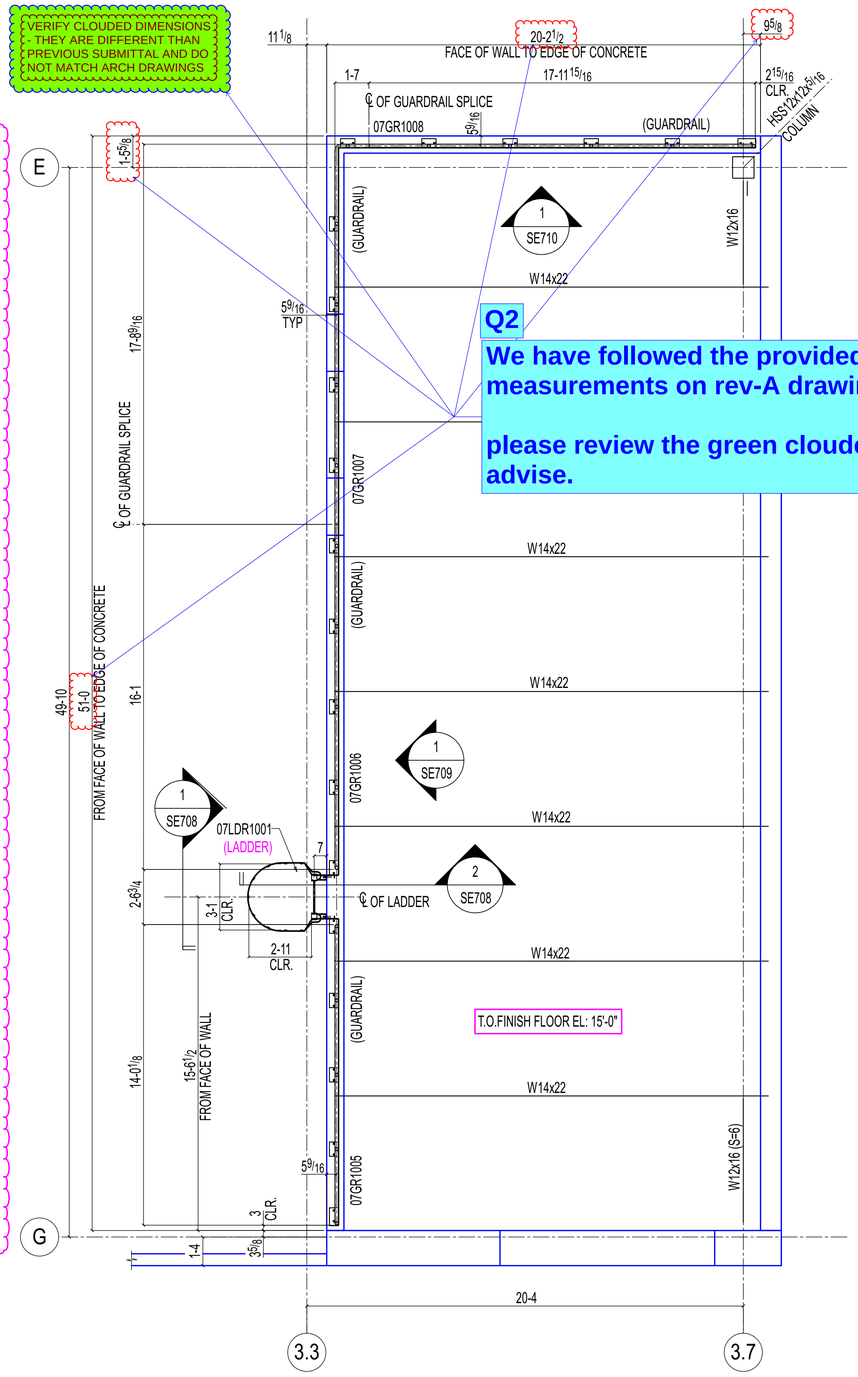

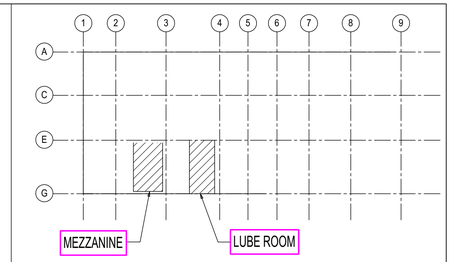

KEY PLAN

Q2

We have followed the provided field measurements on rev-A drawings.

please review the green clouded note and advise.

2 / E703 LUBE ROOM DUST CAP (LADDER AND GUARDRAIL PLAN)

(REF: 1/A102,5/A173)

TRUE NORTH PROJECT NORTH

NOTE:
1. ALL ELEVATION ARE REFERENCED FROM THE FINISHED FLOOR EL: [0'-0"] = DATUM EL: 100'-0" (U.N.O).
2. ALL GUARDRAILS ARE PIPE 1 1/2 SCH40 (U.N.O)

SK#31
03-06-2026

REVISIONS

REV#	DWN BY	DESCRIPTION	DATE
A	SRP	ISSUED FOR APPROVAL	Jun 16 2025
0	GSV	ISSUED FOR CONSTRUCTION	Jan 27 2026
B	GSV	ISSUED FOR RE-APPROVAL	Feb 23 2026

THE INFORMATION NOTED HEREON THIS DRAWING IS THE PROPERTY OF STEEL FAB ENTERPRISES, INC. AND SHALL NOTED BE USED WITHOUT WRITTEN CONSENT.

STEEL FAB ENTERPRISES, LLC
AISC CERTIFIED FABRICATOR AND ERECTOR
MISCELLANEOUS METALS FABRICATOR AND ERECTORS
623 BAUMGARDNER ROAD, LANCASTER, PA 17603
TEL. (717)464-0330 FAX (717)464-9464
WWW.STEELFABENTERPRISES.COM

PROJECT OWNER : CK CAPITAL, LLC
PROJECT DESCRIPTION : CLEVELAND BROTHERS-MILESBURG
PROJECT ADDRESS : 4025N. EAGLE VALLEY ROAD, HOWARD, PA 16841
CONTRACTOR : KINSLEY CONSTRUCTION, INC.

DRAWN BY : BAS	DATE : 5-20-25	PROJ. NO. : 25912	REV # B
CHECKED BY : SRP	DATE : 5-20-25	DWG NO. : E703	

DWG DESCRIPTION : GUARDRAIL & LADDER PLAN

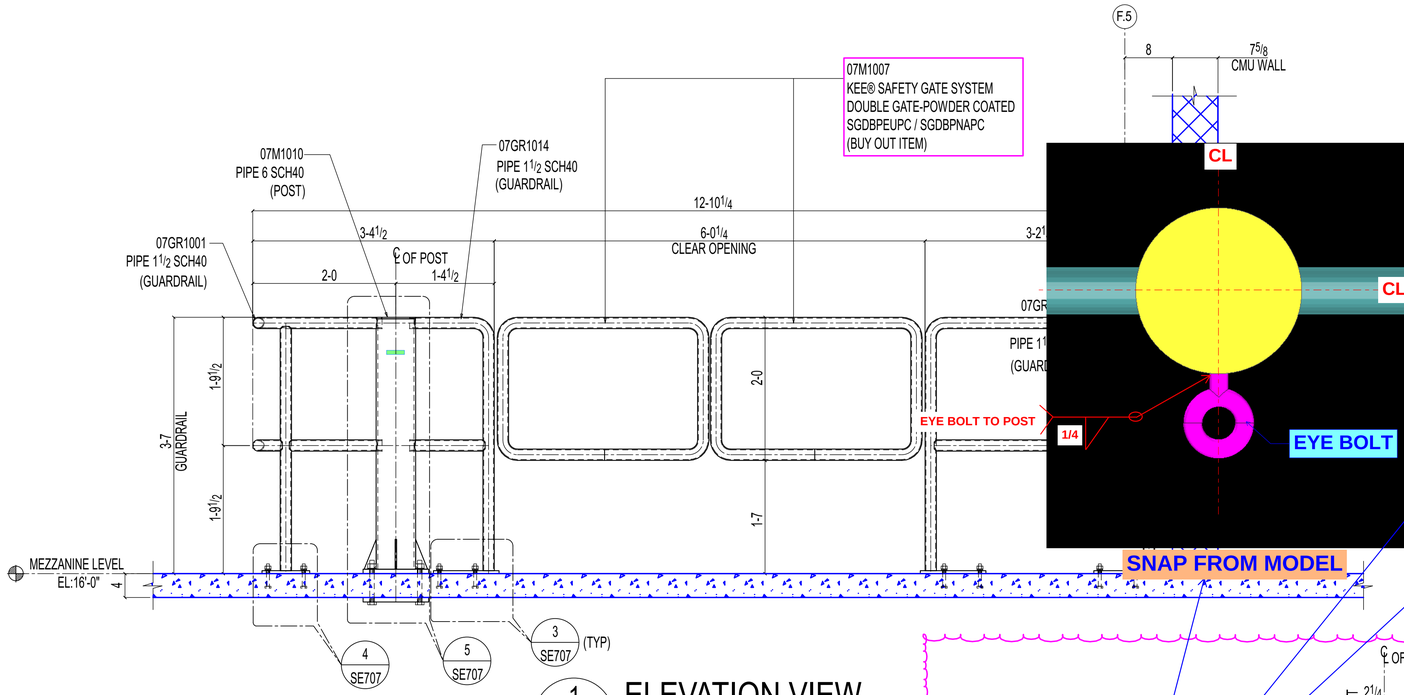

1 SE707 ELEVATION VIEW

(REF: 1/A380)

OTHER NOT SHOWN FOR CLARITY

APPROVER,
PLEASE REVIEW SHOWN TIE OFF POINT SUPPORT ARRANGEMENT AND LET US KNOW IF ANY ADDITIONAL STEEL REQURED FOR THIS.

Q4

Per EOR comment, Please confirm the 3/4" Ø eye bolt details and the eye bolt location (green clouded) are OK to proceed?

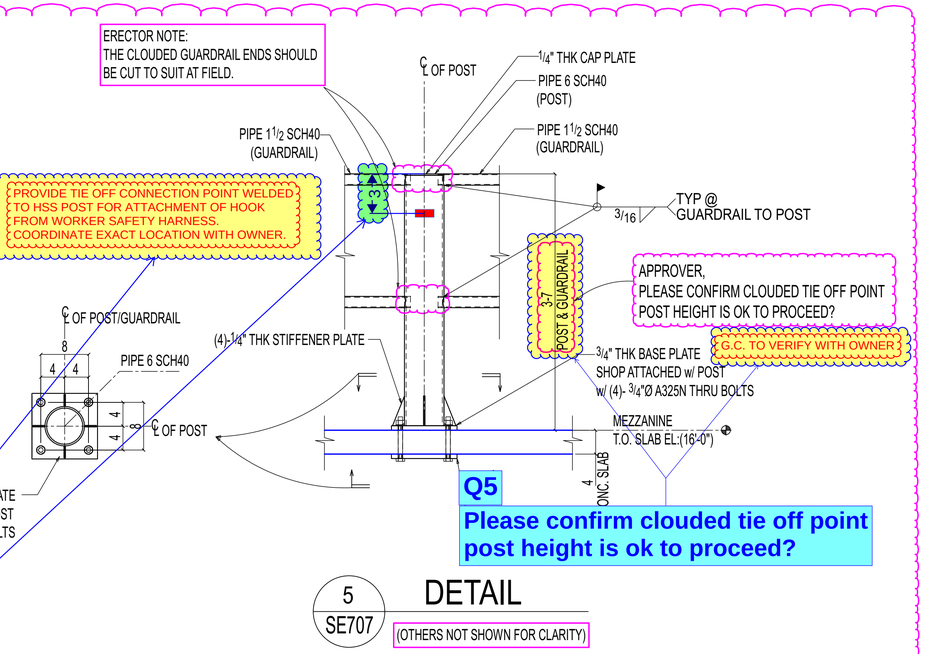

Q5

Please confirm clouded tie off point post height is ok to proceed?

5 SE707 DETAIL

(OTHERS NOT SHOWN FOR CLARITY)

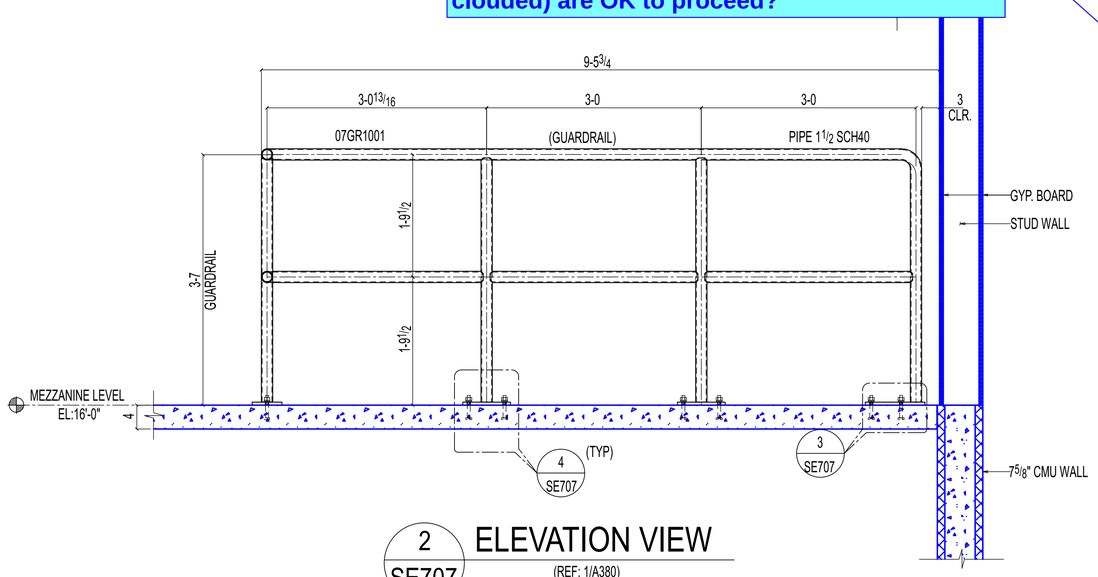

2 SE707 ELEVATION VIEW

(REF: 1/A380)

OTHER NOT SHOWN FOR CLARITY

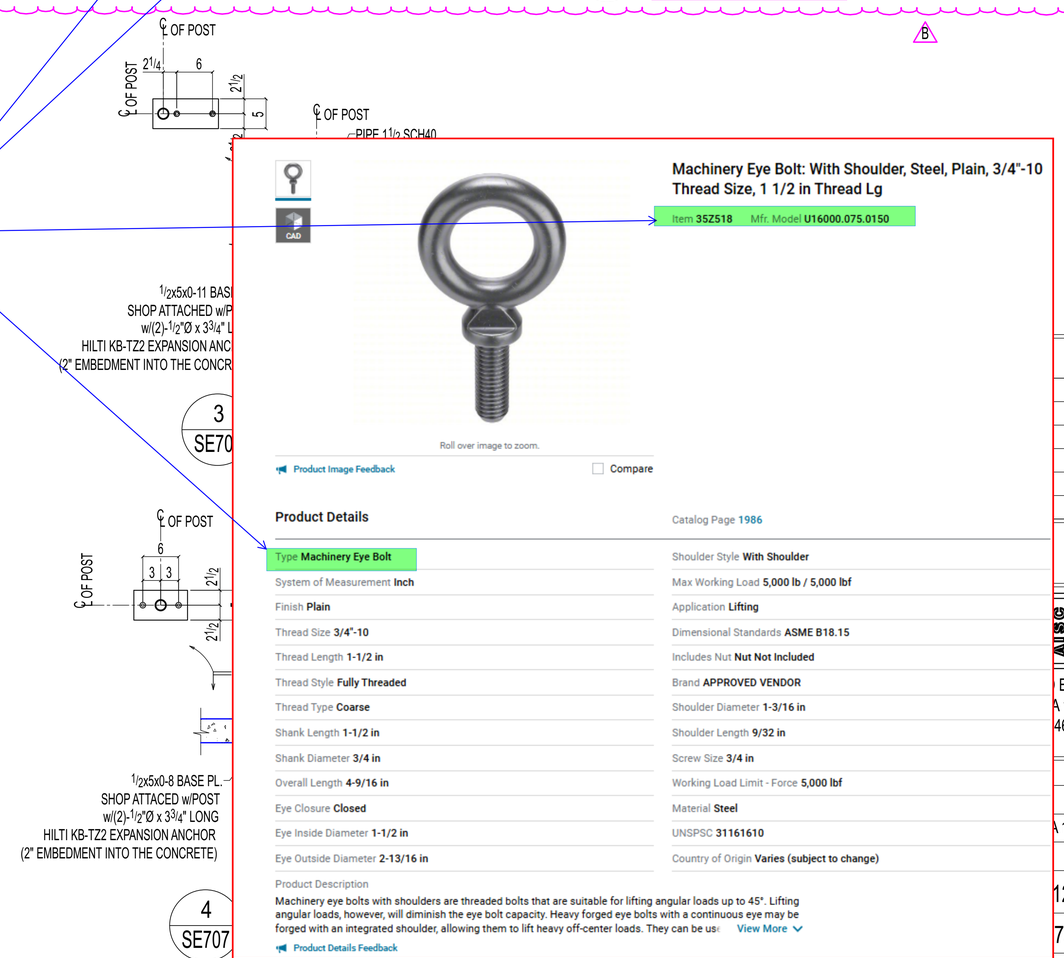

SNAP FROM PRODUCT DATA

	DATE
	Jun 16 2025
	Jan 27 2026
	Feb 23 2026

AISC CERTIFIED FABRICATOR AND ERECTOR

ERECTORS
A 17603
464

A 16841

12
707

REV #
B

IL ELEVATION VIEW
