NOTE IF THIS SHEET IS NOT 36"W X 48"L THEN IT IS NOT THE INTENDED SIZE. IN ALL CASES WORK TO FIGURED DIMENSIONS.

RED HIGHLIGHTED GRIDS HAVE CONFICT IN PLAN LOCATIONS.

GREEN HIGHLIGHTED GRIDS NOT COVERD IN PLANS.

MAGENTA HIGHLIGHTED GRIDS HAVE CONFICT & NOT COVERD IN PLANS.

COLUMN SIZE	FLANGE PLATES WIDTH	FLANGE PLATES THICKNESS	FLANGE PLATES LENGTH	NUMBER OF BOLTS BELOW SPLICE
W14X455 TO 730	16"	3/4"	1'-6 1/2"	8
291 TO 426	14"	5/8"	1'-6 1/2"	6
145 TO 233	14"	1/2"	1'-6 1/2"	4
90 TO 132	14"	3/8"	1'-0 1/2"	4
48 TO 82	8"	3/8"	1'-0 1/2"	4
W12X120	8"	5/8"	1'-0 1/2"	4
40	8"	3/8"	1'-0 1/2"	4
W10X3	8"	3/8"	1'-0 1/2"	4
W8X3				

Q1

Please review and advise on column schedule conflicts.



NOTES:
1) DEPTH OF d_f NOMINALLY TWO INCHES LESS THAN d_b (i.e. W8 ON W10, W10 ON W12....)
2) PER AISC, FABRICATOR SHALL "SELECT BOLTS THROUGH FILLERS (INCLUDING BOLTS THROUGH FLANGE PLATES) ON EACH SIDE TO DEVELOP BEARING STRENGTH OF THE FILLER."
3) REFER TO AISC 13th EDITION STEEL CONSTRUCTION MANUAL TABLE 14-3, CASE II.

2 COLUMN SPLICE - BOLTED (FOR GRAVITY COLUMNS)
SCALE: 3/4" = 1'-0"

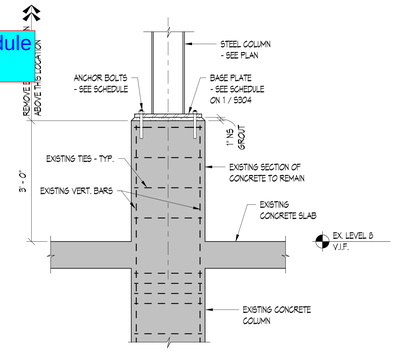

3 COLUMN BASE DETAIL - EXISTING PIER
SCALE: 3/4" = 1'-0"



NOTE:
CONTRACTOR TO LOCATE EXISTING REBAR PRIOR TO PLATE FABRICATION DO NOT DRILL THROUGH REBAR.

4 DETAIL
SCALE: 1 1/2" = 1'-0"

STEEL COLUMN SCHEDULE

COLUMN MARK / LEVEL	A-7	A-8	A-9	A-10	A-10.9	A-11.1	A-12	A-13	A-14	A-15	A.2-13	A.2-8	A.2-9	A.2-10	A.2-10.9	A.2-11.1	A.2-12	A.2-13	A.8-5.9	B-7	B-8	B-9	B-10	B-10.9	B-11.1	B-12	B-13	B-14	B-15	B.05-5	B.1-2	B.1-3	B.1-4	B.1-7.4	B.1-8	B.1-9	B.1-10	B.1-10.9	B.1-11.1	B.1-12	B.1-13	B.1-14	B.2-8	B.2-9	B.2-10
STAIR ROOF																																														
ROOF																																														
LEVEL 11																																		W8x31	W8x31	W8x31	W8x31	W8x31	W8x31	W8x31	W8x31	W8x31			
LEVEL 10																				W10x33								W10x33	W10x33					TRANSFER	TRANSFER	TRANSFER	TRANSFER	TRANSFER	TRANSFER	TRANSFER	TRANSFER	TRANSFER			
LEVEL 9											W10x31	W10x31	W8x31	W10x31	W10x31	W10x31	W10x31	W10x31																									W10x31	W8x31	W10x31
	W10x33	W10x77	W10x77	W10x60	W10x77	W10x77	W10x77	W10x77	W10x77	W10x33	TRANSFER	TRANSFER	TRANSFER	TRANSFER	TRANSFER	TRANSFER	TRANSFER	TRANSFER	W10x33	W10x33	W10x66	W10x66	W10x106	W10x60	W10x45	W10x66	W10x66	W10x45	W10x33	W10x33	HSS8x8x1/2	W10x33	W10x33										TRANSFER	TRANSFER	TRANSFER
LEVEL 8																																														
BASE PLATE (1/S301)	BP-1	BP-5	BP-5	BP-5	BP-5	BP-7	BP-5	BP-5	BP-5	BP-1									BP-1	BP-1	BP-5	BP-5	BP-13	BP-7	BP-8	BP-5	BP-5	BP-4	BP-1	BP-1	BP-2	BP-1	BP-1												
AXIAL LOAD (KIPS)	60	95	95	75	40	50	90	95	65	75	30	75	75	75	40	40	75	55	65	140	175	175	195	100	90	170	175	230	165	65	60	60	60	15	50	55	55	25	30	55	55	50	100	105	70
SHEAR LOAD (KIPS)																																														
MOMENT (KIPS-FT)																																														

STEEL COLUMN SCHEDULE

COLUMN MARK / LEVEL	B.2-10.9	B.2-11.1	B.2-12	B.2-13	B.9-6.8	B.9-7.4	B.9-7.8	B.9-8.4	B.9-9	C-3	C-4	C-5	C-8.8	C-6	C-10	C-10.9	C-11.1	C-12	C-13	C-14	C.4-3.8	C.4-4	C.4-4.9	C.4-5.4	C.4-6	C.6-2.3	C.6-9	C.8-6.8	C.8-7.4	C.8-7.8	C.8-8.4	D-3	D-3.1	D-4	D-10	D-10.9	D-11.1	D-12	D-13	D-14	D-15	D.3-2.3	D.4-4.9	D.4-5.4	D.4-6
STAIR ROOF																																														
ROOF																																														
LEVEL 11													W8x31								W8x31	W8x31											W8x31													
LEVEL 10					HSS8x8x1/2	HSS8x8x1/2	W10x33	W10x33	W10x45	W10x54	W10x33	W10x33	TRANSFER	W10x33	W10x54	W10x45	W10x60	W10x45	W10x45	W10x45	TRANSFER	TRANSFER	W10x45	W10x33	W10x33		W10x45	HSS8x8x1/2	HSS8x8x1/2	W10x33	W10x33	W10x66	TRANSFER	W10x66	W10x45	W10x45	W10x45	W10x45	W10x45	W10x77	W10x66		W10x45	W10x33	W10x33
LEVEL 9	W8x31	W8x31	W8x31	W8x31																						W10x33																				
	TRANSFER	TRANSFER	TRANSFER	TRANSFER	HSS8x8x1/2	HSS8x8x1/2	W10x77	W10x60	W10x60	W10x45	W10x45			W10x60	W10x60	W10x60	W10x60	W10x60	W10x60	W10x60			W10x66	W10x77	W10x33	TRANSFER	W10x60	HSS8x8x1/2	HSS8x8x1/2	W10x33	W10x33	W12x87		W10x77	W10x60	W10x60	W10x91	W12x72	W12x72	W12x87	W10x49	W10x33	W10x66	W10x77	W10x60
LEVEL 8																																														
BASE PLATE (1/S301)					BP-6	BP-6	BP-7	BP-7	BP-9	BP-5	BP-5	BP-1		BP-4	BP-5	BP-7	BP-7	BP-4	BP-5	BP-4			BP-7	BP-7	BP-2		BP-9	BP-3	BP-3	BP-3	BP-3	BP-5		BP-5	BP-9	BP-7	BP-7	BP-5	BP-5	BP-5	BP-14	BP-1	BP-7	BP-7	BP-11
AXIAL LOAD (KIPS)	35	55	105	105	170	80	155	115	145	130	150	125	25	210	235	125	140	265	275	230	20	30	105	85	175	105	160	65	65	65	65	165	35	225	290	140	150	295	290	280	195	180	125	110	150
SHEAR LOAD (KIPS)					5	5	5	5	5					5	10	5	10	10	10	10			10				5					10		10	5	10	10	5	5	10	10		10		5
MOMENT (KIPS-FT)					20	20	20	5	5					15	45	25	25	30	40	30			25				25					25		30	25	30	30	20	20	45	35		25		15

COLUMN SCHEDULE NOTES:
1) AXIAL LOAD, SHEAR LOAD, AND MOMENT ARE FACTORED VALUES.
2) LATERAL COLUMN SPLICE CONNECTION ARE DESIGNED BY STEEL MANUFACTURER'S ENGINEERS. SHEAR LOAD AND MOMENT ARE GIVEN AT THE SPLICE LOCATION.

5 STEEL COLUMN SCHEDULE
SCALE: 3/4" = 1'-0"

SK#01
03 pages
Date: 01-24-2025

DOB STAMP

1250 Maryland Avenue
1250 MARYLAND AVENUE SW
WASHINGTON, DC 20024

BEYER BLINDER BELLE
3307 M Street Northwest, Suite 301
Washington, DC, 20007
202 333 8000

MECHANICAL & PLUMBING
HURST ENGINEERS
703-534-7872

ELECTRICAL
POWER DESIGN INC.
727-497-9811

STRUCTURAL
RATHGEBER GOSS ASSOCIATES
301-590-0071

CIVIL
GORDON DC
202-869-1600

LANDSCAPE
OVS
202-546-7575

INTERIORS
KTGY SDDG
312-274-0707

LIGHTING
CM KLING + ASSOCIATES
703-684-6270

KEY PLAN

STAMP

DISTRICT OF COLUMBIA
NEDERIAS J. IGLESIAS
PE-S40000152
11/08/2024
STRUCTURAL
PROFESSIONAL ENGINEER

NO	DATE	DESCRIPTION

REVISIONS

SUBMITTAL

PERMIT SUBMISSION

DRAWING TITLE

STEEL COLUMNS SCHEDULE AND TYPICAL DETAILS

SCALE	As indicated
DATE	11/08/2024
PROJECT NUMBER	6415.00
DRAWING NUMBER	S301

of

STEEL COLUMN SCHEDULE

COLUMN MARK / LEVEL	D-4-9.3	D-4-11.4	D-4-13.3	D-4-13.4	D-4-14	E-1.2	E-3	E-3.1	E-4	E-5	E-6	E-7.3	E-8.3	E-9.3	E-10.3	E-10.4	E-11.1	E-12	E-13	E-14	F-1.1	F-3	F-3.1	F-4	F-5	F-6	F-7.3	F-8.3	F-9.3	F-10.3	F-10.4	F-11.1	F-12	F-13	F.3-13	F.1-3	F.1-4	F.1-5	F.1-6	F.1-7.3	F.1-8.3	F.1-9.3	F.1-10.3	F.1-11.1	F.1-11.4	F.1-11.4
PENTHOUSE																																															
LEVEL 11								W10x31															W10x31												W10x33												
LEVEL 10	HSS8x8x1/2	HSS8x8x1/2	W10x33	W10x33	W10x45		W10x45	TRANSFER	W10x45	W10x45	W10x45	W10x45	W10x45	W10x45	W10x45	W10x68	W10x45	W10x45	W10x45	W10x77		W10x60	TRANSFER	W10x68	W10x45	W10x45	W10x68	W10x45	W10x45	W10x68	W10x45	W10x45	W10x60	W10x45													
LEVEL 9																																			W10x33	W10x31	W10x31	W10x31	W10x31	W10x31	W10x31	W10x31	W10x31	W10x31	W10x31	W10x31	W10x31
LEVEL 8	HSS8x8x1/2	HSS8x8x1/2	W10x68	W10x60	W10x33	HSS8x8x1/2	W10x68		W10x68	W10x77	W10x60	W10x60	W10x60	W10x60	W10x60	W10x68	W10x60	W10x79	W10x72	W10x31	W10x45	W10x68		W10x68	W10x68	W10x60	W10x68	W10x60	W10x60	W10x68	W10x60	W10x60	W10x79	W10x72	TRANSFER	TRANSFER	TRANSFER	TRANSFER	TRANSFER	TRANSFER	TRANSFER	TRANSFER	TRANSFER	TRANSFER	TRANSFER	TRANSFER
BASE PLATE (1/S301)	BP-6	BP-6	BP-4	BP-4	BP-2	BP-2	BP-5		BP-5	BP-5	BP-4	BP-5	BP-4	BP-4	BP-5	BP-1	BP-1	BP-5	BP-5	BP-5	BP-5	BP-5		BP-5	BP-5	BP-4	BP-5	BP-4	BP-4	BP-5	BP-1	BP-1	BP-5	BP-5													
AXIAL LOAD (KIPS)	90	90	65	105	110	130	210	40	230	215	240	250	235	240	260	125	140	230	290	265	80	205	31	240	230	240	240	240	230	200	95	115	235	270	135	65	65	65	60	60	60	60	55	30	30	55
SHEAR LOAD (KIPS)	5	5	5	5			15		10	10	5	5	5	10	10	5	10	5	5	10		10		5	10	5	10	5	10	10	5	5	10	10													
MOMENT (KIPS-FT)	20	15	25	15			50		35	30	15	20	15	30	25	25	30	20	20	45		35		5	40	15	20	15	45	35	25	20	30	30													

STEEL COLUMN SCHEDULE

COLUMN MARK / LEVEL	G-1.1	G-3	G-4	G-5	G-6	G-7.3	G-8.3	G-9.3	G-10.3	G-11.3	G-11.4	G-12	G-12.5	G-13	A'-21	A'-22	A'-23	A'-24	A'-25	A'-26	A'-26.4	A'-27	A'-28	A'-29	A'.5-22	A'.5-23	A'.5-24	A'.5-25	A'.5-26	A'.5-26.4	A'.5-27	A'.5-28	B'-21	B'-22	B'-23	B'-24	B'-25	B'-26	B'-26.4	B'-27	B'-28	B'-29	B'.2-22	B'.2-23	B'.2-24	B'.2-25
PENTHOUSE																																															
LEVEL 11																																	W10x31									W10x33	W10x31	W10x31	W10x31	W10x31
LEVEL 10																																	TRANSFER									W10x33				
LEVEL 9													W10x31												W10x31	W10x31	W10x31	W10x31	W10x31	W10x31	W10x31	W10x31											W10x31	W10x31	W10x31	W10x31
LEVEL 8	W12x45	W10x33	W10x68	W10x68	W10x68	W10x33	W10x33	W10x68	W10x68	W10x33	W10x68	W10x68	TRANSFER	W10x68	W10x68	W10x68	W10x68	W10x33	W10x60	W10x68	W10x60	W12x45	W12x45	W12x45	TRANSFER	TRANSFER	TRANSFER	TRANSFER	TRANSFER	TRANSFER	TRANSFER	TRANSFER		W10x33	W10x33	W10x34	W10x33	W10x33	W10x33	W12x79	W12x46	W12x46	TRANSFER	TRANSFER	TRANSFER	TRANSFER
BASE PLATE (1/S301)	BP-4	BP-1	BP-1	BP-5	BP-5	BP-1	BP-1	BP-5	BP-5	BP-2	BP-1	BP-13		BP-13	BP-5	BP-4	BP-4	BP-1	BP-4	BP-4	BP-1	BP-5	BP-5	BP-5										BP-1	BP-1	BP-1	BP-1	BP-1	BP-1	BP-8	BP-5	BP-14				
AXIAL LOAD (KIPS)	60	120	110	110	110	100	95	95	90	45	35	135	50	135	75	100	95	95	95	95	50	240	95	70	65	65	60	60	60	35	40	70	45	145	145	215	205	200	110	105	140	240	125	95	145	135
SHEAR LOAD (KIPS)																																															
MOMENT (KIPS-FT)																																															

STEEL COLUMN SCHEDULE

COLUMN MARK / LEVEL	B'.2-26	B'.2-26.4	B'.2-27	B'.2-28	C-23.2	C-24	C-24.6	C-25.3	C-25.6	C-25.4	C-26.3	C-27.1	C-28	C-29	C'-27.1	C.6-24	C.6-24.6	C.6-27.1	C.7-27.1	C.9-25.3	C.9-25.6	C.9-25.4	C.9-26.3	D'-28	D'-29	D'.1-32.6	D'.3-26.4	D'.3-27.2	D'.4-23.5	D'.4-25.3	D'.4-25.6	D'.5-25.4	D'.5-26.3	E'-24	E'-24.6	E'-25.4	E'-26	E'-26.6	E'-27.3	E'-27.5	E-23	E-26	F'-24	F'-24.6	F'-25.4	F'-26
PENTHOUSE																																															
LEVEL 11	W10x31	W10x31	W10x45	W10x31																																											
LEVEL 10					W10x33	W10x33	W10x45	W10x45	W10x33	HSS8x8x1/2	HSS8x8x1/2	W10x45	W10x45	W10x45	W10x45	W10x33	W10x33	W10x60	W10x60	W10x33	W10x33	HSS8x8x1/2	HSS8x8x1/2	W10x33		W10x51	W10x33	W10x45	W10x45	W10x33	W10x33	HSS8x8x1/2	HSS8x8x1/2	W10x45	W10x33	W10x45	W10x33	W10x45	W10x68	W10x68	W10x45	W10x45	W10x45	W10x45	W10x45	W10x45
LEVEL 9	TRANSFER	TRANSFER	TRANSFER	TRANSFER																						TRANSFER																					
LEVEL 8					W12x106	W10x33	W12x72	W12x72	W10x45	HSS8x8x1/2	HSS8x8x1/2	W10x77	W12x72	W12x72	W10x68	W10x79	W10x33	W10x86	W10x51	W10x33	W10x33	HSS8x8x1/2	HSS8x8x1/2	W10x51	W10x51		W12x79	W12x86	W12x79	W10x33	W10x33	HSS8x8x1/2	HSS8x8x1/2	W10x60	W12x65	W10x65	W10x65	W10x51	W10x68	W10x68	W12x72	W12x72	W10x60	W10x60	W10x60	W10x60
BASE PLATE (1/S301)					BP-14	BP-1	BP-4	BP-1	BP-1	BP-6	BP-3	BP-12	BP-4	BP-4	BP-12	BP-5	BP-1	BP-10	BP-10	BP-2	BP-2	BP-3	BP-3	BP-4	BP-4		BP-7	BP-5	BP-4	BP-2	BP-2	BP-3	BP-3	BP-4	BP-4	BP-4	BP-4	BP-5	BP-12	BP-7	BP-4	BP-4	BP-4	BP-4	BP-4	BP-4
AXIAL LOAD (KIPS)	135	75	75	125	240	145	110	190	70	185	65	95	265	250	110	145	120	110	115	120	75	65	60	280	280	200	95	100	205	95	95	65	60	220	265	215	225	205	95	115	275	285	200	230	245	235
SHEAR LOAD (KIPS)			10		10		5	10	5	5		10	10	10	5	5		5	10								5	10	10					10	5	5	5	10	5	10	10	10	10	5	10	5
MOMENT (KIPS-FT)			45		35		20	35	30	20		25	30	30	20	15		30	30								15	25	30					40	15	25	15	35	15	35	25	25	45	30	35	20

COLUMN SCHEDULE NOTES:
1) AXIAL LOAD, SHEAR LOAD, AND MOMENT ARE FACTORED VALUES.
2) LATERAL COLUMN SPLICE CONNECTION ARE DESIGNED BY STEEL MANUFACTURER'S ENGINEERS. SHEAR LOAD AND MOMENT ARE GIVEN AT THE SPLICE LOCATION.

RED HIGHLIGHTED GRIDS HAVE CONFICT IN PLAN LOCATIONS.

GREEN HIGHLIGHTED GRIDS NOT COVERD IN PLANS.

MAGENTA HIGHLIGHTED GRIDS HAVE CONFICT & NOT COVERD IN PLANS.

Q1
Please review and advise on column schedule conflicts.

1 STEEL COLUMN SCHEDULE
SCALE: 3/4" = 1'-0"

NOTE: IF THIS SHEET IS NOT 36"W x 48", THEN IT IS NOT THE INTENDED SIZE. IN ALL CASES, WORK TO FIGURED DIMENSIONS.

0 0.5' 1' 2'

Autodesk Docs://6415 - 1250 Maryland Avenue/S302-6415-1250 Maryland Ave-R24.rvt
1/15/2025 9:48:21 PM

DOB STAMP

1250 Maryland Avenue
1250 MARYLAND AVENUE SW
WASHINGTON, DC 20024

BEYER BLINDER BELLE
3307 M Street Northwest, Suite 301
Washington, DC, 20007
202 333 8000

MECHANICAL & PLUMBING
HURST ENGINEERS
703-534-7872

ELECTRICAL
POWER DESIGN INC.
727-497-9811

STRUCTURAL
RATHGEBER GOSS ASSOCIATES
301-590-0071

CIVIL
GORDON DC
202-869-1600

LANDSCAPE
OVS
202-546-7575

INTERIORS
KTGY SDDG
312-274-0707

LIGHTING
CM KLING + ASSOCIATES
703-684-6270

KEY PLAN

STAMP

NO	DATE	DESCRIPTION
2	01/15/2025	50% CD ADDENDUM 2

REVISIONS

SUBMITTAL

50% CD ADDENDUM

DRAWING TITLE

STEEL COLUMN SCHEDULE

SCALE	3/4" = 1'-0"
DATE	01/15/25
PROJECT NUMBER	6415.00
DRAWING NUMBER	

S302

of

NOTE: IF THIS SHEET IS NOT 36"W x 48"L THEN IT IS NOT THE INTENDED SIZE. IN ALL CASES, WORK TO FIGURED DIMENSIONS.

0 0.5' 1' 2'

STEEL COLUMN SCHEDULE

COLUMN MARK / LEVEL	F'-26.6	F'-21.3	F'-21.5	F'-28	F'-29	F'.5-13	F'.5-24	F'.5-24.6	F'.5-25.4	F'.5-26	F'.5-26.6	F'.5-27.3	F'.5-27.5	F'.5-28	F'.6-29
PENTHOUSE															
LEVEL 11						W10x33									
LEVEL 10	W10x45	W10x49	W10x60	W10x33	W10x33										
LEVEL 9						W10x33	W8x31	W8x31	W8x31	W8x31	W8x31	W8x31	W8x31	W8x31	W8x31
	W12x31	W10x49	W10x49	W12x31	W12x31	TRANSFER	TRANSFER	TRANSFER	TRANSFER	TRANSFER	TRANSFER	TRANSFER	TRANSFER	TRANSFER	TRANSFER
LEVEL 8															
BASE PLATE (1/S307)	BP-5	BP-5	BP-1	BP-5	BP-5										
AXIAL LOAD (KIPS)	240	240	125	245	110	135	55	55	55	55	55	35	30	65	55
SHEAR LOAD (KIPS)	10	10	10												
MOMENT (KIPS-FT)	40	30	30												

COLUMN MARK / LEVEL	G'-24	G'-24.6	G'-25.4	G'-26	G'-26.6	G'-27.3	G'-27.5	G'-28	G'-29
PENTHOUSE									
LEVEL 11									
LEVEL 10									
LEVEL 9									
	W12x31	W12x31	W12x31	W12x26	W12x26	W10x77	W10x45	W12x31	W12x31
LEVEL 8									
BASE PLATE (1/S307)	BP-5	BP-5	BP-5	BP-5	BP-13	BP-7	BP-7	BP-5	BP-5
AXIAL LOAD (KIPS)	90	45	90	90	90	50	50	100	100
SHEAR LOAD (KIPS)									
MOMENT (KIPS-FT)									

COLUMN MARK / LEVEL	AA-30	AA-31	AA-31.1	AA-33.3	AA-34	AA-35	AA-35.5	AA-37	AA-38	AA4-31.1	AA4-34	AA4-35	AA4-35.5	AA4-36.4	AA4-38
PENTHOUSE															
LEVEL 11										W8x31					
LEVEL 10		W10x60		W10x49											
LEVEL 9										W8x31	W8x31	W8x31	W8x31	W8x31	W8x31
	W10x33	W10x60	W12x72	W12x49	W10x77	W10x77	W10x60	W10x31	W12x72	TRANSFER	TRANSFER	TRANSFER	TRANSFER	TRANSFER	TRANSFER
LEVEL 8															
BASE PLATE (1/S307)	BP-2	BP-1	BP-13	BP-5	BP-5	BP-5	BP-5	BP-1	BP-13						
AXIAL LOAD (KIPS)	45	220	210	220	105	105	100	115	80	205	60	60	65	80	55
SHEAR LOAD (KIPS)															
MOMENT (KIPS-FT)															

COLUMN MARK / LEVEL	BB-31	BB-32	BB-33	BB-33.3	BB-34	BB-35	BB-36
PENTHOUSE							
LEVEL 11	W8x31			W8x31			
LEVEL 10		W10x45	W10x45		W10x45	W10x45	W10x45
LEVEL 9	W8x31			W8x31			
	TRANSFER	W12x49	W12x49	TRANSFER	W10x60	W10x60	W10x60
LEVEL 8							
BASE PLATE (1/S307)		BP-5	BP-5		BP-4	BP-5	BP-5
AXIAL LOAD (KIPS)	120	265	240	115	115	145	110
SHEAR LOAD (KIPS)		5	5		5	10	5
MOMENT (KIPS-FT)		25	30		20	30	20

STEEL COLUMN SCHEDULE

COLUMN MARK / LEVEL	BB-37	BB.5-38	CC-33	CC-33.3	CC-34	CC-35	CC-36	CC-37	CC.5-38	DD-34	DD-35	DD-36	DD.5-38	EE-35	EE-36	EE-38	E-1.1	E.5-6
PENTHOUSE																		
LEVEL 11				W8x31														
LEVEL 10	W10x39	W10x45	W10x33	TRANSFER	W10x45	W10x45	W10x45	W10x39	W10x45	W10x45	W10x45	W10x45	W10x45	W10x45	W10x45	W10x60		
LEVEL 9																		W10x33
	W12x39	W12x49	W10x33		W12x72	W12x87	W12x72	W12x39	W12x87	W10x60	W10x60	W10x60	W12x87	W12x72	W12x72	W12x87	W33x118 / W12	TRANSFER
LEVEL 8																		
BASE PLATE (1/S307)	BP-1	BP-13	BP-1		BP-5	BP-5	BP-4	BP-1	BP-5	BP-4	BP-4	BP-4	BP-5	BP-4	BP-5	BP-5	11A / S308	
AXIAL LOAD (KIPS)	245	160	160	35	170	150	230	235	180	120	170	230	195	120	125	90	130	50
SHEAR LOAD (KIPS)		15			5	10	10		10	10	10	5	10	10	10	10		
MOMENT (KIPS-FT)		40			20	30	20		35	25	35	25	30	30	30	35		

COLUMN SCHEDULE NOTES:
1) AXIAL LOAD, SHEAR LOAD, AND MOMENT ARE FACTORED VALUES.
2) LATERAL COLUMN SPLICE CONNECTION ARE DESIGNED BY STEEL MANUFACTURER'S ENGINEERS. SHEAR LOAD AND MOMENT ARE GIVEN AT THE SPLICE LOCATION.

1 STEEL COLUMN SCHEDULE
SCALE: 3/4" = 1'-0"

RED HIGHLIGHTED GRIDS HAVE CONFICT IN PLAN LOCATIONS.

GREEN HIGHLIGHTED GRIDS NOT COVERD IN PLANS.

MAGENTA HIGHLIGHTED GRIDS HAVE CONFICT & NOT COVERD IN PLANS.

Q1
Please review and advise on column schedule conflicts.

DOB STAMP

1250 Maryland Avenue
1250 MARYLAND AVENUE SW
WASHINGTON, DC 20024

BEYER BLINDER BELLE
3307 M Street Northwest, Suite 301
Washington, DC, 20007
202 333 8000

MECHANICAL & PLUMBING
HURST ENGINEERS
703-534-7872

ELECTRICAL
POWER DESIGN INC.
727-497-9811

STRUCTURAL
RATHGEBER GOSS ASSOCIATES
301-590-0071

CIVIL
GORDON DC
202-869-1600

LANDSCAPE
OVS
202-546-7575

INTERIORS
KTGY SDDG
312-274-0707

LIGHTING
CM KLING + ASSOCIATES
703-684-6270

KEY PLAN



STAMP

NO	DATE	DESCRIPTION
2	01/15/2025	50% CD ADDENDUM 2

REVISIONS

SUBMITTAL

50% CD ADDENDUM

DRAWING TITLE

STEEL COLUMN SCHEDULE

SCALE	3/4" = 1'-0"
DATE	11/08/2024
PROJECT NUMBER	6415.00
DRAWING NUMBER	

S303

of

Autodesk Docs://6415 - 1250 Maryland Avenue/S304R1-1250 Maryland Ave-R24.rvt
1/15/2025 5:48:22 PM
