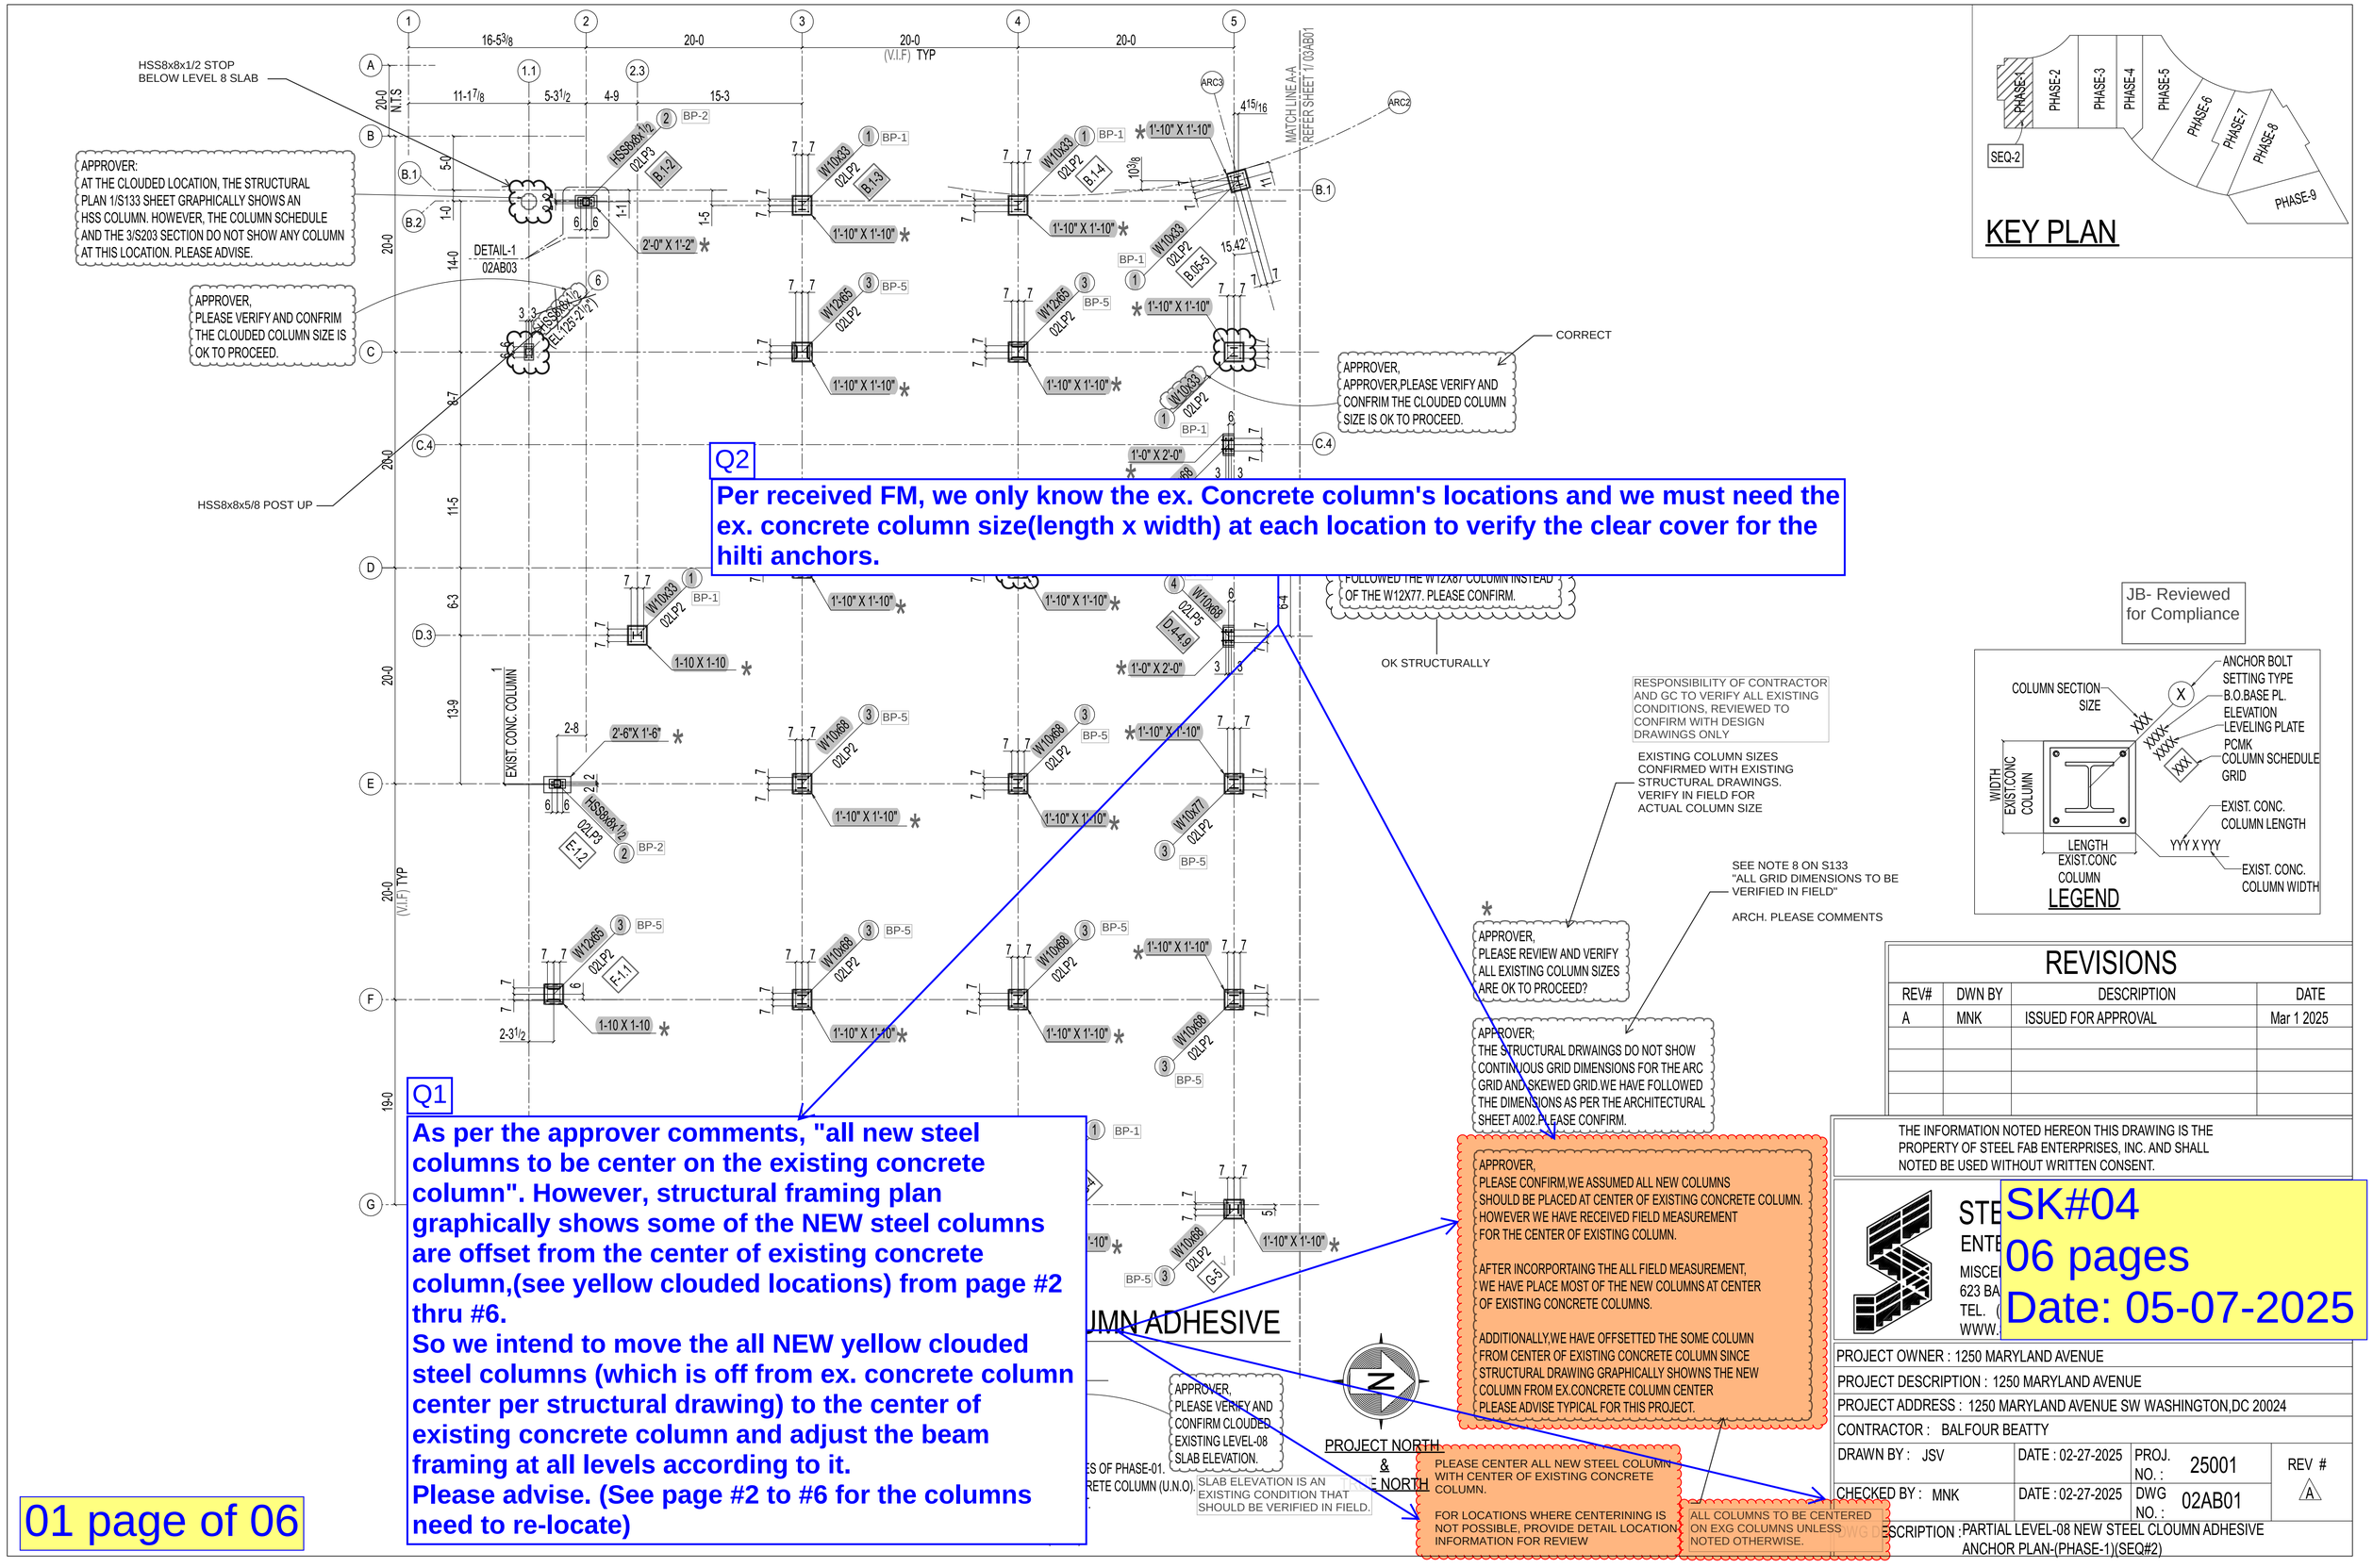

Q2

Per received FM, we only know the ex. Concrete column's locations and we must need the ex. concrete column size(length x width) at each location to verify the clear cover for the hilti anchors.

Q1

As per the approver comments, "all new steel columns to be center on the existing concrete column". However, structural framing plan graphically shows some of the NEW steel columns are offset from the center of existing concrete column,(see yellow clouded locations) from page #2 thru #6.
So we intend to move the all NEW yellow clouded steel columns (which is off from ex. concrete column center per structural drawing) to the center of existing concrete column and adjust the beam framing at all levels according to it.
Please advise. (See page #2 to #6 for the columns need to re-locate)

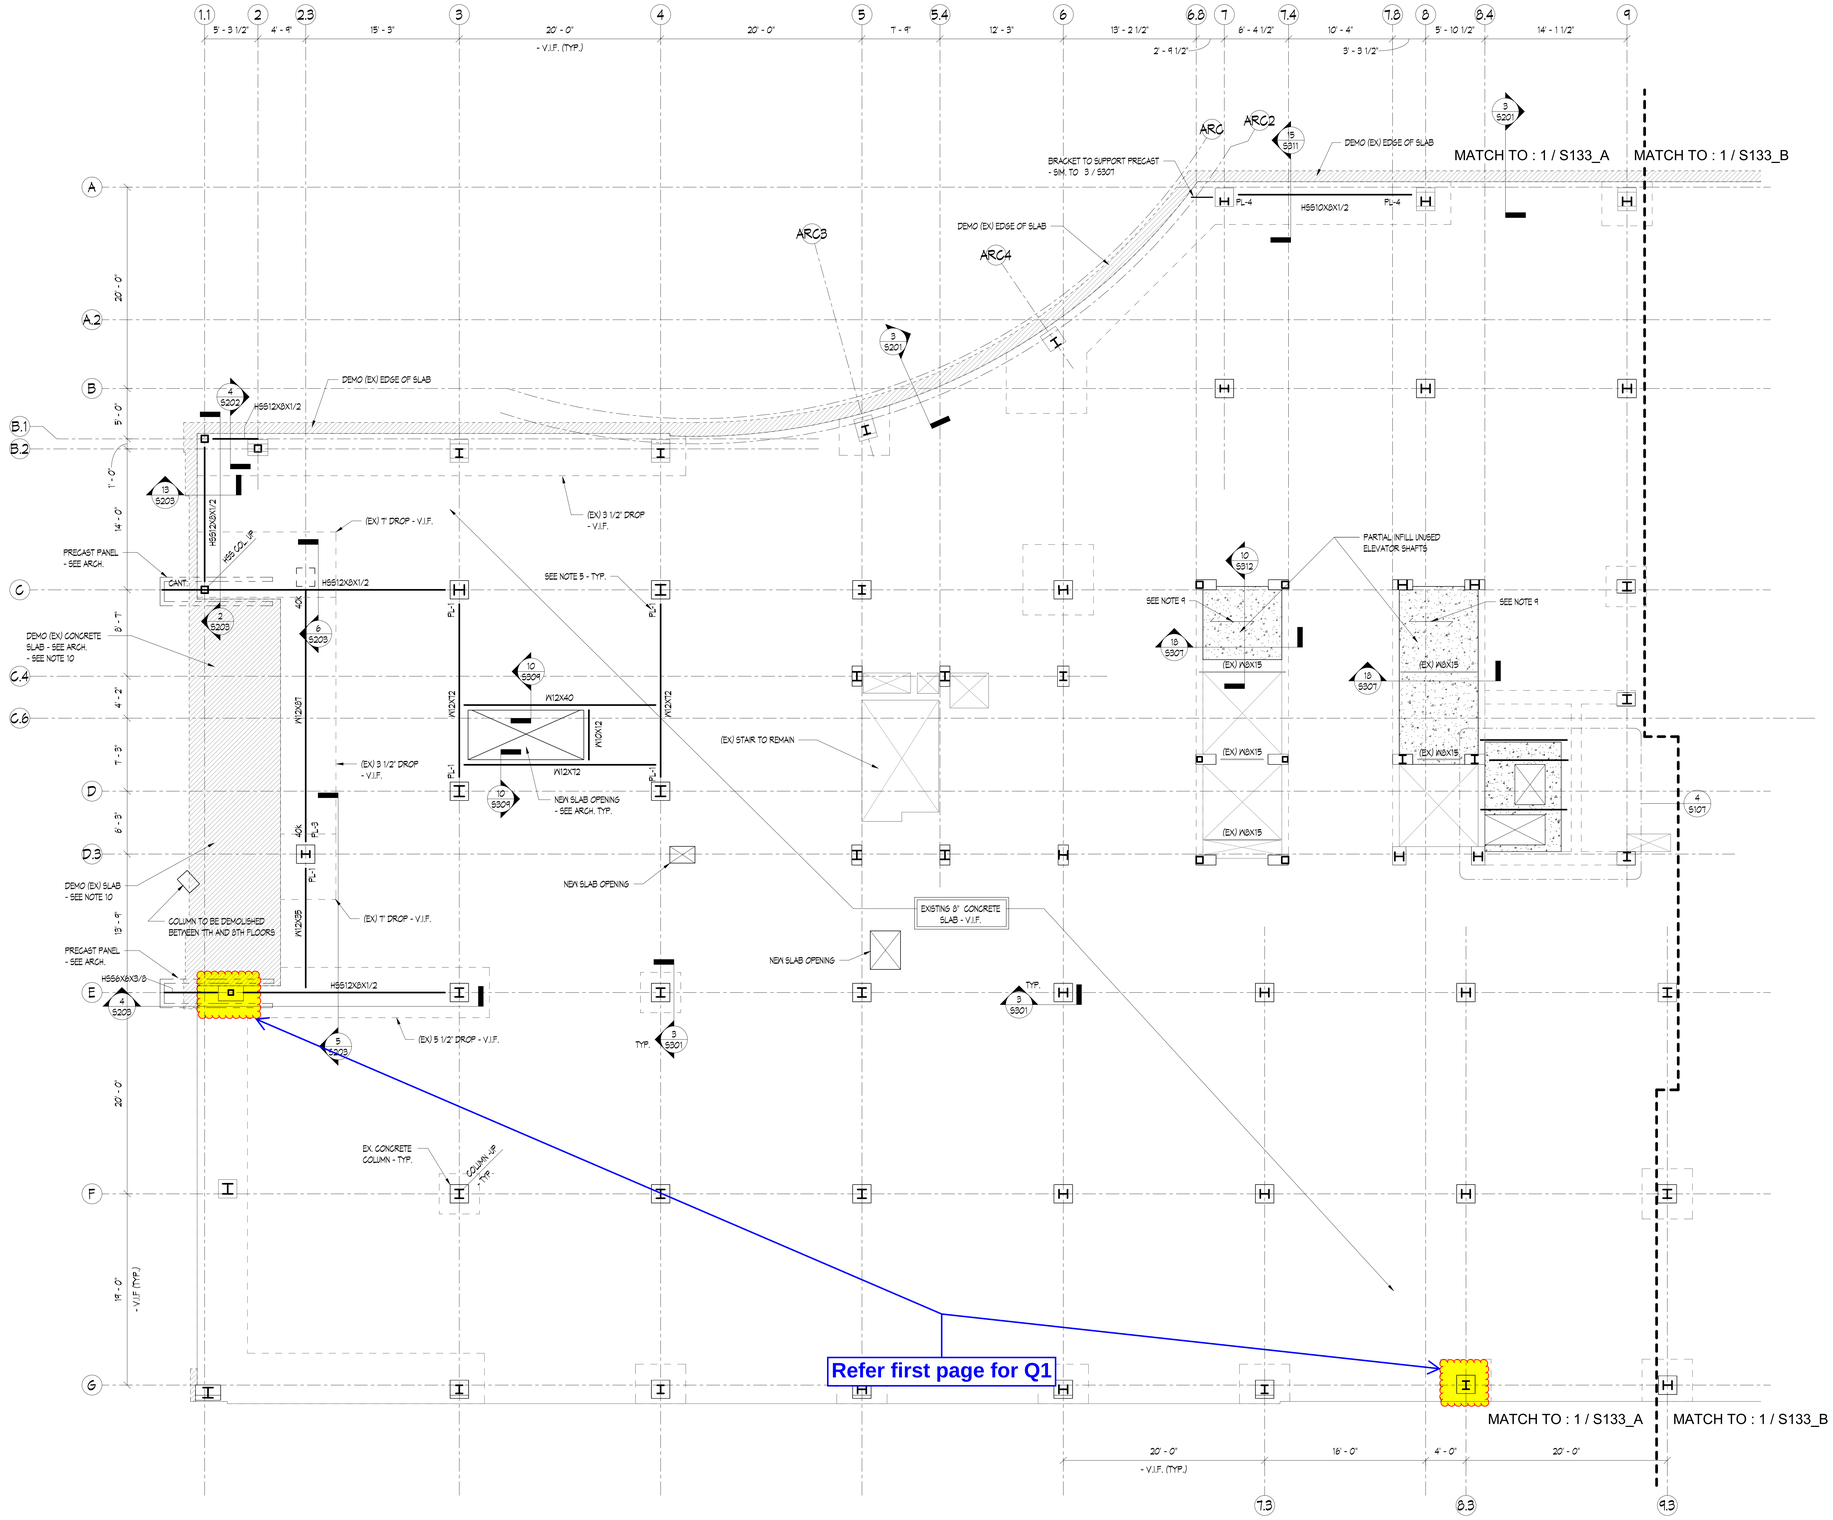

1 PARTIAL LEVEL 08 FRAMING PLAN - ZONE A

SCALE: 3/16" = 1'-0"

PLAN NOTES:

1) TOP OF EXISTING LEVEL 8 SLAB ELEVATION = 125' - 1" (VERIFY IN FIELD).
2) NEW COLUMNS CENTERED OVER EXISTING COLUMNS SHOWN THUS:

EXISTING COLUMN TO 3'-0" ABOVE THE FLOOR SLAB

NEW STEEL COLUMN - SEE SCHEDULE ON S301, S302, AND S303

3) USE GPR/X-RAY OPERATIONS TO LOCATE ALL REBAR IN SLAB PRIOR TO ANY CORE DRILLS. SUBMIT TO STRUCTURAL ENGINEER FOR REVIEW AND APPROVAL.
4) ALL DIMENSIONS FOR NEW OPENINGS IN EXISTING SLAB TO BE VERIFIED WITH ARCHITECTAL DRAWINGS PRIOR TO DEMOLITION OF CONCRETE.
5) SEE SCHEDULE 3 / S309 FOR CONNECTION TO EXISTING STRUCTURAL MEMBERS.
6) SEE S001 FOR GENERAL NOTES.
7) SEE S001, S002, S003, S501, S502, S503, S504, S506, S507, S508, S509, AND S401 FOR TYPICAL DETAILS.
8) ALL GRID DIMENSIONS TO BE VERIFIED IN FIELD.
9) STRUCTURAL SLAB TO BE 5" NORMAL WEIGHT CONCRETE OVER 3" DEEP x 18 GAGE GALVANIZED FORM DECK (TOTAL THICKNESS = 8") REINFORCED WITH 4x4 - W4.0x4.0 WWF.
10) NEW BEAMS MUST BE INSTALLED PRIOR TO SLAB REMOVAL OR TEMPORARY SHORING TO BE PROVIDED AT CONTRACTOR'S OPTION.
11) SEE SHEET S006 FOR REINFORCING AT EXISTING CONCRETE SLAB AND EXISTING CONCRETE COLUMN WHERE OCCURS.

NOTE IF THIS SHEET IS NOT 36"W X 48"D, THEN IT IS NOT THE INTENDED SIZE. IN ALL CASES, WORK TO FIGURED DIMENSIONS.

DOB STAMP

1250 Maryland Avenue
1250 MARYLAND AVENUE SW
WASHINGTON, DC 20024

BEYER BLINDER BELLE
3307 M Street Northwest, Suite 301
Washington, DC, 20007
202 333 8000

MECHANICAL & PLUMBING
HURST ENGINEERS
703-534-7872

ELECTRICAL
POWER DESIGN INC.
727-497-9811

STRUCTURAL
RATHGEBBER GOSS ASSOCIATES
301-590-0071

CIVIL
GORDON DC
202-869-1600

LANDSCAPE
OVS
202-546-7575

INTERIORS
KTGY SDDG
312-274-0707

LIGHTING
CM KLING + ASSOCIATES
703-684-6270

KEY PLAN

STAMP

NO	DATE	DESCRIPTION
4	02/14/2025	50% CD ADDENDUM 4
1	12/13/2024	50% CD ADDENDUM 1

REVISIONS

SUBMITTAL

85% CONSTRUCTION DOCUMENTS

DRAWING TITLE

PARTIAL LEVEL 08
FRAMING PLAN - ZONE A

SCALE	As indicated
DATE	01/24/25
PROJECT NUMBER	6415.00

DRAWING NUMBER

S133_A

of

Autodesk Docs://6415 - 1250 Maryland Avenue/S/S133_A - 1250 Maryland Ave-R24.rvt

3/13/2025 5:12:15 PM

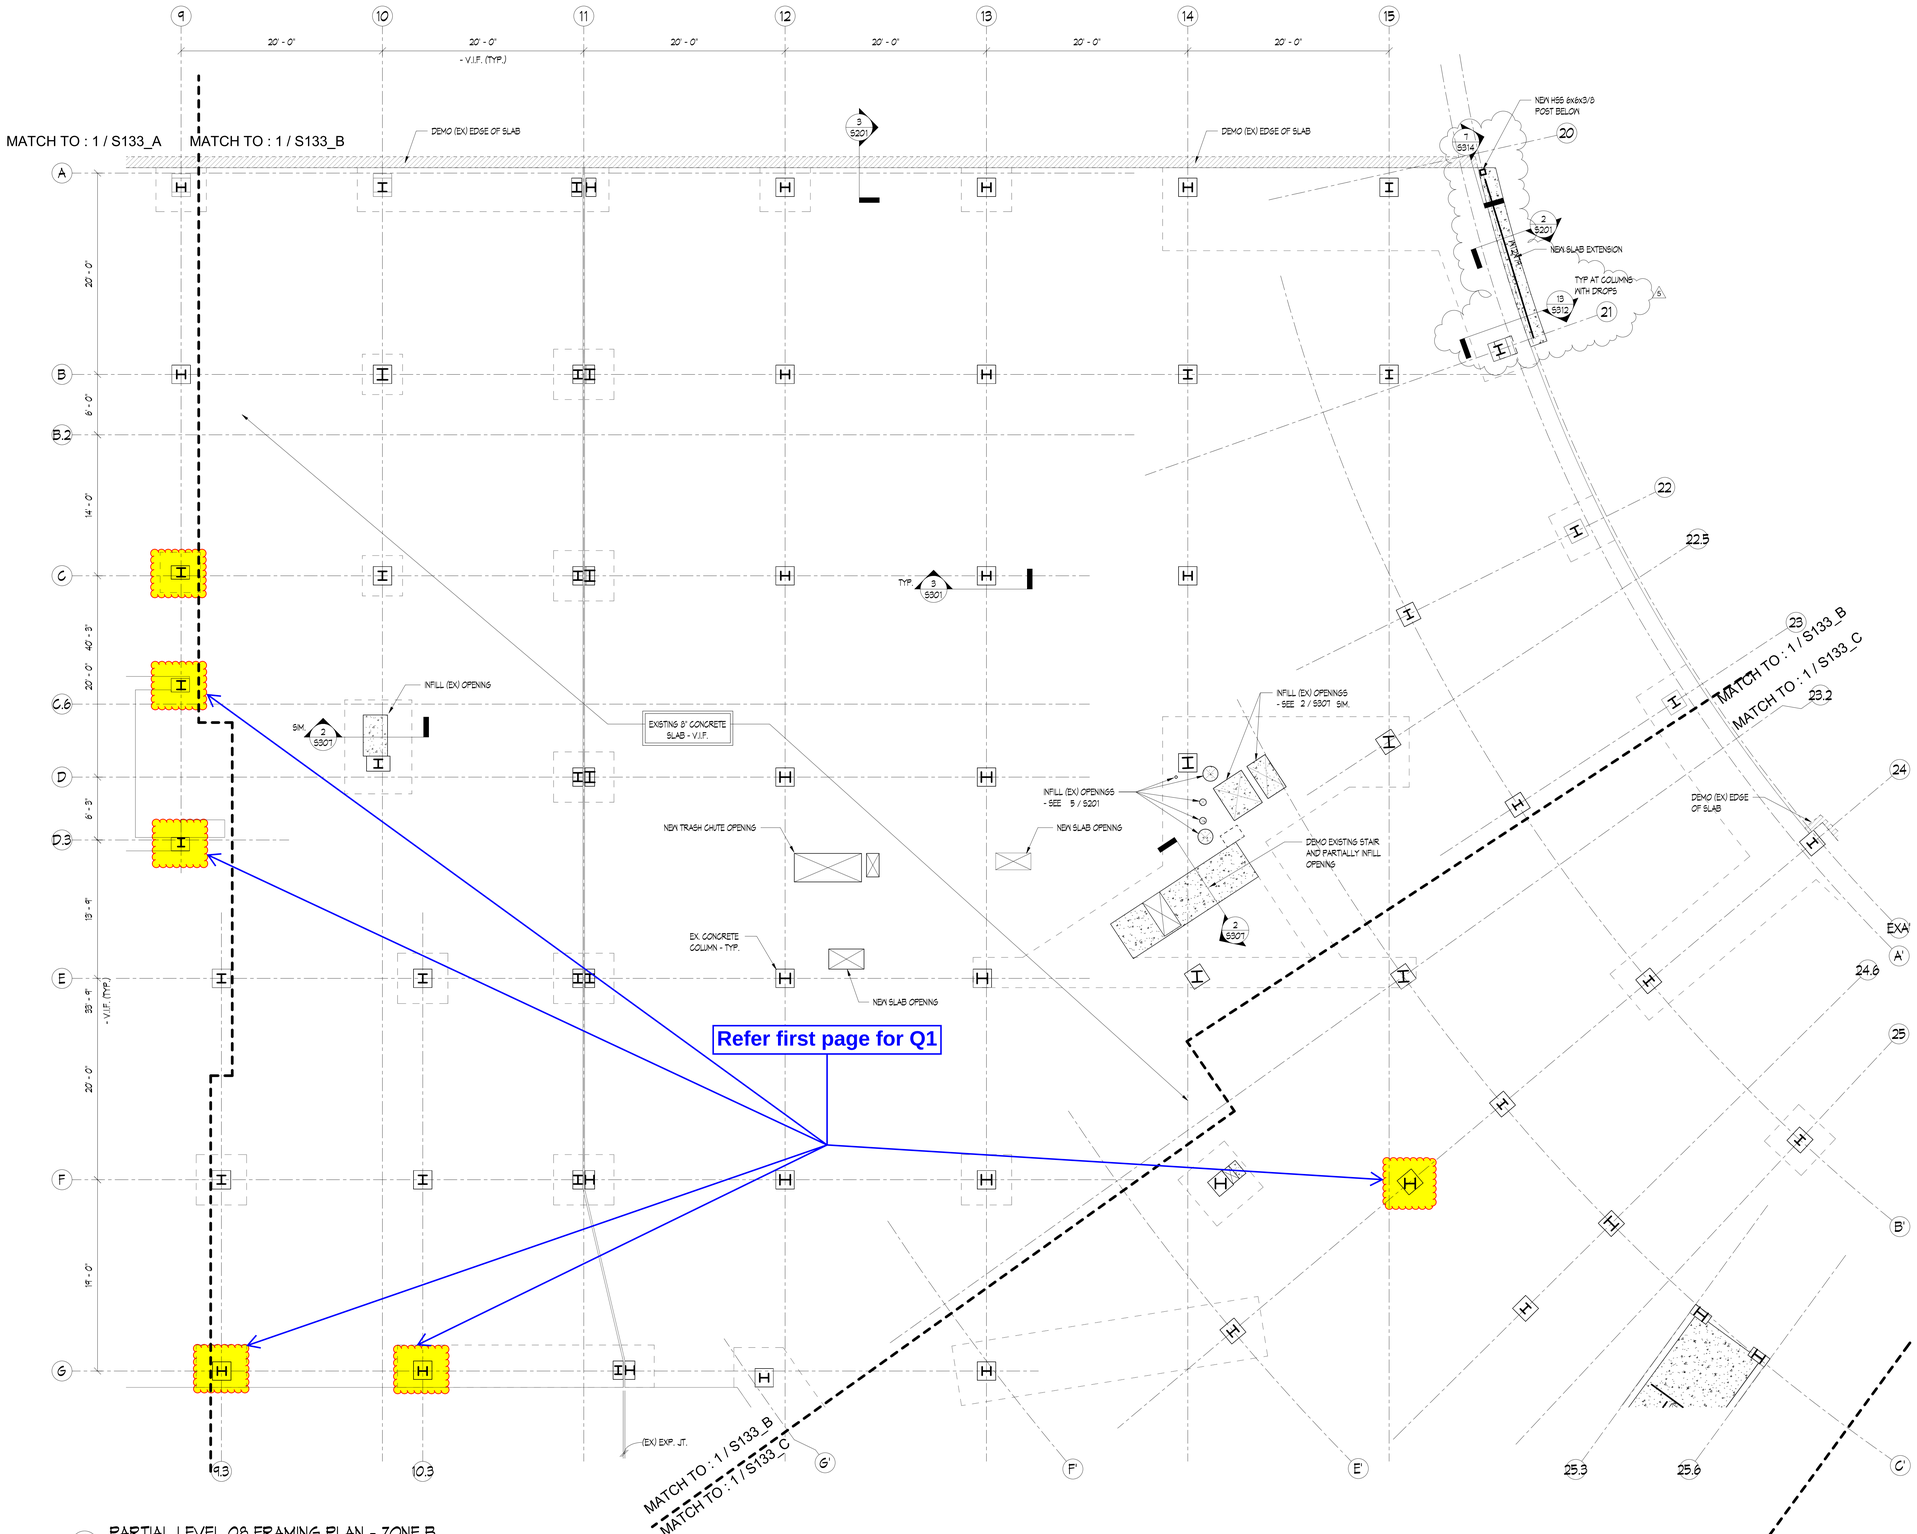

1 PARTIAL LEVEL 08 FRAMING PLAN - ZONE B

SCALE: 3/16" = 1'-0"

PLAN NOTES:

1) TOP OF EXISTING LEVEL 9 SLAB ELEVATION = 125' - 1" (VERIFY IN FIELD).
2) NEW COLUMNS CENTERED OVER EXISTING COLUMNS SHOWN THUS:

EXISTING COLUMN TO 9'-0" ABOVE THE FLOOR SLAB

NEW STEEL COLUMN - SEE SCHEDULE ON S301, S302, AND S303

3) USE GPR/X-RAY OPERATIONS TO LOCATE ALL REBAR IN SLAB PRIOR TO ANY CORE DRILLS. SUBMIT TO STRUCTURAL ENGINEER FOR REVIEW AND APPROVAL.
4) ALL DIMENSIONS FOR NEW OPENINGS IN EXISTING SLAB TO BE VERIFIED WITH ARCHITECTAL DRAWINGS PRIOR TO DEMOLITION OF CONCRETE.
5) SEE SCHEDULE 9 / S304 FOR CONNECTION TO EXISTING STRUCTURAL MEMBERS.
6) SEE S001 FOR GENERAL NOTES.
7) SEE S201, S202, S203, S301, S302, S303, S304, S306, S307, S309, S309, AND S401 FOR TYPICAL DETAILS.
8) ALL GRID DIMENSIONS TO BE VERIFIED IN FIELD.
9) STRUCTURAL SLAB TO BE 5" NORMAL WEIGHT CONCRETE OVER 3" DEEP x 18 GAGE GALVANIZED FORM DECK (TOTAL THICKNESS = 8") REINFORCED WITH 4x4 - W4.0xW4.0 WWF.
10) NEW BEAMS MUST BE INSTALLED PRIOR TO SLAB REMOVAL OR TEMPORARY SHORING TO BE PROVIDED AT CONTRACTOR'S OPTION.
11) SEE SHEET S006 FOR REINFORCING AT EXISTING CONCRETE SLAB AND EXISTING CONCRETE COLUMN WHERE OCCURS.

NOTE IF THIS SHEET IS NOT 36"W x 48"L THEN IT IS NOT THE INTENDED SIZE. IN ALL CASES, WORK TO FIGURED DIMENSIONS.

DOB STAMP

1250 Maryland Avenue
1250 MARYLAND AVENUE SW
WASHINGTON, DC 20024

BEYER BLINDER BELLE
3307 M Street Northwest, Suite 301
Washington, DC, 20007
202 333 8000

MECHANICAL & PLUMBING
HURST ENGINEERS
703-534-7872

ELECTRICAL
POWER DESIGN INC.
727-497-9811

STRUCTURAL
RATHGEBBER GOSS ASSOCIATES
301-590-0071

CIVIL
GORDON DC
202-869-1600

LANDSCAPE
OVS
202-546-7575

INTERIORS
KTGY SDDG
312-274-0707

LIGHTING
CM KLING + ASSOCIATES
703-684-6270

KEY PLAN

STAMP

NO	DATE	DESCRIPTION
5	03/14/2025	85% CD
4	02/14/2025	50% CD ADDENDUM 4
3	01/24/2025	50% CD ADDENDUM 3
1	12/13/2024	50% CD ADDENDUM 1

REVISIONS

SUBMITTAL

85% CONSTRUCTION DOCUMENTS

DRAWING TITLE

PARTIAL LEVEL 08
FRAMING PLAN - ZONE B

SCALE	As indicated
DATE	01/24/25
PROJECT NUMBER	6415.00

DRAWING NUMBER

S133_B

of

Autodesk Docs://6415 - 1250 Maryland Avenue/S/6415-1250-Maryland-Ave-R24.rvt
3/13/2025 5:31:27 PM

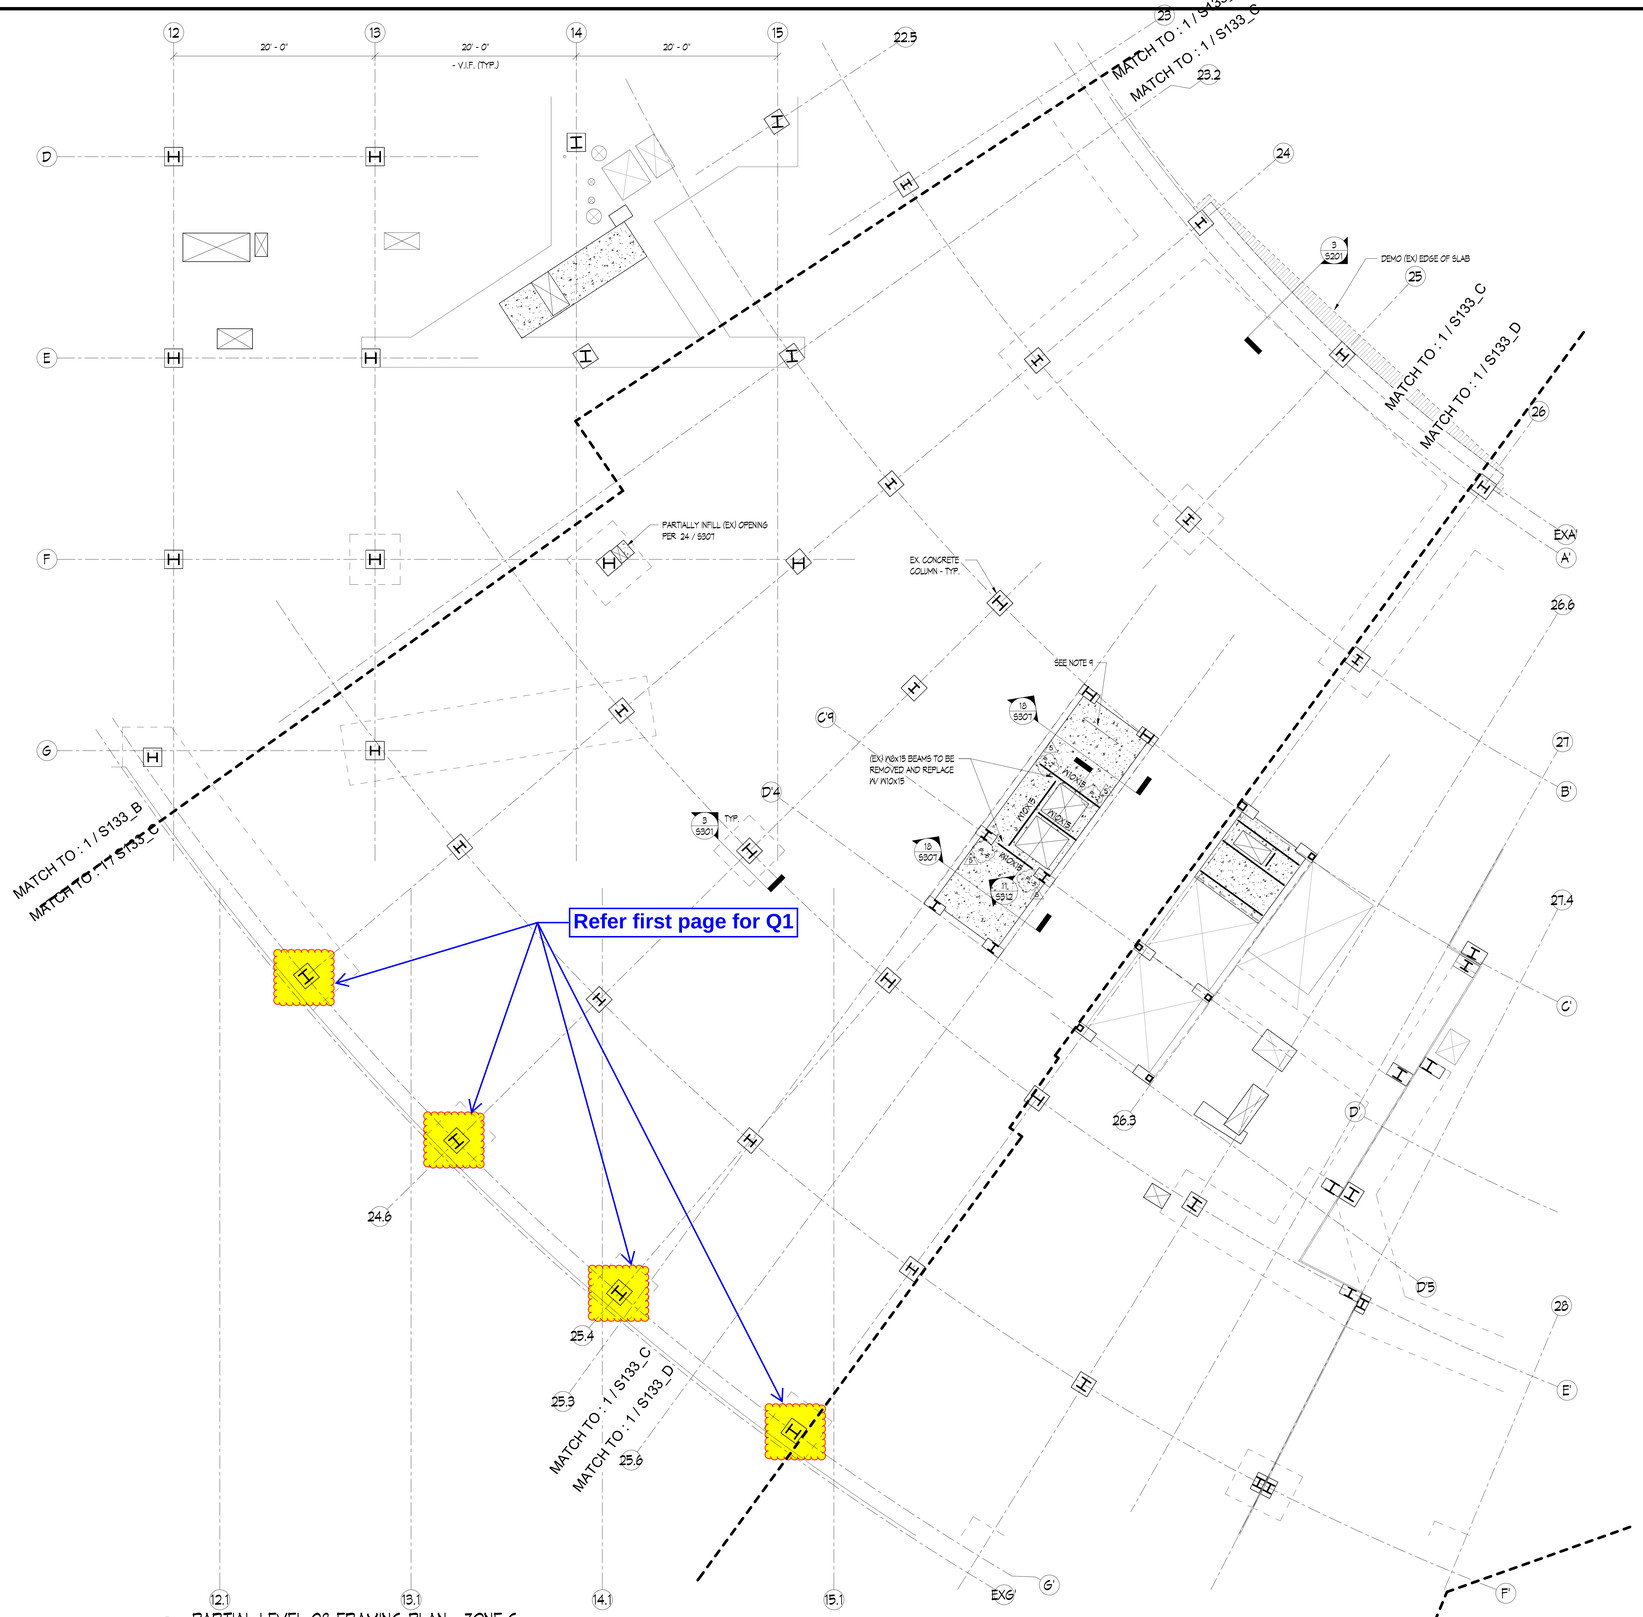

1 PARTIAL LEVEL 08 FRAMING PLAN - ZONE C

SCALE: 3/16" = 1'-0"

PLAN NOTES:

1) TOP OF EXISTING LEVEL 8 SLAB ELEVATION = 125' - 1" (VERIFY IN FIELD).
2) NEW COLUMNS CENTERED OVER EXISTING COLUMNS SHOWN THUS:

EXISTING COLUMN TO 3'-0" ABOVE THE FLOOR SLAB

NEW STEEL COLUMN - SEE SCHEDULE ON S301, S302, AND S303

3) USE GPR/X-RAY OPERATIONS TO LOCATE ALL REBAR IN SLAB PRIOR TO ANY CORE DRILLS. SUBMIT TO STRUCTURAL ENGINEER FOR REVIEW AND APPROVAL.
4) ALL DIMENSIONS FOR NEW OPENINGS IN EXISTING SLAB TO BE VERIFIED WITH ARCHITECTAL DRAWINGS PRIOR TO DEMOLITION OF CONCRETE.
5) SEE SCHEDULE 3 / S304 FOR CONNECTION TO EXISTING STRUCTURAL MEMBERS.
6) SEE S001 FOR GENERAL NOTES.
7) SEE S201, S202, S203, S301, S302, S303, S304, S306, S307, S308, S309, AND S401 FOR TYPICAL DETAILS.
8) ALL GRID DIMENSIONS TO BE VERIFIED IN FIELD.
9) STRUCTURAL SLAB TO BE 5" NORMAL WEIGHT CONCRETE OVER 3" DEEP x 18 GAGE GALVANIZED FORM DECK (TOTAL THICKNESS = 8") REINFORCED WITH 4x4 - W4.0x4.0 WWF.
10) NEW BEAMS MUST BE INSTALLED PRIOR TO SLAB REMOVAL OR TEMPORARY SHORING TO BE PROVIDED AT CONTRACTOR'S OPTION.
11) SEE SHEET S006 FOR REINFORCING AT EXISTING CONCRETE SLAB AND EXISTING CONCRETE COLUMN WHERE OCCURS.

DOB STAMP

1250 Maryland Avenue
1250 MARYLAND AVENUE SW
WASHINGTON, DC 20024

BEYER BLINDER BELLE
3307 M Street Northwest, Suite 301
Washington, DC, 20007
202 333 8000

MECHANICAL & PLUMBING
HURST ENGINEERS
703-534-7872

ELECTRICAL
POWER DESIGN INC.
727-497-9811

STRUCTURAL
RATHGEBBER GOSS ASSOCIATES
301-590-0071

CIVIL
GORDON DC
202-869-1600

LANDSCAPE
OVS
202-546-7575

INTERIORS
KTGY SDDG
312-274-0707

LIGHTING
CM KLING + ASSOCIATES
703-684-6270

KEY PLAN

STAMP

NO	DATE	DESCRIPTION
5	03/14/2025	85% CD
4	02/14/2025	50% CD ADDENDUM 4
1	12/13/2024	50% CD ADDENDUM 1

REVISIONS

SUBMITTAL

85% CONSTRUCTION DOCUMENTS

DRAWING TITLE

PARTIAL LEVEL 08
FRAMING PLAN - ZONE C

SCALE	As indicated
DATE	01/24/25
PROJECT NUMBER	6415.00

DRAWING NUMBER

S133_C

of

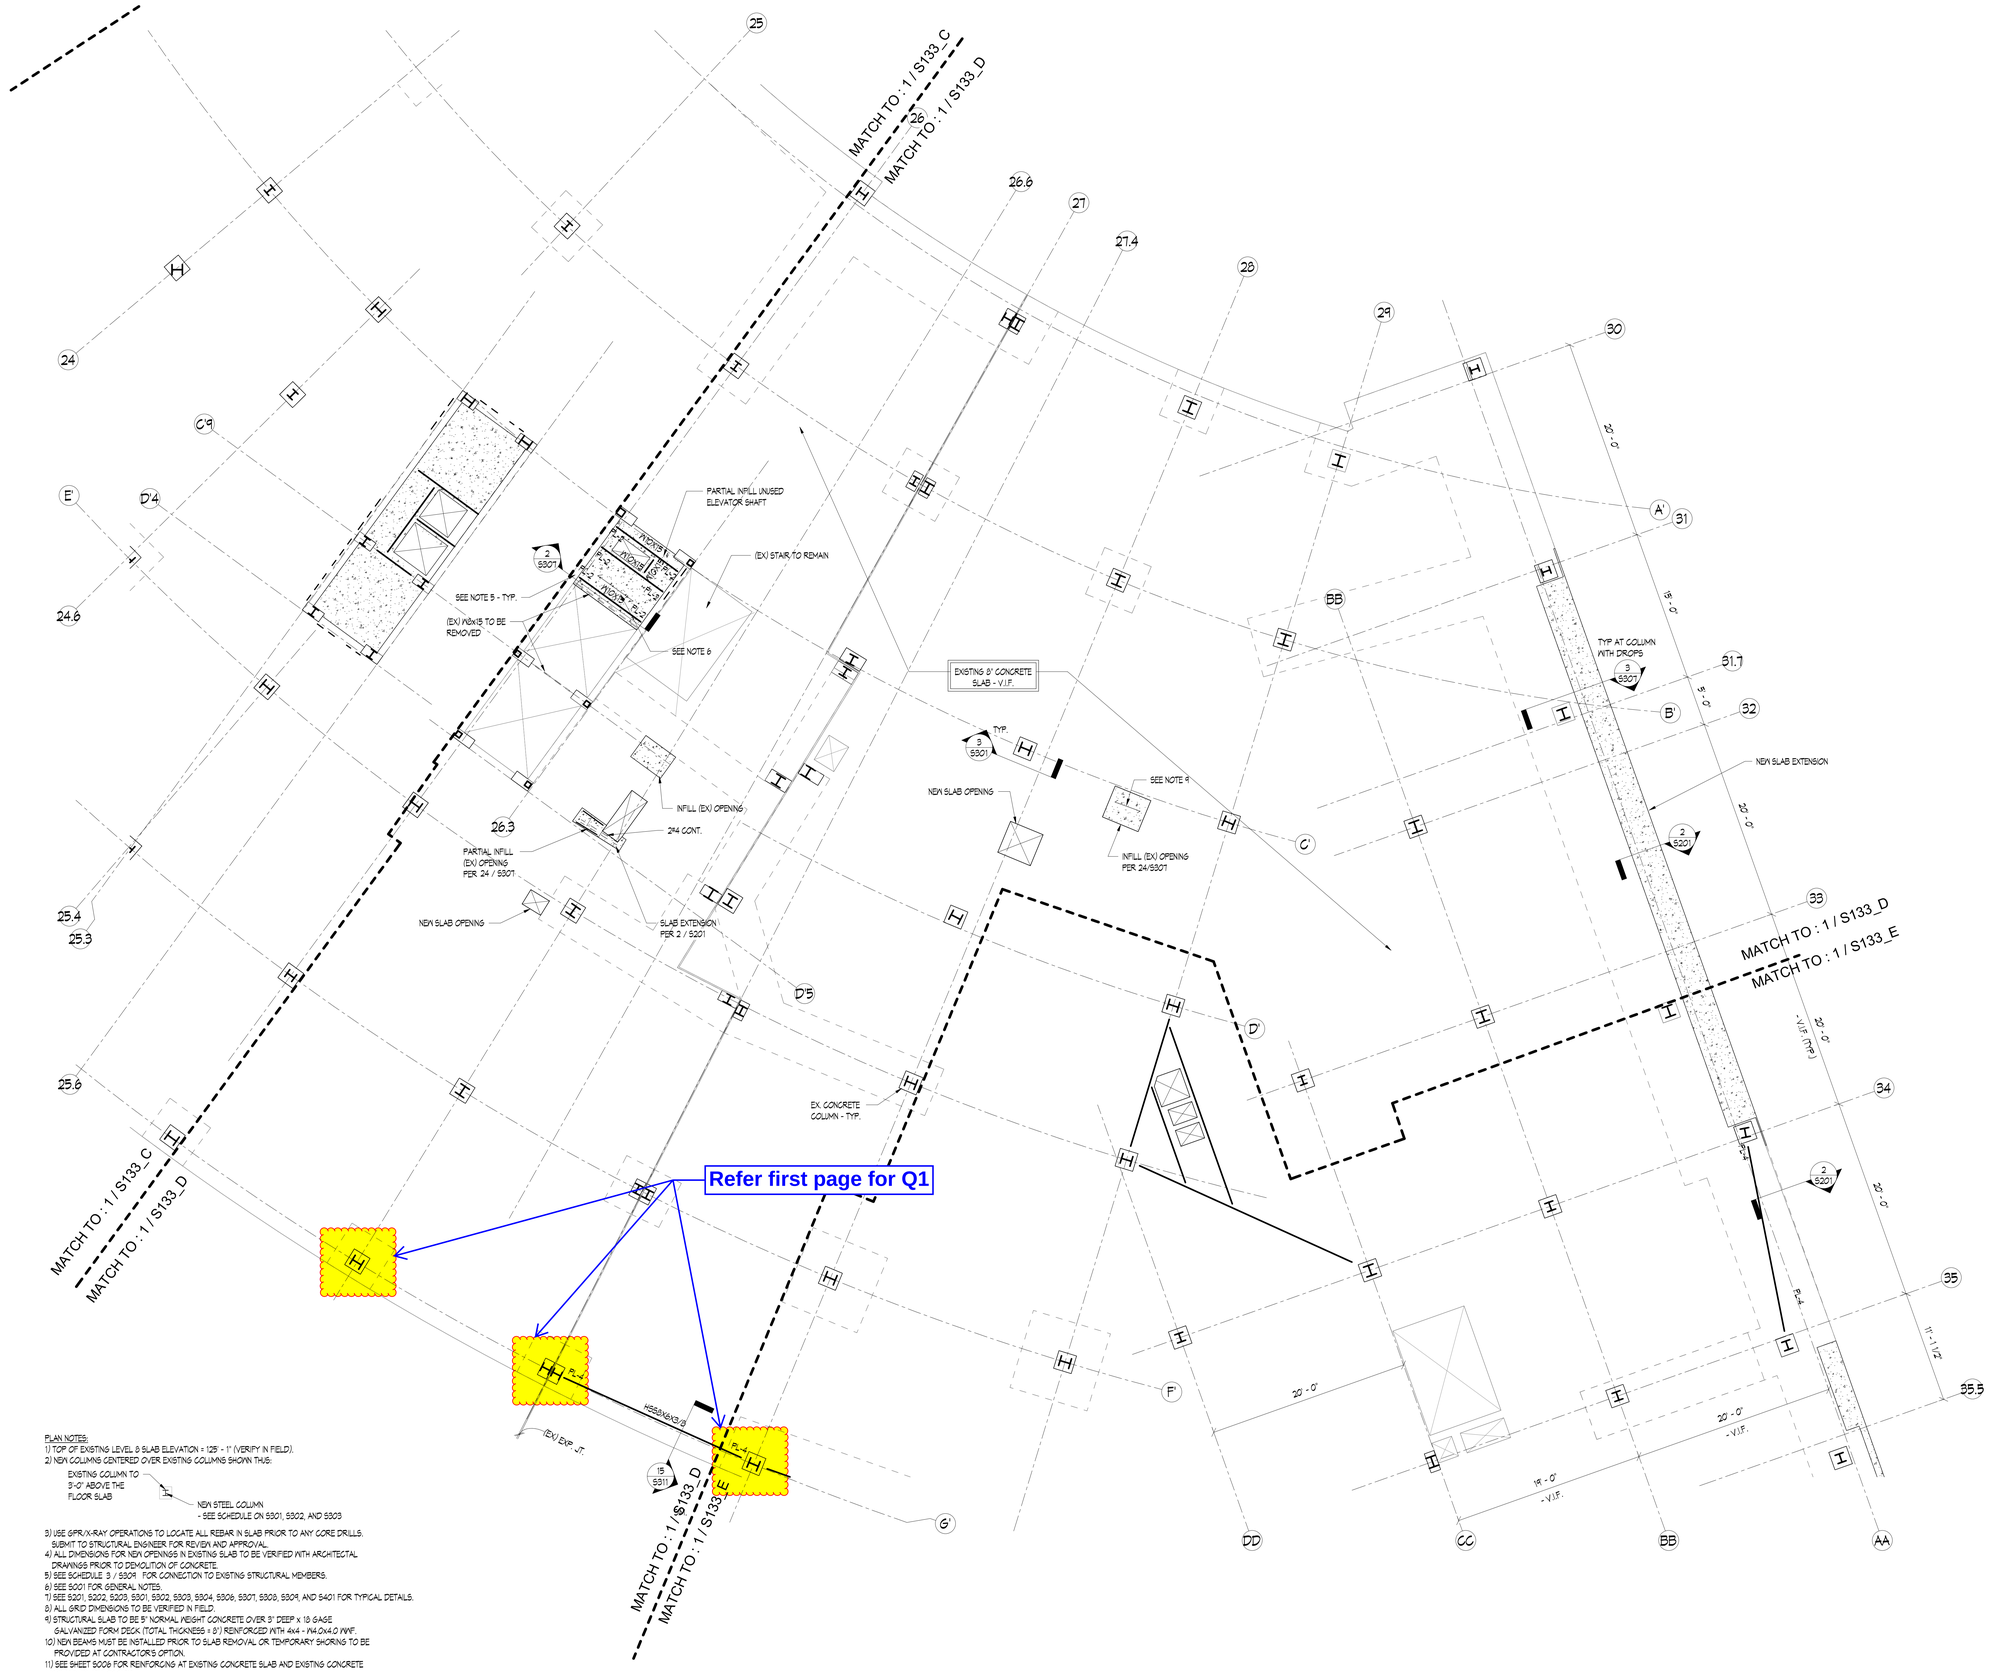

PLAN NOTES:
1) TOP OF EXISTING LEVEL 8 SLAB ELEVATION = 125' - 1" (VERIFY IN FIELD).
2) NEW COLUMNS CENTERED OVER EXISTING COLUMNS SHOWN THUS:
EXISTING COLUMN TO 9'-0" ABOVE THE FLOOR SLAB
NEW STEEL COLUMN - SEE SCHEDULE ON S301, S302, AND S303
3) USE GPR/X-RAY OPERATIONS TO LOCATE ALL REBAR IN SLAB PRIOR TO ANY CORE DRILLS. SUBMIT TO STRUCTURAL ENGINEER FOR REVIEW AND APPROVAL.
4) ALL DIMENSIONS FOR NEW OPENINGS IN EXISTING SLAB TO BE VERIFIED WITH ARCHITECTAL DRAWINGS PRIOR TO DEMOLITION OF CONCRETE.
5) SEE SCHEDULE 3 / S304 FOR CONNECTION TO EXISTING STRUCTURAL MEMBERS.
6) SEE S001 FOR GENERAL NOTES.
7) SEE S201, S202, S203, S301, S302, S303, S304, S306, S307, S308, S309, AND S401 FOR TYPICAL DETAILS.
8) ALL GRID DIMENSIONS TO BE VERIFIED IN FIELD.
9) STRUCTURAL SLAB TO BE 9" NORMAL WEIGHT CONCRETE OVER 3" DEEP X 18 GAGE GALVANIZED FORM DECK (TOTAL THICKNESS = 8") REINFORCED WITH 4x4 - W4.0xW4.0 WWF.
10) NEW BEAMS MUST BE INSTALLED PRIOR TO SLAB REMOVAL OR TEMPORARY SHORING TO BE PROVIDED AT CONTRACTOR'S OPTION.
11) SEE SHEET S006 FOR REINFORCING AT EXISTING CONCRETE SLAB AND EXISTING CONCRETE COLUMN WHERE OCCURS.

1 PARTIAL LEVEL 08 FRAMING PLAN - ZONE D
SCALE: 3/16" = 1'-0"

DOB STAMP

1250 Maryland Avenue
1250 MARYLAND AVENUE SW
WASHINGTON, DC 20024

BEYER BLINDER BELLE
3307 M Street Northwest, Suite 301
Washington, DC, 20007
202 333 8000

MECHANICAL & PLUMBING
HURST ENGINEERS
703-534-7872

ELECTRICAL
POWER DESIGN INC.
727-497-9811

STRUCTURAL
RATHGEBBER GOSS ASSOCIATES
301-590-0071

CIVIL
GORDON DC
202-869-1600

LANDSCAPE
OVS
202-546-7575

INTERIORS
KTGY SDDG
312-274-0707

LIGHTING
CM KLING + ASSOCIATES
703-684-6270

KEY PLAN

STAMP

NO	DATE	DESCRIPTION
4	03/14/2025	50% CD ADDENDUM 4
3	01/24/2025	50% CD ADDENDUM 3
1	12/13/2024	50% CD ADDENDUM 1

REVISIONS

SUBMITTAL
85% CONSTRUCTION DOCUMENTS

DRAWING TITLE
PARTIAL LEVEL 08 FRAMING PLAN - ZONE D

SCALE	As indicated
DATE	01/24/25
PROJECT NUMBER	6415.00

DRAWING NUMBER
S133_D
of

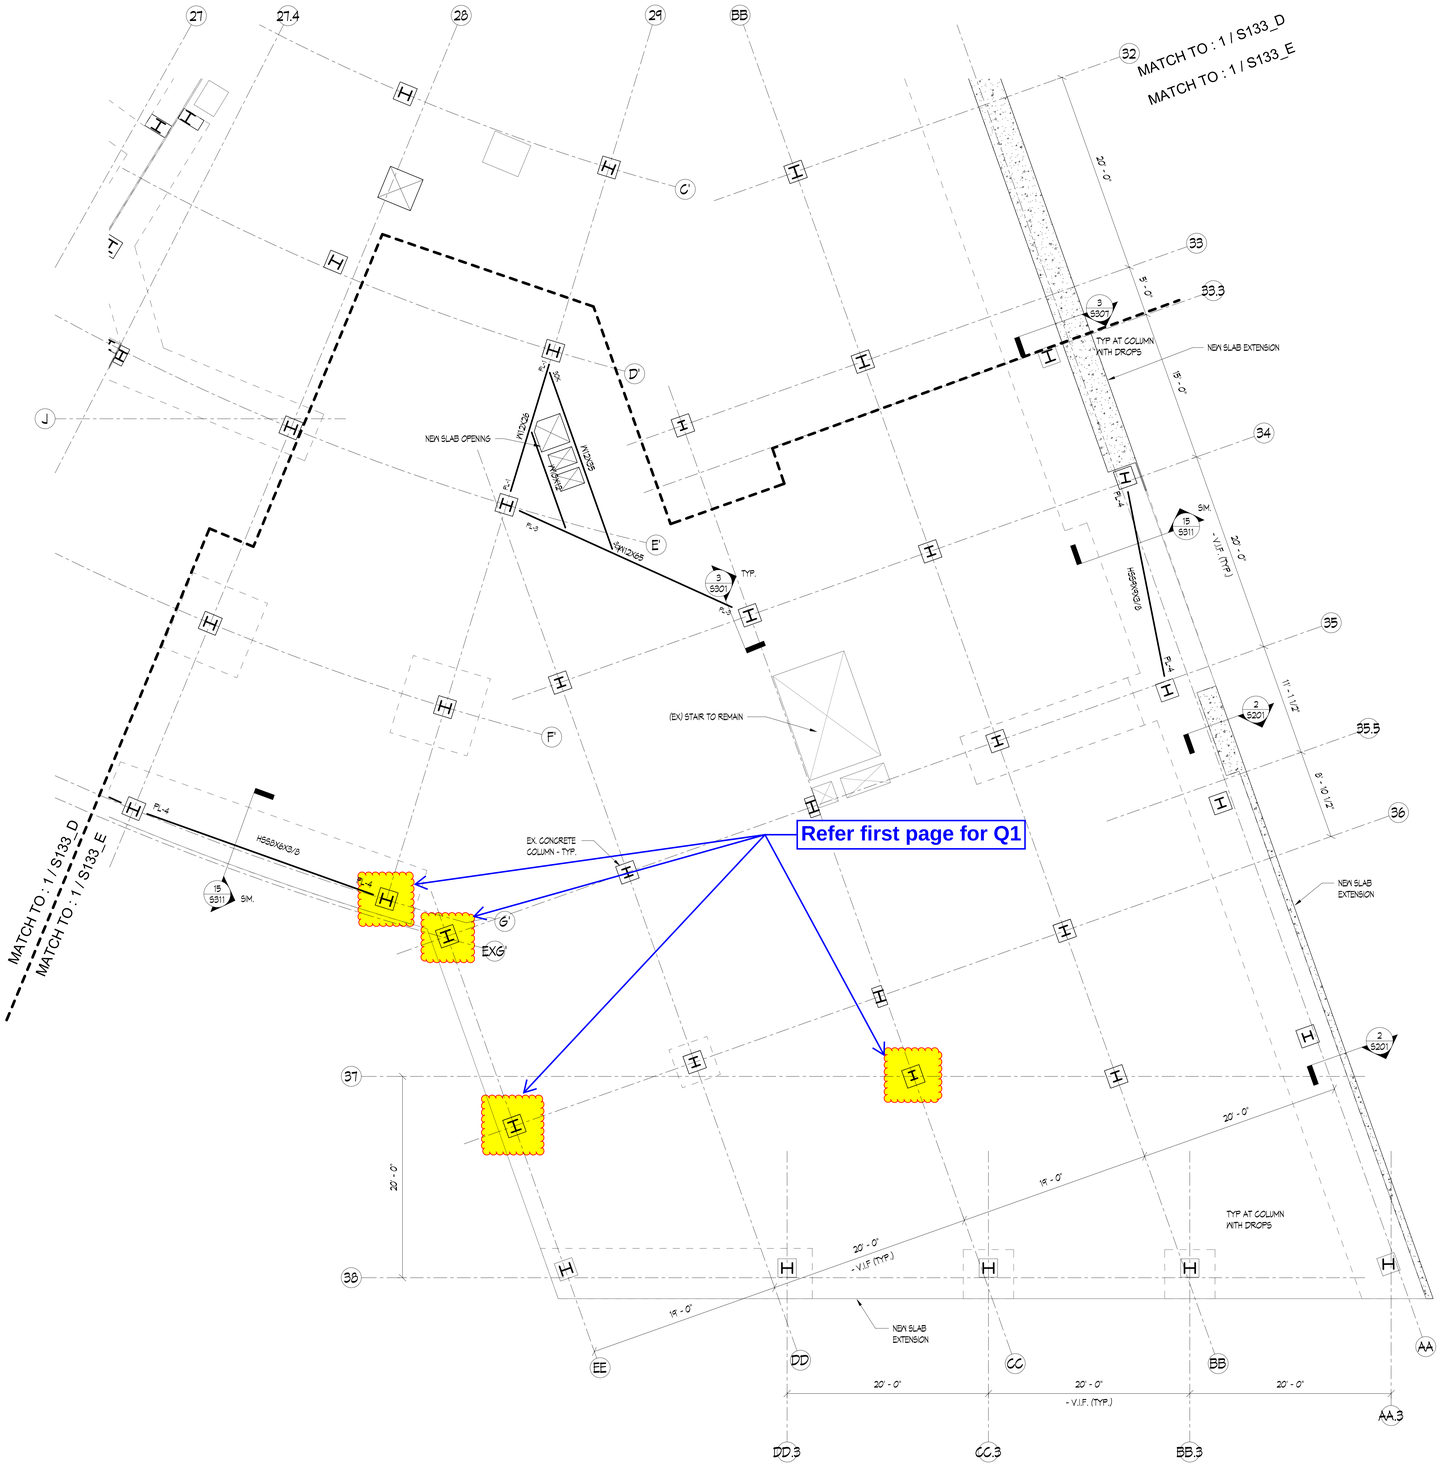

1 PARTIAL LEVEL 08 FRAMING PLAN - ZONE E

SCALE: 3/16" = 1'-0"

PLAN NOTES:
1) TOP OF EXISTING LEVEL 8 SLAB ELEVATION = 125' - 1' (VERIFY IN FIELD).
2) NEW COLUMNS CENTERED OVER EXISTING COLUMNS SHOWN THIS.
EXISTING COLUMN TO 3'-0" ABOVE THE FLOOR SLAB
NEW STEEL COLUMN - SEE SCHEDULE ON 5301, 5302, AND 5303
3) USE GPR/X-RAY OPERATIONS TO LOCATE ALL REBAR IN SLAB PRIOR TO ANY CORE DRILLS. SUBMIT TO STRUCTURAL ENGINEER FOR REVIEW AND APPROVAL.
4) ALL DIMENSIONS FOR NEW OPENINGS IN EXISTING SLAB TO BE VERIFIED WITH ARCHITECTAL DRAWINGS PRIOR TO DEMOLITION OF CONCRETE.
5) SEE SCHEDULE 3 / 5309 FOR CONNECTION TO EXISTING STRUCTURAL MEMBERS.
6) SEE 5001 FOR GENERAL NOTES.
7) SEE 5201, 5202, 5203, 5301, 5302, 5303, 5304, 5306, 5307, 5308, 5309, AND 5401 FOR TYPICAL DETAILS.
8) ALL GRID DIMENSIONS TO BE VERIFIED IN FIELD.
9) STRUCTURAL SLAB TO BE 5" NORMAL WEIGHT CONCRETE OVER 3" DEEP X 18 GASE GALVANIZED FORM DECK (TOTAL THICKNESS = 8") REINFORCED WITH 4x4 - W4.0xW4.0 WWF.
10) NEW BEAMS MUST BE INSTALLED PRIOR TO SLAB REMOVAL OR TEMPORARY SHORING TO BE
T EXISTING CONCRETE SLAB AND EXISTING CONCRETE

NOTE IF THIS SHEET IS NOT 36"W X 48"D, THEN IT IS NOT THE INTENDED SIZE. IN ALL CASES, WORK TO FIGURED DIMENSIONS.

DOB STAMP

1250 Maryland Avenue
1250 MARYLAND AVENUE SW
WASHINGTON, DC 20024

BEYER BLINDER BELLE
3307 M Street Northwest, Suite 301
Washington, DC, 20007
202 333 8000

MECHANICAL & PLUMBING
HURST ENGINEERS
703-534-7872

ELECTRICAL
POWER DESIGN INC.
727-497-9811

STRUCTURAL
RATHGEBBER GOSS ASSOCIATES
301-590-0071

CIVIL
GORDON DC
202-869-1600

LANDSCAPE
OVS
202-546-7575

INTERIORS
KTGY SDDG
312-274-0707

LIGHTING
CM KLING + ASSOCIATES
703-684-6270

KEY PLAN

STAMP

NO	DATE	DESCRIPTION
4	02/14/2025	50% CD ADDENDUM 4
3	01/24/2025	50% CD ADDENDUM 3

REVISIONS

SUBMITTAL

85% CONSTRUCTION DOCUMENTS

DRAWING TITLE

PARTIAL LEVEL 08
FRAMING PLAN - ZONE E

SCALE	As indicated
DATE	01/24/25
PROJECT NUMBER	6415.00

DRAWING NUMBER

S133_E

of

Autodesk Docs://6415 - 1250 Maryland Avenue/S2-6415-1250 Maryland Ave-R24.rvt
3/13/2025 5:13:35 PM
