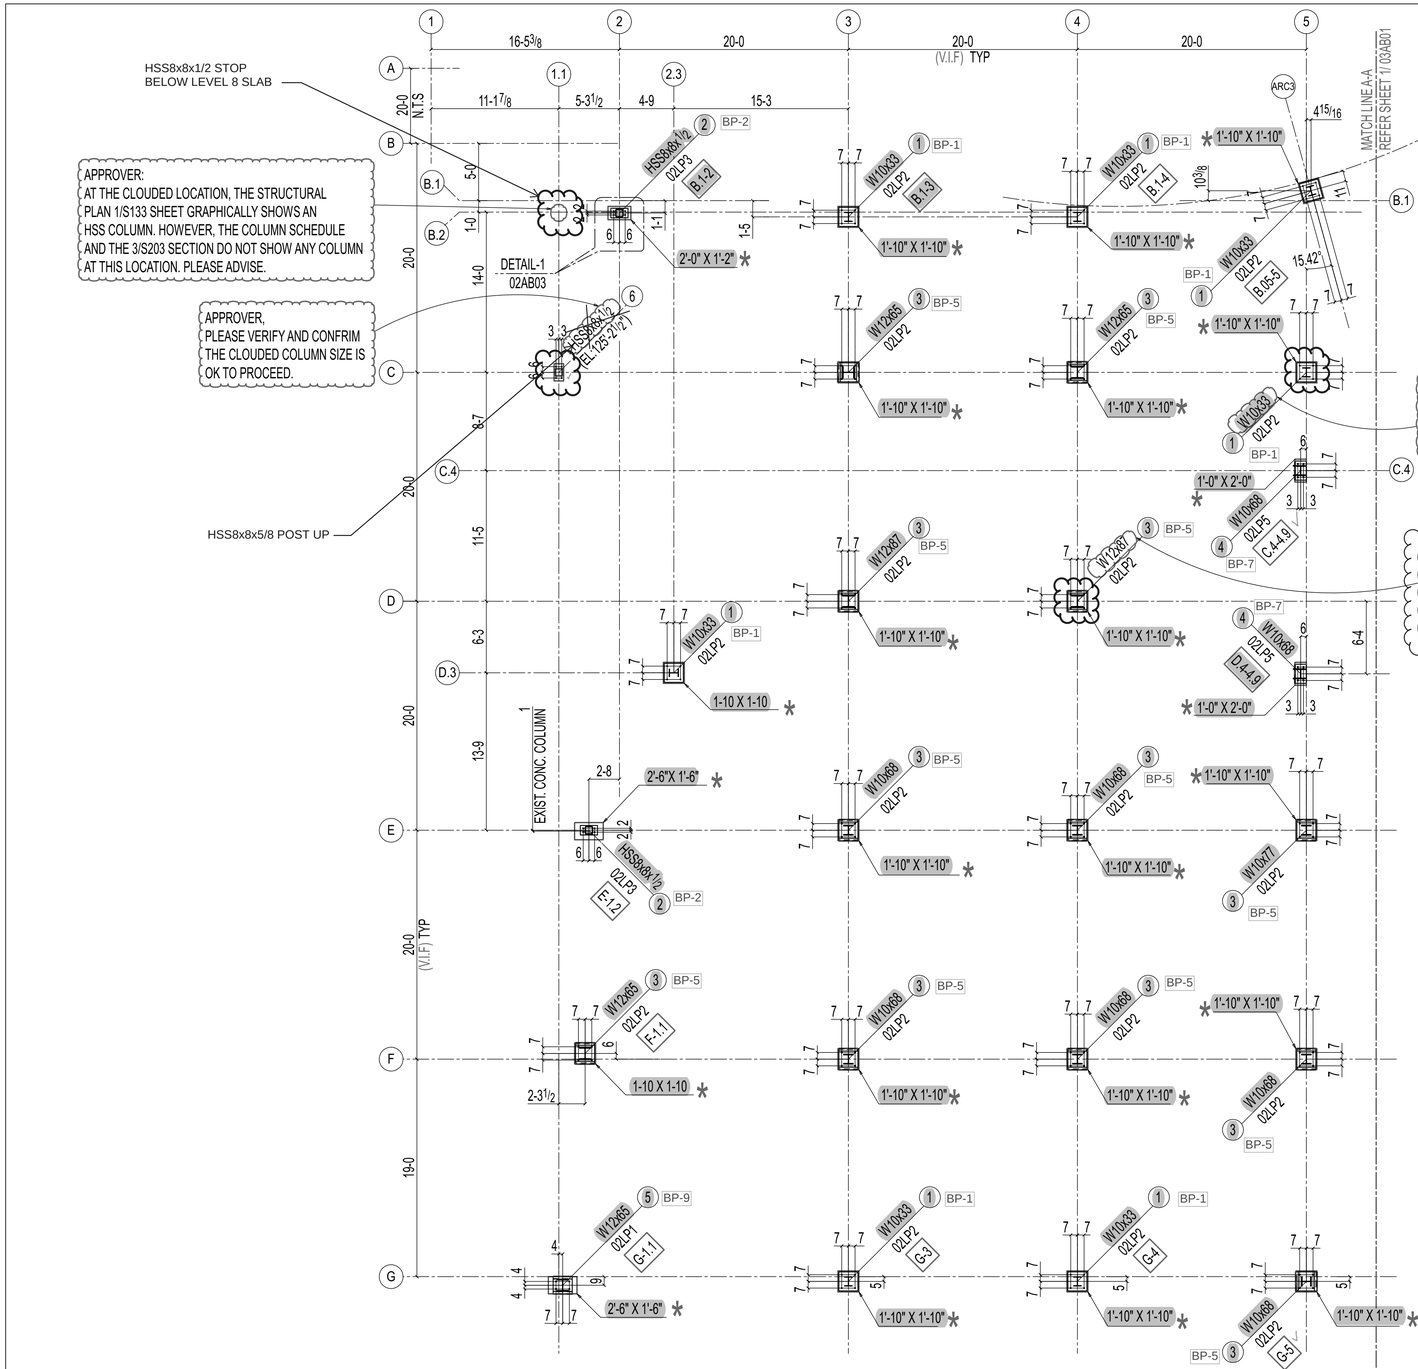

1 / 02AB01

PARTIAL LEVEL-08 NEW STEEL COLUMN ADHESIVE ANCHOR PLAN-(PHASE-1) (SEQ#-1)

(REF: 1/S133_A)

NOTES:
1. TOP OF EXSITING SLAB ELEVATION AT LEVEL-08: 125'-1" (V.I.F).
2. ALL COLUMN BOTTOM OF BASE PL. ELEVATION [128'-2 1/4"] (U.N.O).
3. ALL GRID DIMENSIONS TO BE VERIFY IN FIELD (U.N.O).
4. REFER SHEET 02AB02 & 02AB03 FOR ADHESIVE ANCHOR SETTING TYPES OF PHASE-01.
5. ALL NEW STEEL COLUMN LOCATIONS ARE CENTER OF EXISTING CONCRETE COLUMN (U.N.O).
6. ALL DIMENSIONS ARE LOCATE FROM GRID TO CENTER OF NEW & EXIST. CONCRETE COLUMN CENTER (U.N.O).
7. ALL ELEVATION SHOWN IN PLAN FOR BOTTOM OF BASE PLATE (U.N.O).

APPROVER, PLEASE VERIFY AND CONFIRM CLOUDED EXISTING LEVEL-08 SLAB ELEVATION.

SLAB ELEVATION IS AN EXISTING CONDITION THAT SHOULD BE VERIFIED IN FIELD.

PROJECT NORTH & TRUE NORTH

PLEASE CENTER ALL NEW STEEL COLUMN WITH CENTER OF EXISTING CONCRETE COLUMN.

FOR LOCATIONS WHERE CENTERINING IS NOT POSSIBLE, PROVIDE DETAIL LOCATION INFORMATION FOR REVIEW

ALL COLUMNS TO BE CENTERED ON EXG COLUMNS UNLESS NOTED OTHERWISE.

RESPONSIBILITY OF CONTRACTOR AND GC TO VERIFY ALL EXISTING CONDITIONS, REVIEWED TO CONFIRM WITH DESIGN DRAWINGS ONLY

EXISTING COLUMN SIZES CONFIRMED WITH EXISTING STRUCTURAL DRAWINGS. VERIFY IN FIELD FOR ACTUAL COLUMN SIZE

APPROVER, PLEASE REVIEW AND VERIFY ALL EXISTING COLUMN SIZES ARE OK TO PROCEED?

SEE NOTE 8 ON S133 "ALL GRID DIMENSIONS TO BE VERIFIED IN FIELD"

ARCH. PLEASE COMMENTS

APPROVER; THE STRUCTURAL DRWAINGS DO NOT SHOW CONTINUOUS GRID DIMENSIONS FOR THE ARC GRID AND SKEWED GRID.WE HAVE FOLLOWED THE DIMENSIONS AS PER THE ARCHITECTURAL SHEET A002.PLEASE CONFIRM.

APPROVER, PLEASE CONFIRM,WE ASSUMED ALL NEW COLUMNS SHOULD BE PLACED AT CENTER OF EXISTING CONCRETE COLUMN. HOWEVER WE HAVE RECEIVED FIELD MEASUREMENT FOR THE CENTER OF EXISTING COLUMN.

AFTER INCORPORTAING THE ALL FIELD MEASUREMENT, WE HAVE PLACE MOST OF THE NEW COLUMNS AT CENTER OF EXISTING CONCRETE COLUMNS.

ADDITIONALLY,WE HAVE OFFSETTED THE SOME COLUMN FROM CENTER OF EXISTING CONCRETE COLUMN SINCE STRUCTURAL DRAWING GRAPHICALLY SHOWNS THE NEW COLUMN FROM EX.CONCRETE COLUMN CENTER PLEASE ADVISE TYPICAL FOR THIS PROJECT.



KEY PLAN

JB- Reviewed for Compliance

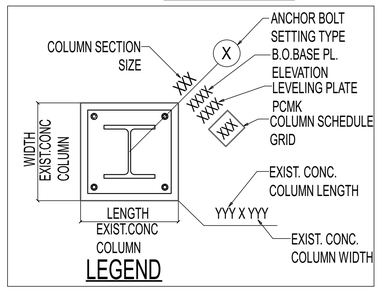

LEGEND

REVISIONS

REV#	DWN	DESCRIPTION	DATE
A	MNK	ISSUED FOR APPROVAL	Mar 1 2025

Q1

Arch, Please review clouded notes and advise.

THE INFORMATION NOTED HEREON THIS DRAWING IS THE PROPERTY OF STEEL FAB ENTERPRISES, INC. AND SHALL NOT BE USED WITHOUT WRITTEN CONSENT.

STEEL FAB ENTERPRISES, LLC
MISCELLANEOUS METALS FABRICATOR AND ERECTORS
623 BAUMGARDNER ROAD, LANCASTER, PA 17603
TEL. (717)464-0330 FAX (717)464-9464
WWW.STEELFABENTERPRISES.COM

PROJECT OWNER : 1250 MARYLAND AVENUE
PROJECT DESCRIPTION : 1250 MARYLAND AVENUE
PROJECT ADDRESS : 12
CONTRACTOR : BALFO
DRAWN BY : JSV
CHECKED BY : MNK
DWG DESCRIPTION : PA ANCHOR PLAN-(PHASE-1)(SEQ#2)

SK#07
One page
Date: 05-08-2025
