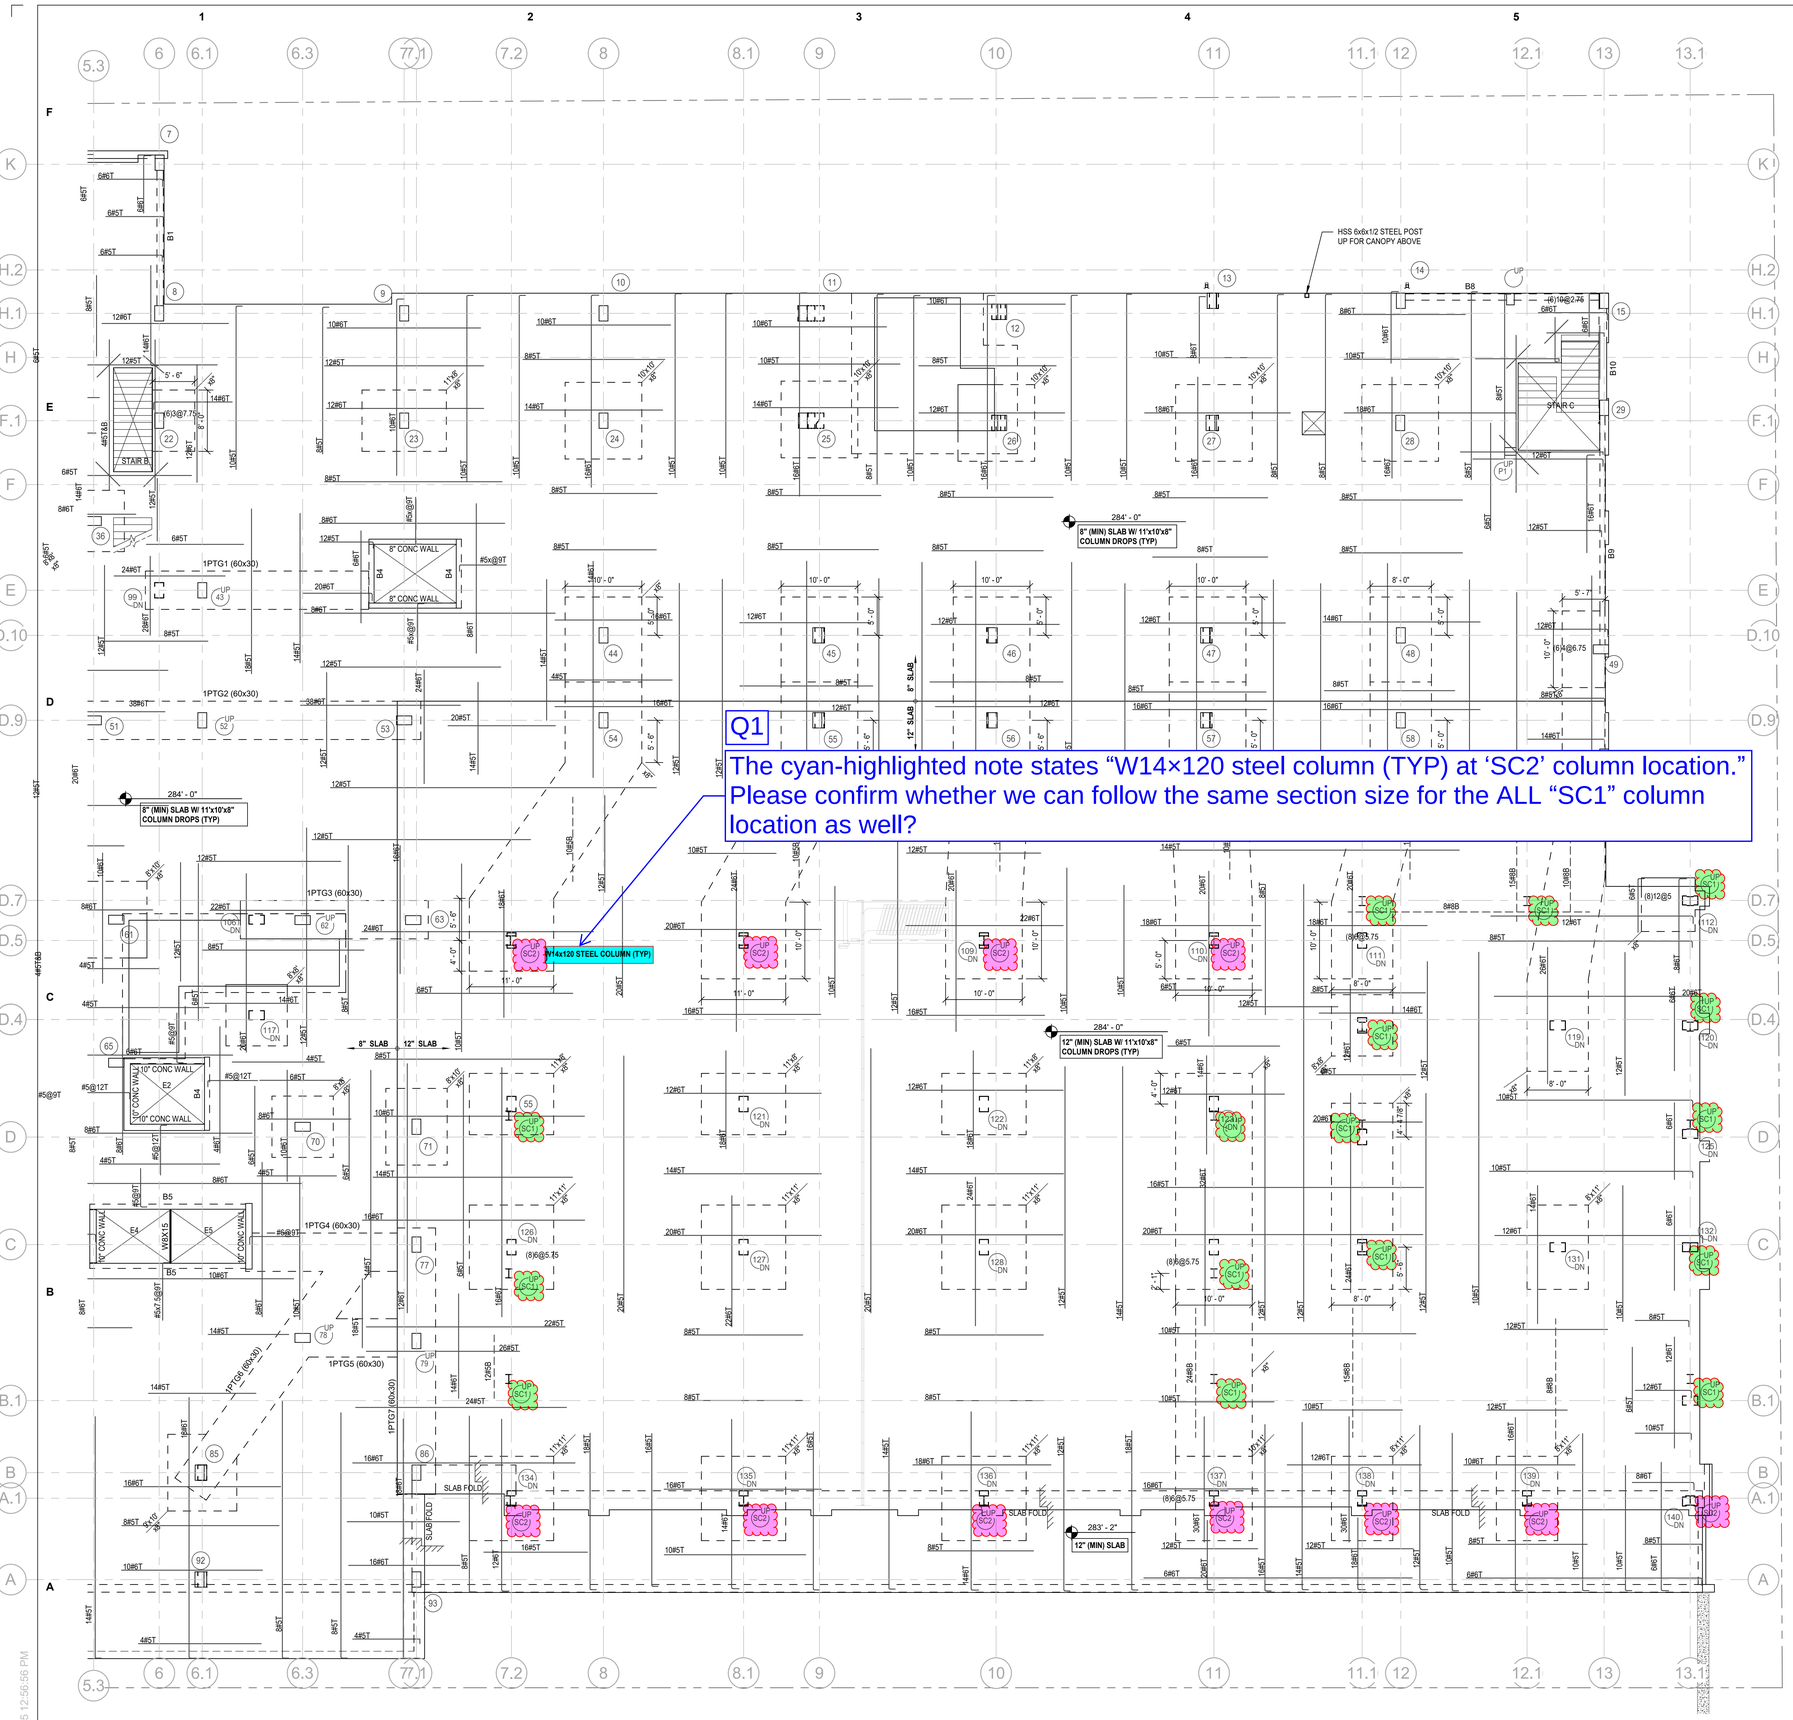

Q1

The cyan-highlighted note states "W14×120 steel column (TYP) at 'SC2' column location." Please confirm whether we can follow the same section size for the ALL "SC1" column location as well?

1 LEVEL 1 PLAN - PART B

1/8" = 1'-0"

SLAB NOTES

1. TOP OF SLAB ELEVATION SEE PLAN & ARCH DWGS.
2. FLOOR SLAB TO BE 8" (MIN) CONCRETE SLAB REINF W/ #5@10" BOT EACH WAY (GENERAL REINF) & 12" (MIN) CONCRETE SLAB REINF W/ #6@10" BOT EACH WAY (GENERAL REINF).
3. "T" DENOTES TOP BARS; "B" DENOTES BOTTOM BARS.
4. ALL REINF SHOWN ON PLAN SHALL BE IN ADDITION TO GENERAL REINF (U.N.O.)
5. PROVIDE 3/4" CONCRETE COVER FOR TOP & BOTTOM BARS IN SLAB (U.N.O.)
6. ALL REINF STEEL (TOP & BOTTOM) IN THE SLABS EXPOSED TO WEATHER (i.e. BALCONIES) TO BE EPOXY COATED AND SHALL HAVE 1 1/2" CONCRETE COVER FOR TOP BARS (U.N.O.)
7. 28 DAY CONCRETE STRENGTH OF SLAB, f'c= 5000 psi (NWC). TYPICAL (U.N.O.)
8. |(3)8SR| DENOTES SHEAR HEAD REINFORCING EACH WAY SEE TYPICAL DETAILS.
9. DESIGN LIVE LOAD = 100 psf AT LOBBIES, RESTAURANT, BALL ROOMS, OFFICE AND AMENITY
   = 450 psf AT FIRE ENGINE ACCESS
10. DO NOT REMOVE SHORING BELOW THE HANGING FLOOR SLAB WHICH ARE SUPPORTED BY THE HANGERS UNTIL THE FLOOR SLAB ABOVE ACHIEVE 28 DAYS STRENGTH.
11. DENOTES SLOPING COLUMN, SEE COLUMN SCHEDULE
12. DROP PANELS EXTEND 8" MINIMUM BELOW THE LOWEST SLAB ELEVATION AT EACH COLUMN U.N.O.

OUTERMOST LAYER

SK#04
11-pages
Date: 01-08-2026

FILLAT+ ARCHITECTURE
400 E. PRATT | SUITE 502 | BALTIMORE MD | 21202
Ph: 410.576.9310 | PFARC.COM

STRUCTURAL ENGINEER
TADJER-COHEN-EDELSON ASSOCIATES ,INC.
1109 SILVER SPRING ST., SUITE 510
SILVER SPRING, MD 20910
(301) 587-1820
12402000

MEP ENGINEER
ALLEN & SHARIFF ENGINEERING, LLC
7061 DEEPAGE DRIVE
COLUMBIA, MD 21045
(443) 545-7100

CIVIL ENGINEER
BOHLER
901 DULANEY VALLEY ROAD, SUITE 801
TOWSON, MD 21204
(410) 821-7900

INTERIOR DESIGNER
LOONEY & ASSOCIATES
20 N WACKER DR. SUITE 2010
CHICAGO, ILLINOIS 60606
(312) 329-0464

LANDSCAPE
EDSA
400 E. PRATT STREET, SUITE 502
BALTIMORE, MARYLAND 21202
(443)539-3350

TEHNOLOGY
MICHAEL RAISER ASSOCIATES, INC.
500 VALLEY ROAD SUITE 106
WAYNE, NJ 07470
(973)305-0011

FREDERICK CONFERENCE CENTER HOTEL

20 SOUTH CARROLL STREET
FREDERICK, MARYLAND, 21701

Copyright 2021 Fillat Architecture, Inc. All rights reserved

IFC SET

LEVEL 1 PLAN - PART II

PROJECT NO.:	13013
SCALE:	1/8" = 1'-0"
DATE:	12.19.2025

REVISIONS:

1	PRE-GMP	06.09.25
2	IFC SET	12.19.25

S103B

12/19/2025 12:56:56 PM

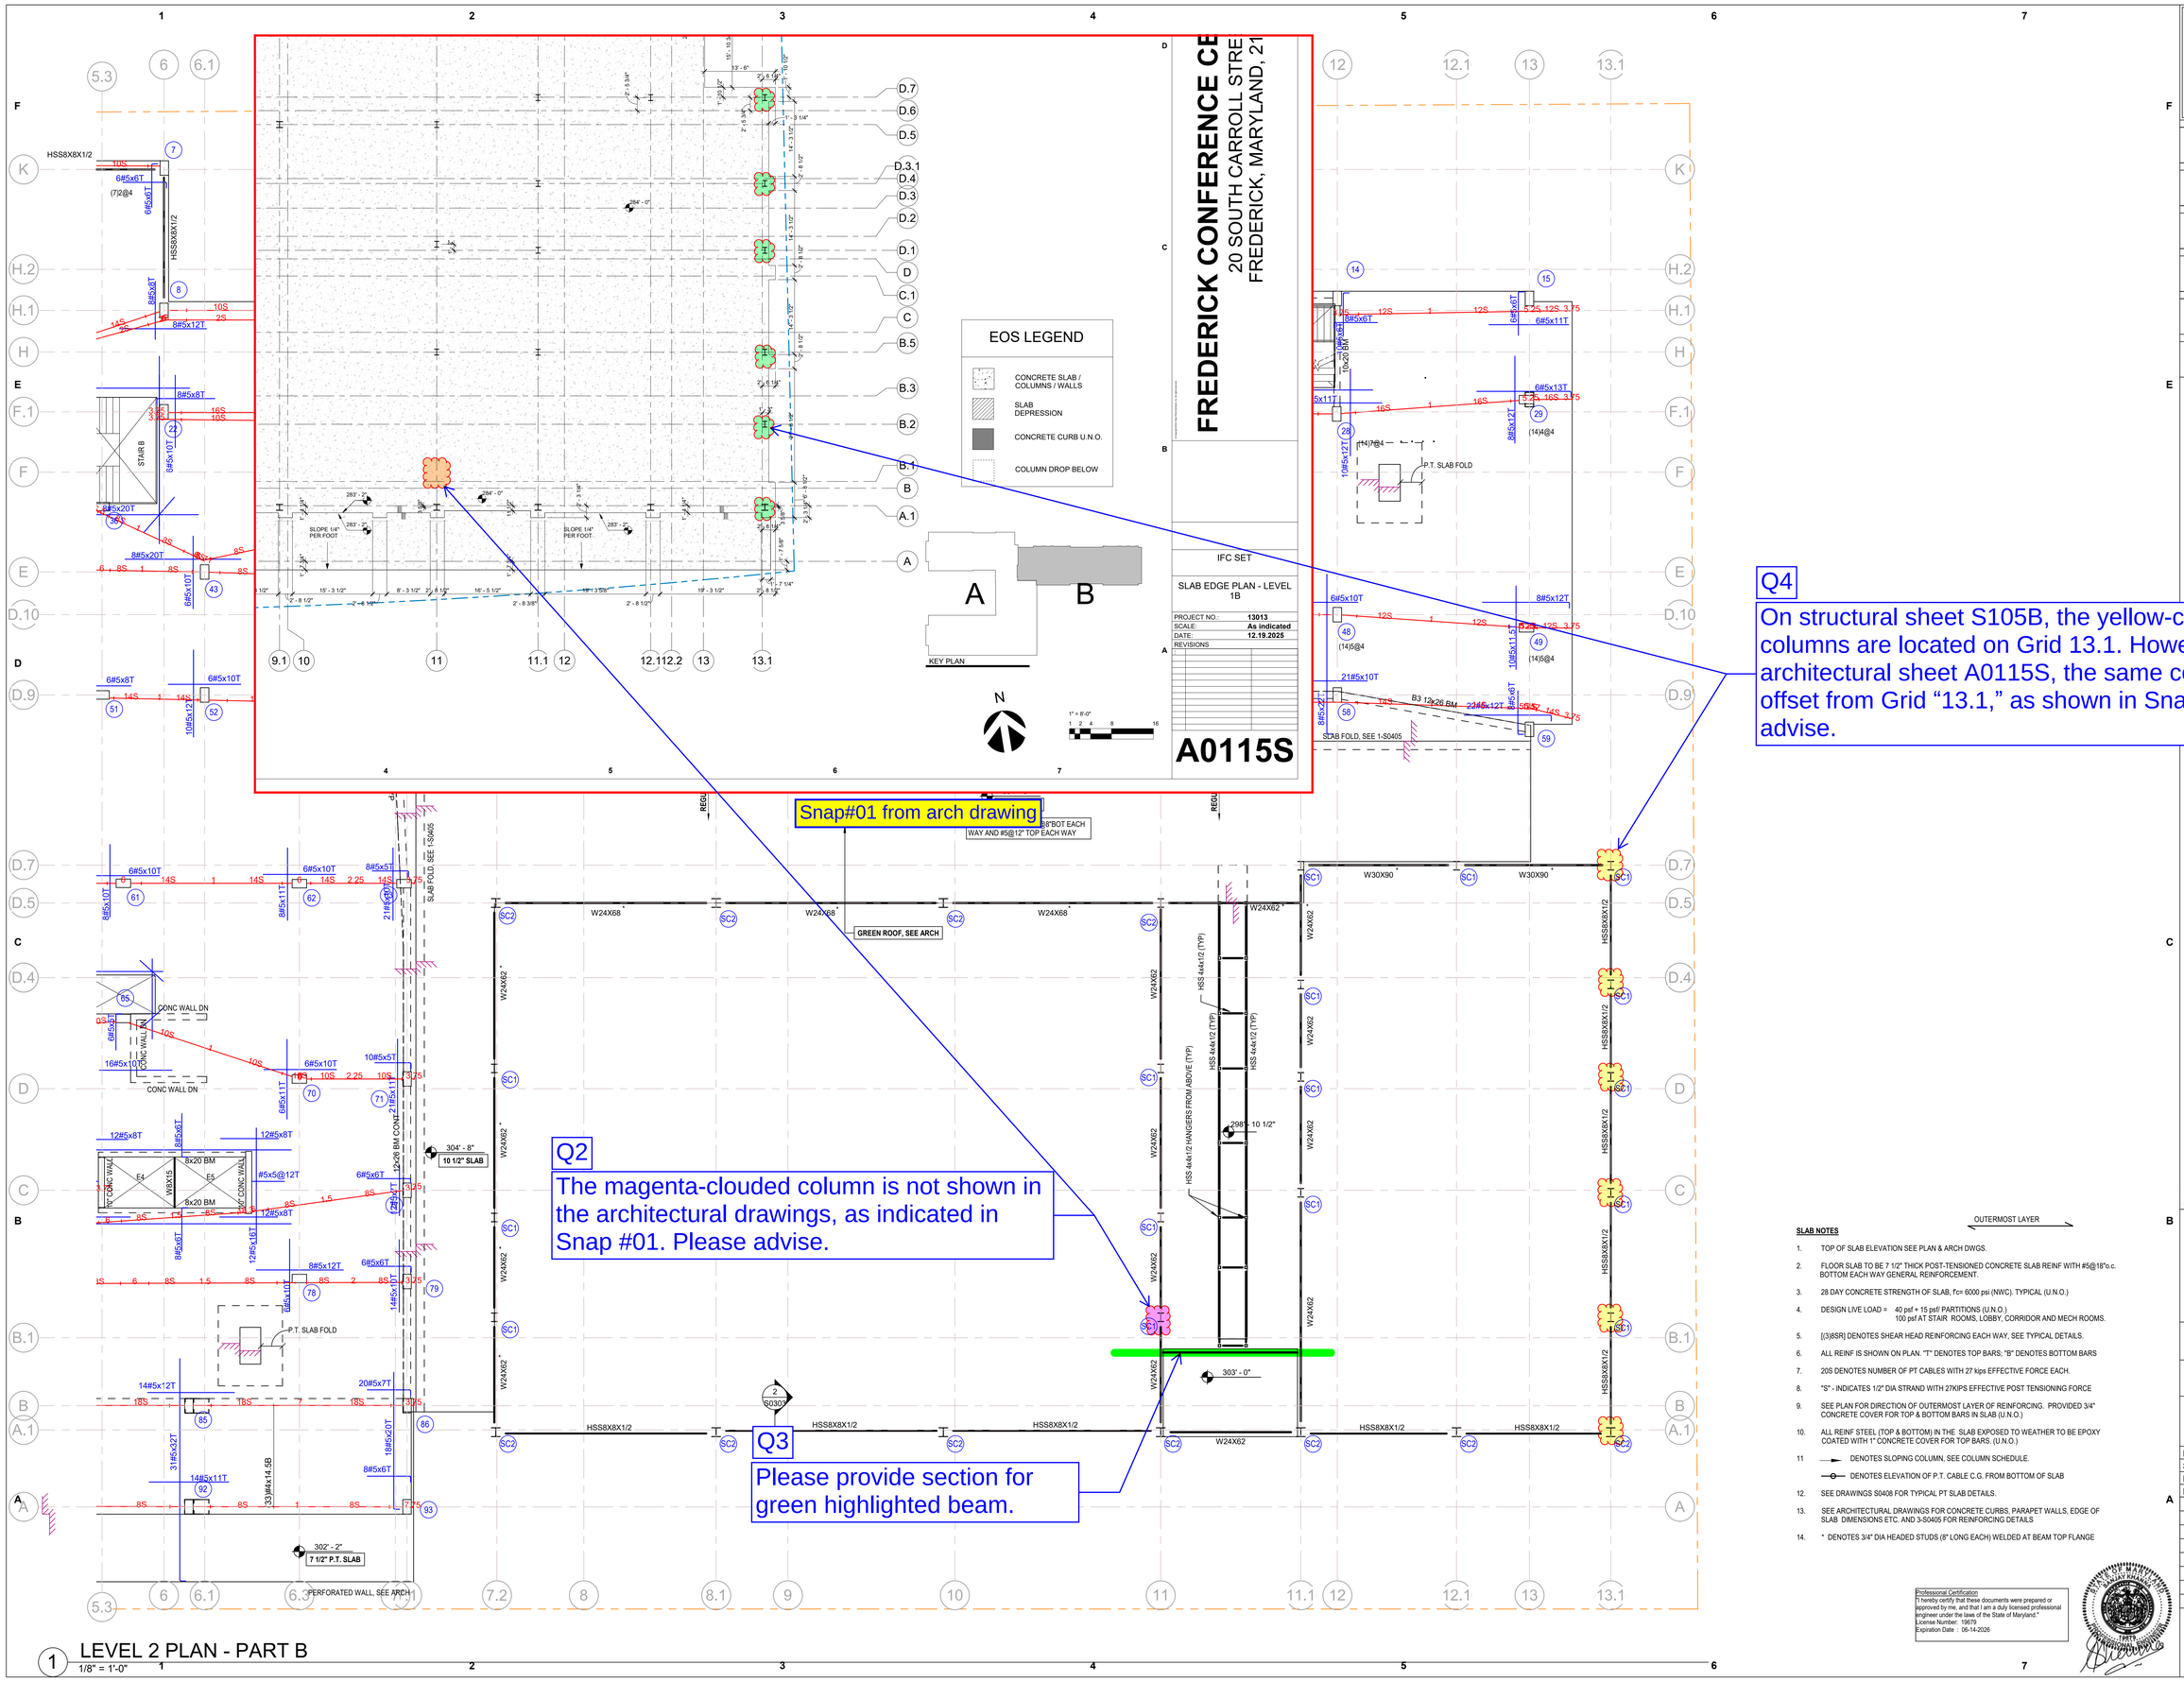

Q4

On structural sheet S105B, the yellow-clouded columns are located on Grid 13.1. However, on architectural sheet A0115S, the same columns are offset from Grid "13.1," as shown in Snap #01. Please advise.

1 LEVEL 2 PLAN - PART B
1/8" = 1'-0"

SLAB NOTES

1. TOP OF SLAB ELEVATION SEE PLAN & ARCH DWGS.
2. FLOOR SLAB TO BE 7 1/2" THICK POST-TENSIONED CONCRETE SLAB REINF WITH #5@18"o.c. BOTTOM EACH WAY GENERAL REINFORCEMENT.
3. 28 DAY CONCRETE STRENGTH OF SLAB, f'c= 6000 psi (NWC). TYPICAL (U.N.O.)
4. DESIGN LIVE LOAD = 40 psf + 15 psf// PARTITIONS (U.N.O.)
   100 psf AT STAIR ROOMS, LOBBY, CORRIDOR AND MECH ROOMS.
5. [(3)8SR] DENOTES SHEAR HEAD REINFORCING EACH WAY, SEE TYPICAL DETAILS.
6. ALL REINF IS SHOWN ON PLAN. "T" DENOTES TOP BARS; "B" DENOTES BOTTOM BARS
7. 20S DENOTES NUMBER OF PT CABLES WITH 27 kips EFFECTIVE FORCE EACH.
8. "S" - INDICATES 1/2" DIA STRAND WITH 27KIPS EFFECTIVE POST TENSIONING FORCE
9. SEE PLAN FOR DIRECTION OF OUTERMOST LAYER OF REINFORCING. PROVIDED 3/4" CONCRETE COVER FOR TOP & BOTTOM BARS IN SLAB (U.N.O.)
10. ALL REINF STEEL (TOP & BOTTOM) IN THE SLAB EXPOSED TO WEATHER TO BE EPOXY COATED WITH 1" CONCRETE COVER FOR TOP BARS. (U.N.O.)
11. DENOTES SLOPING COLUMN, SEE COLUMN SCHEDULE.
    DENOTES ELEVATION OF P.T. CABLE C.G. FROM BOTTOM OF SLAB
12. SEE DRAWINGS S0408 FOR TYPICAL PT SLAB DETAILS.
13. SEE ARCHITECTURAL DRAWINGS FOR CONCRETE CURBS, PARAPET WALLS, EDGE OF SLAB DIMENSIONS ETC. AND 3-S0405 FOR REINFORCING DETAILS
14. * DENOTES 3/4" DIA HEADED STUDS (8" LONG EACH) WELDED AT BEAM TOP FLANGE

OUTERMOST LAYER

Professional Certification
"I hereby certify that these documents were prepared or approved by me, and that I am a duly licensed professional engineer under the laws of the State of Maryland."
License Number: 19679
Expiration Date : 06-14-2026

FILLAT+ ARCHITECTURE
400 E. PRATT | SUITE 502 | BALTIMORE MD | 21202
Ph: 410.576.9310 | PFARC.COM

STRUCTURAL ENGINEER
TADJER-COHEN-EDELSON ASSOCIATES ,INC.
1109 SILVER SPRING ST., SUITE 510
SILVER SPRING, MD 20910
(301) 587-1820
12402000

MEP ENGINEER
ALLEN & SHARIFF ENGINEERING, LLC
7061 DEEPAGE DRIVE
COLUMBIA, MD 21045
(443) 545-7100

CIVIL ENGINEER
BOHLER
901 DULANEY VALLEY ROAD, SUITE 801
TOWSON, MD 21204
(410) 821-7900

INTERIOR DESIGNER
LOONEY & ASSOCIATES
20 N WACKER DR. SUITE 2010
CHICAGO, ILLINOIS 60606
(312) 329-0464

LANDSCAPE
EDSA
400 E. PRATT STREET, SUITE 502
BALTIMORE, MARYLAND 21202
(443)539-3350

TEHNOLOGY
MICHAEL RAISER ASSOCIATES, INC.
500 VALLEY ROAD SUITE 106
WAYNE, NJ 07470
(973)305-0011

FREDERICK CONFERENCE HOTEL
20 SOUTH CARROLL STREET
FREDERICK, MARYLAND

Copyright © 2025 Fillat Architecture, Inc. All rights reserved

IFC SET

LEVEL 2 PLAN - PART II

PROJECT NO.:	13013
SCALE:	1/8" = 1'-0"
DATE:	12.19.2025

REVISIONS:

1	PRE-GMP	06.09.25
2	IFC SET	12.19.25

S105B

12/19/2025 12:57:20 PM

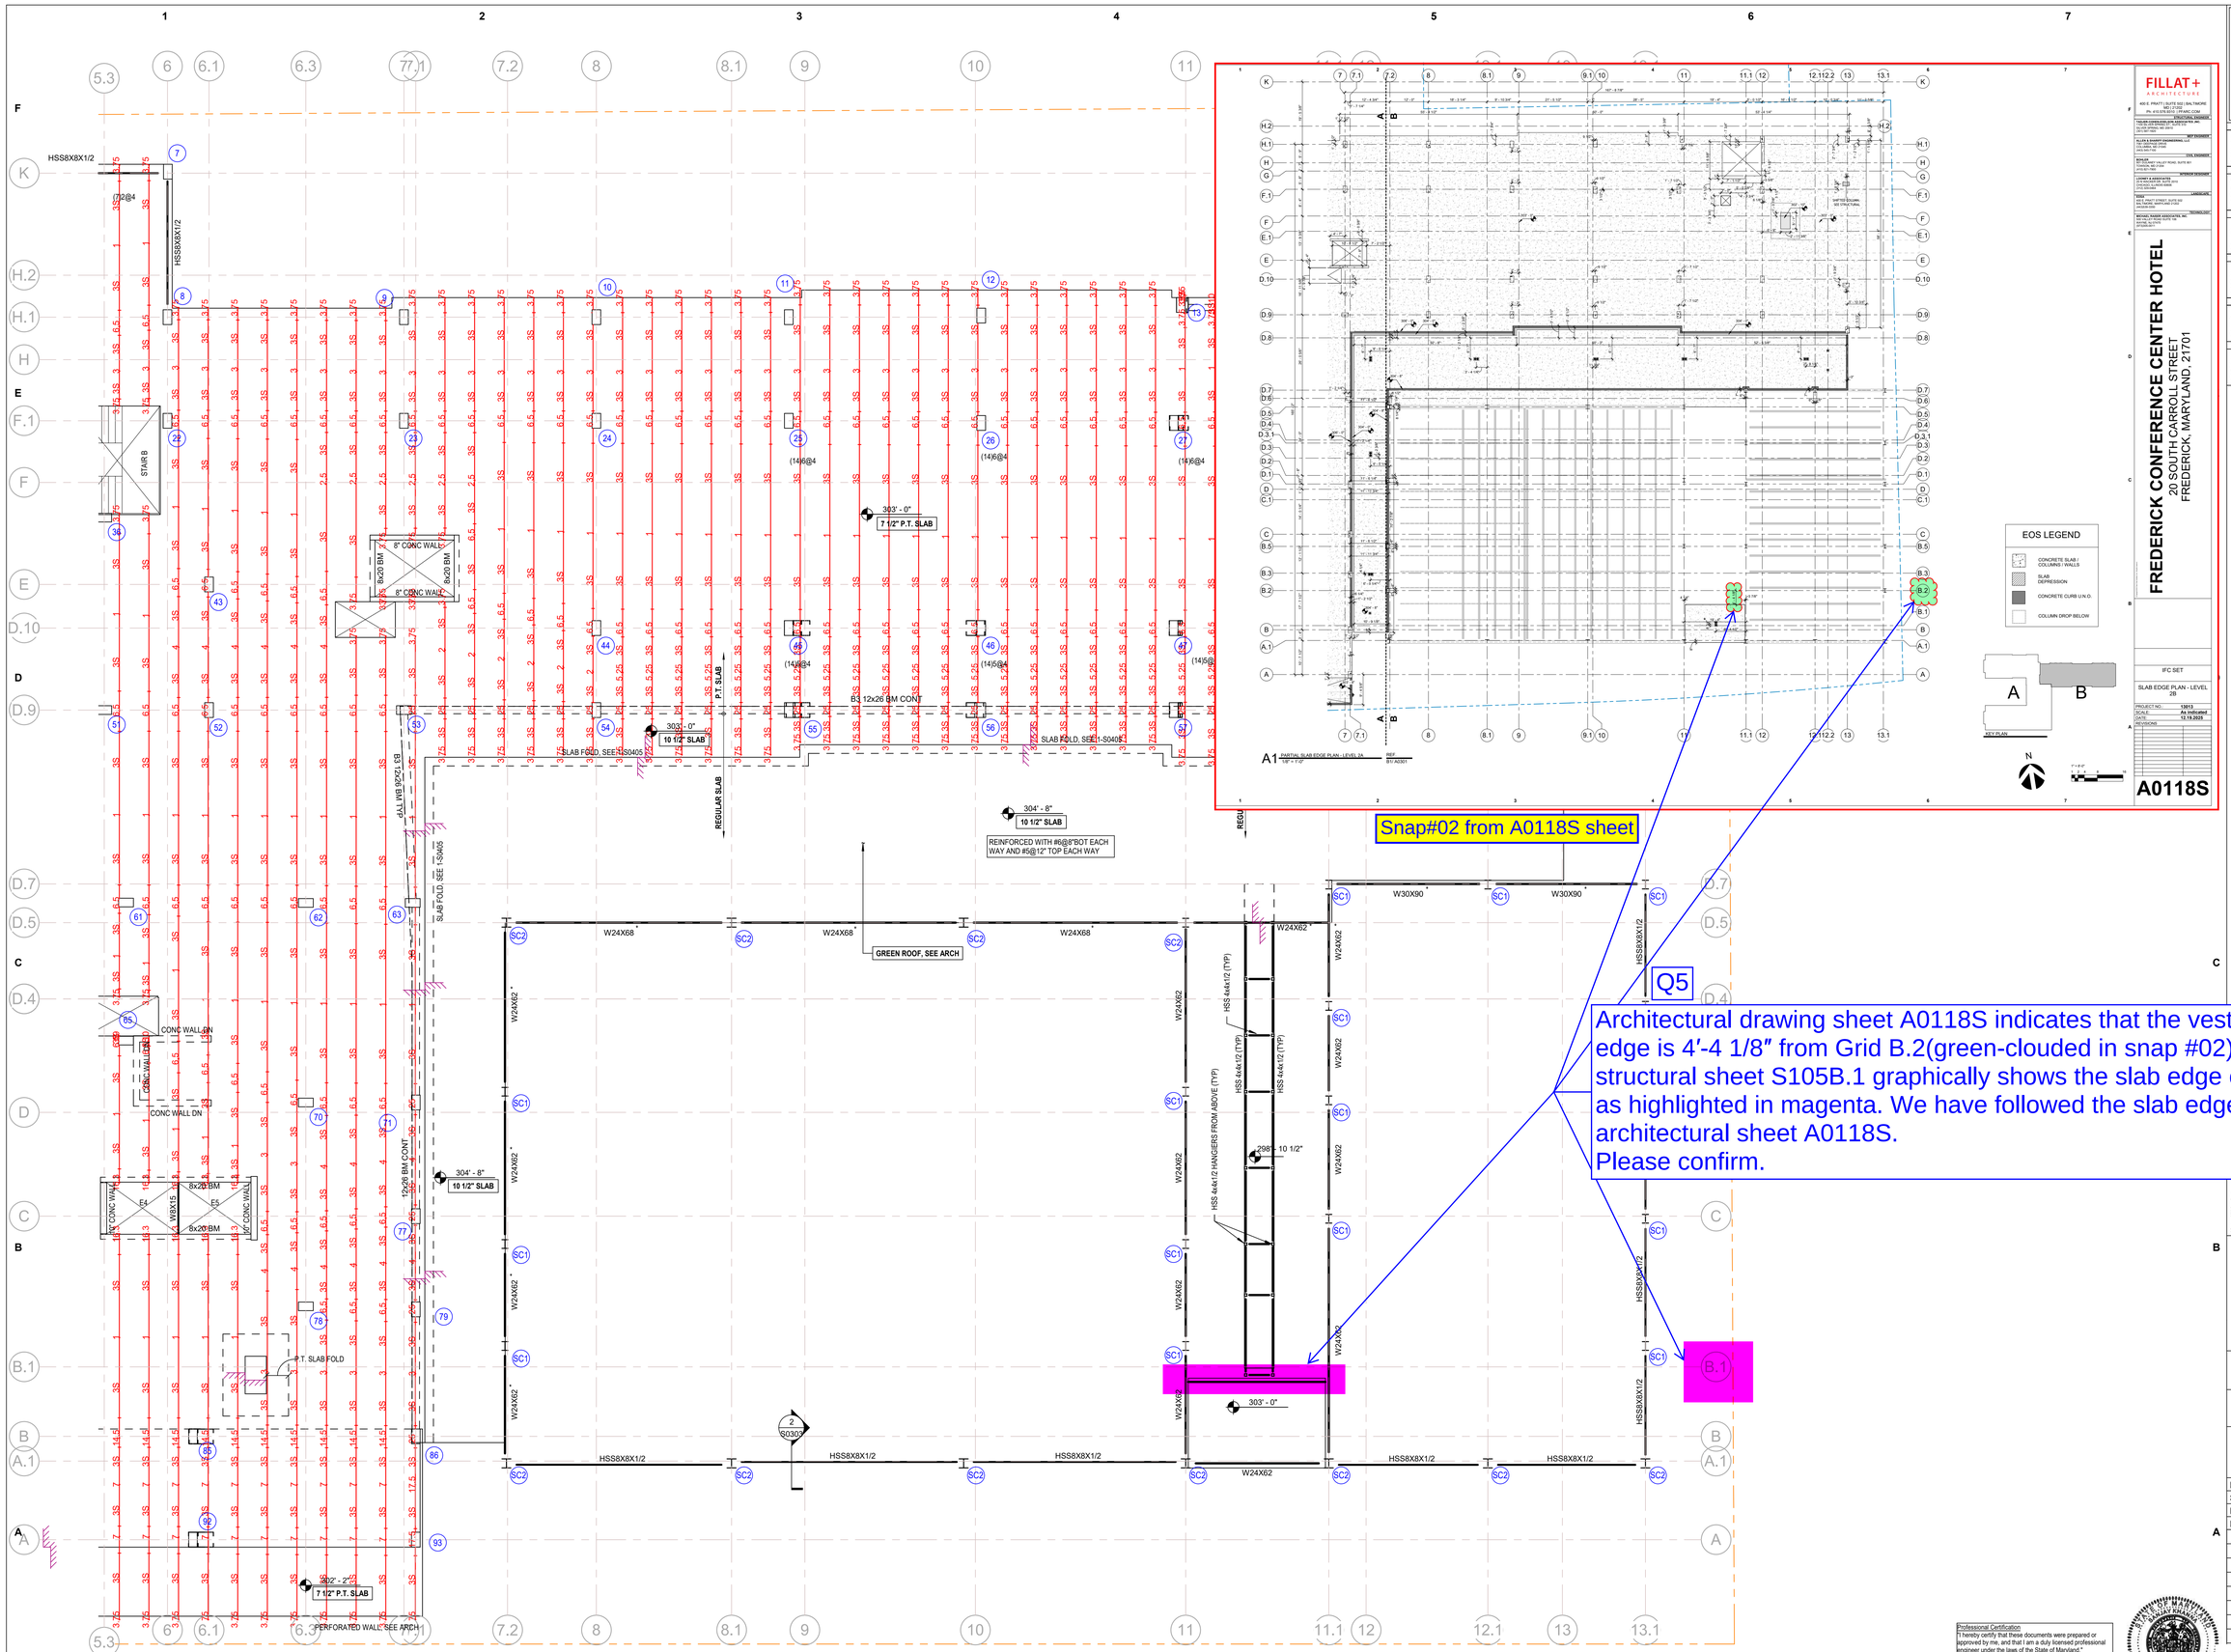

FILLAT+ ARCHITECTURE
400 E. PRATT | SUITE 502 | BALTIMORE MD | 21202
Ph: 410.576.9310 | PFARC.COM

STRUCTURAL ENGINEER
TADJER-COHEN-EDELSON ASSOCIATES ,INC.
1109 SILVER SPRING ST., SUITE 510
SILVER SPRING, MD 20910
(301) 587-1820
12402000

MEP ENGINEER
ALLEN & SHARIFF ENGINEERING, LLC
7061 DEERPAGE DRIVE
COLUMBIA, MD 21045
(443) 545-7100

CIVIL ENGINEER
BOHLER
901 DULANEY VALLEY ROAD, SUITE 801
TOWSON, MD 21204
(410) 821-7900

INTERIOR DESIGNER
LOONEY & ASSOCIATES
20 N WACKER DR. SUITE 2010
CHICAGO, ILLINOIS 60606
(312) 329-0464

LANDSCAPE
EDSA
400 E. PRATT STREET, SUITE 502
BALTIMORE, MARYLAND 21202
(443)539-3350

TEHNOLOGY
MICHAEL RAISER ASSOCIATES, INC.
500 VALLEY ROAD SUITE 106
WAYNE, NJ 07470
(973)305-0011

FREDERICK CONFERENCE CENTER HOTEL
20 SOUTH CARROLL STREET
FREDERICK, MARYLAND, 21701

IFC SET

LEVEL 2 PLAN - PART II (DIST)

PROJECT NO.:	13013
SCALE:	1/8" = 1'-0"
DATE:	12.19.2025

REVISIONS:

1	PRE-GMP	06.09.25
2	IFC SET	12.19.25

Professional Certification
"I hereby certify that these documents were prepared or approved by me, and that I am a duly licensed professional engineer under the laws of the State of Maryland."
License Number: 19679
Expiration Date : 06-14-2026

S105B.1

12/19/2025 12:57:23 PM

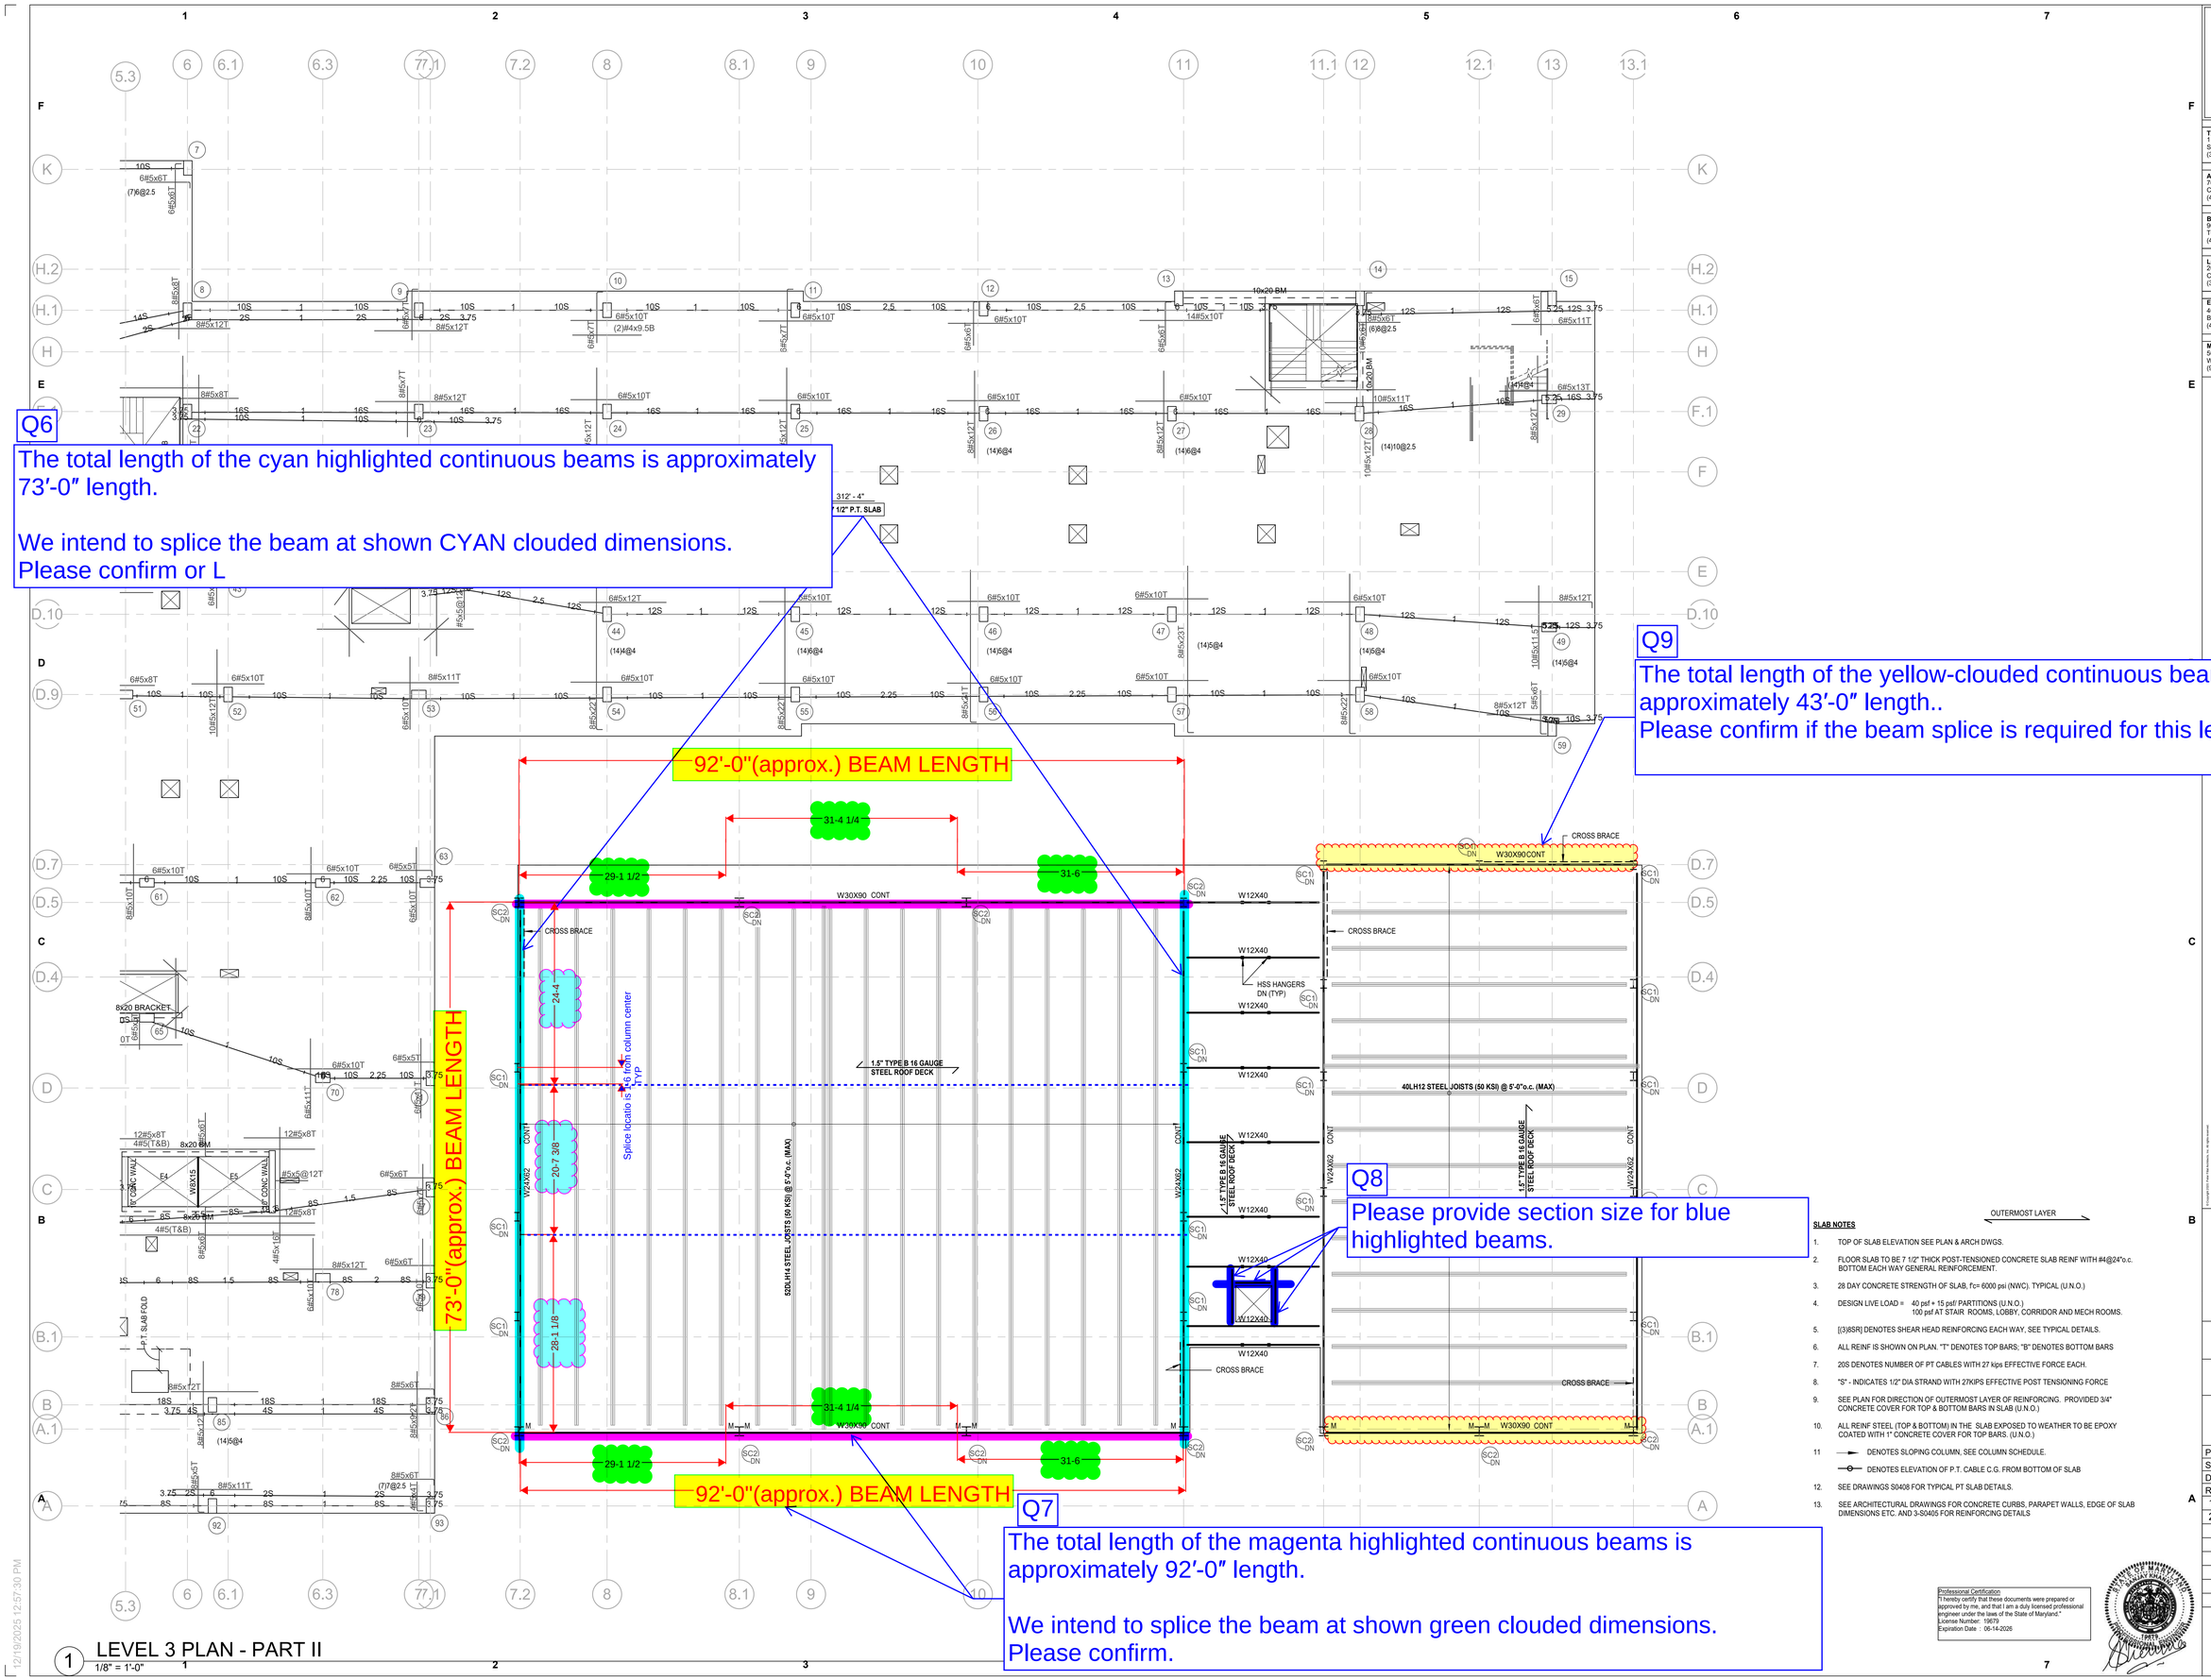

1 LEVEL 3 PLAN - PART II
1/8" = 1'-0"

SLAB NOTES

1. TOP OF SLAB ELEVATION SEE PLAN & ARCH DWGS.
2. FLOOR SLAB TO BE 7 1/2" THICK POST-TENSIONED CONCRETE SLAB REINF WITH #4@24"o.c. BOTTOM EACH WAY GENERAL REINFORCEMENT.
3. 28 DAY CONCRETE STRENGTH OF SLAB, f'c= 6000 psi (NWC). TYPICAL (U.N.O.)
4. DESIGN LIVE LOAD = 40 psf + 15 psf/ PARTITIONS (U.N.O.)
   100 psf AT STAIR ROOMS, LOBBY, CORRIDOR AND MECH ROOMS.
5. [(3)8SR] DENOTES SHEAR HEAD REINFORCING EACH WAY, SEE TYPICAL DETAILS.
6. ALL REINF IS SHOWN ON PLAN. "T" DENOTES TOP BARS; "B" DENOTES BOTTOM BARS
7. 20S DENOTES NUMBER OF PT CABLES WITH 27 kips EFFECTIVE FORCE EACH.
8. "S" - INDICATES 1/2" DIA STRAND WITH 27KIPS EFFECTIVE POST TENSIONING FORCE
9. SEE PLAN FOR DIRECTION OF OUTERMOST LAYER OF REINFORCING. PROVIDED 3/4" CONCRETE COVER FOR TOP & BOTTOM BARS IN SLAB (U.N.O.)
10. ALL REINF STEEL (TOP & BOTTOM) IN THE SLAB EXPOSED TO WEATHER TO BE EPOXY COATED WITH 1" CONCRETE COVER FOR TOP BARS. (U.N.O.)
11. DENOTES SLOPING COLUMN, SEE COLUMN SCHEDULE.
    DENOTES ELEVATION OF P.T. CABLE C.G. FROM BOTTOM OF SLAB
12. SEE DRAWINGS S0408 FOR TYPICAL PT SLAB DETAILS.
13. SEE ARCHITECTURAL DRAWINGS FOR CONCRETE CURBS, PARAPET WALLS, EDGE OF SLAB DIMENSIONS ETC. AND 3-S0405 FOR REINFORCING DETAILS

OUTERMOST LAYER

Professional Certification
I hereby certify that these documents were prepared or approved by me, and that I am a duly licensed professional engineer under the laws of the State of Maryland."
License Number: 19679
Expiration Date : 06-14-2026

FILLAT+ ARCHITECTURE
400 E. PRATT | SUITE 502 | BALTIMORE MD | 21202
Ph: 410.576.9310 | PFARC.COM

STRUCTURAL ENGINEER
TADJER-COHEN-EDELSON ASSOCIATES ,INC.
1109 SILVER SPRING ST., SUITE 510
SILVER SPRING, MD 20910
(301) 587-1820
12402000

MEP ENGINEER
ALLEN & SHARIFF ENGINEERING, LLC
7061 DEEPAGE DRIVE
COLUMBIA, MD 21045
(443) 545-7100

CIVIL ENGINEER
BOHLER
901 DULANEY VALLEY ROAD, SUITE 801
TOWSON, MD 21204
(410) 821-7900

INTERIOR DESIGNER
LOONEY & ASSOCIATES
20 N WACKER DR. SUITE 2010
CHICAGO, ILLINOIS 60606
(312) 329-0464

LANDSCAPE
EDSA
400 E. PRATT STREET, SUITE 502
BALTIMORE, MARYLAND 21202
(443)539-3350

TEHNOLOGY
MICHAEL RAISER ASSOCIATES, INC.
500 VALLEY ROAD SUITE 106
WAYNE, NJ 07470
(973)305-0011

FREDERICK CONFERENCE CENTER HOTEL
20 SOUTH CARR STREET
FREDERICK, MARYLAND, 21701

IFC SET

LEVEL 3 PLAN - PART II

PROJECT NO.:	13013
SCALE:	1/8" = 1'-0"
DATE:	12.19.2025

REVISIONS:

1	PRE-GMP	06.09.25
2	IFC SET	12.19.25

S106B

12/19/2025 12:57:30 PM

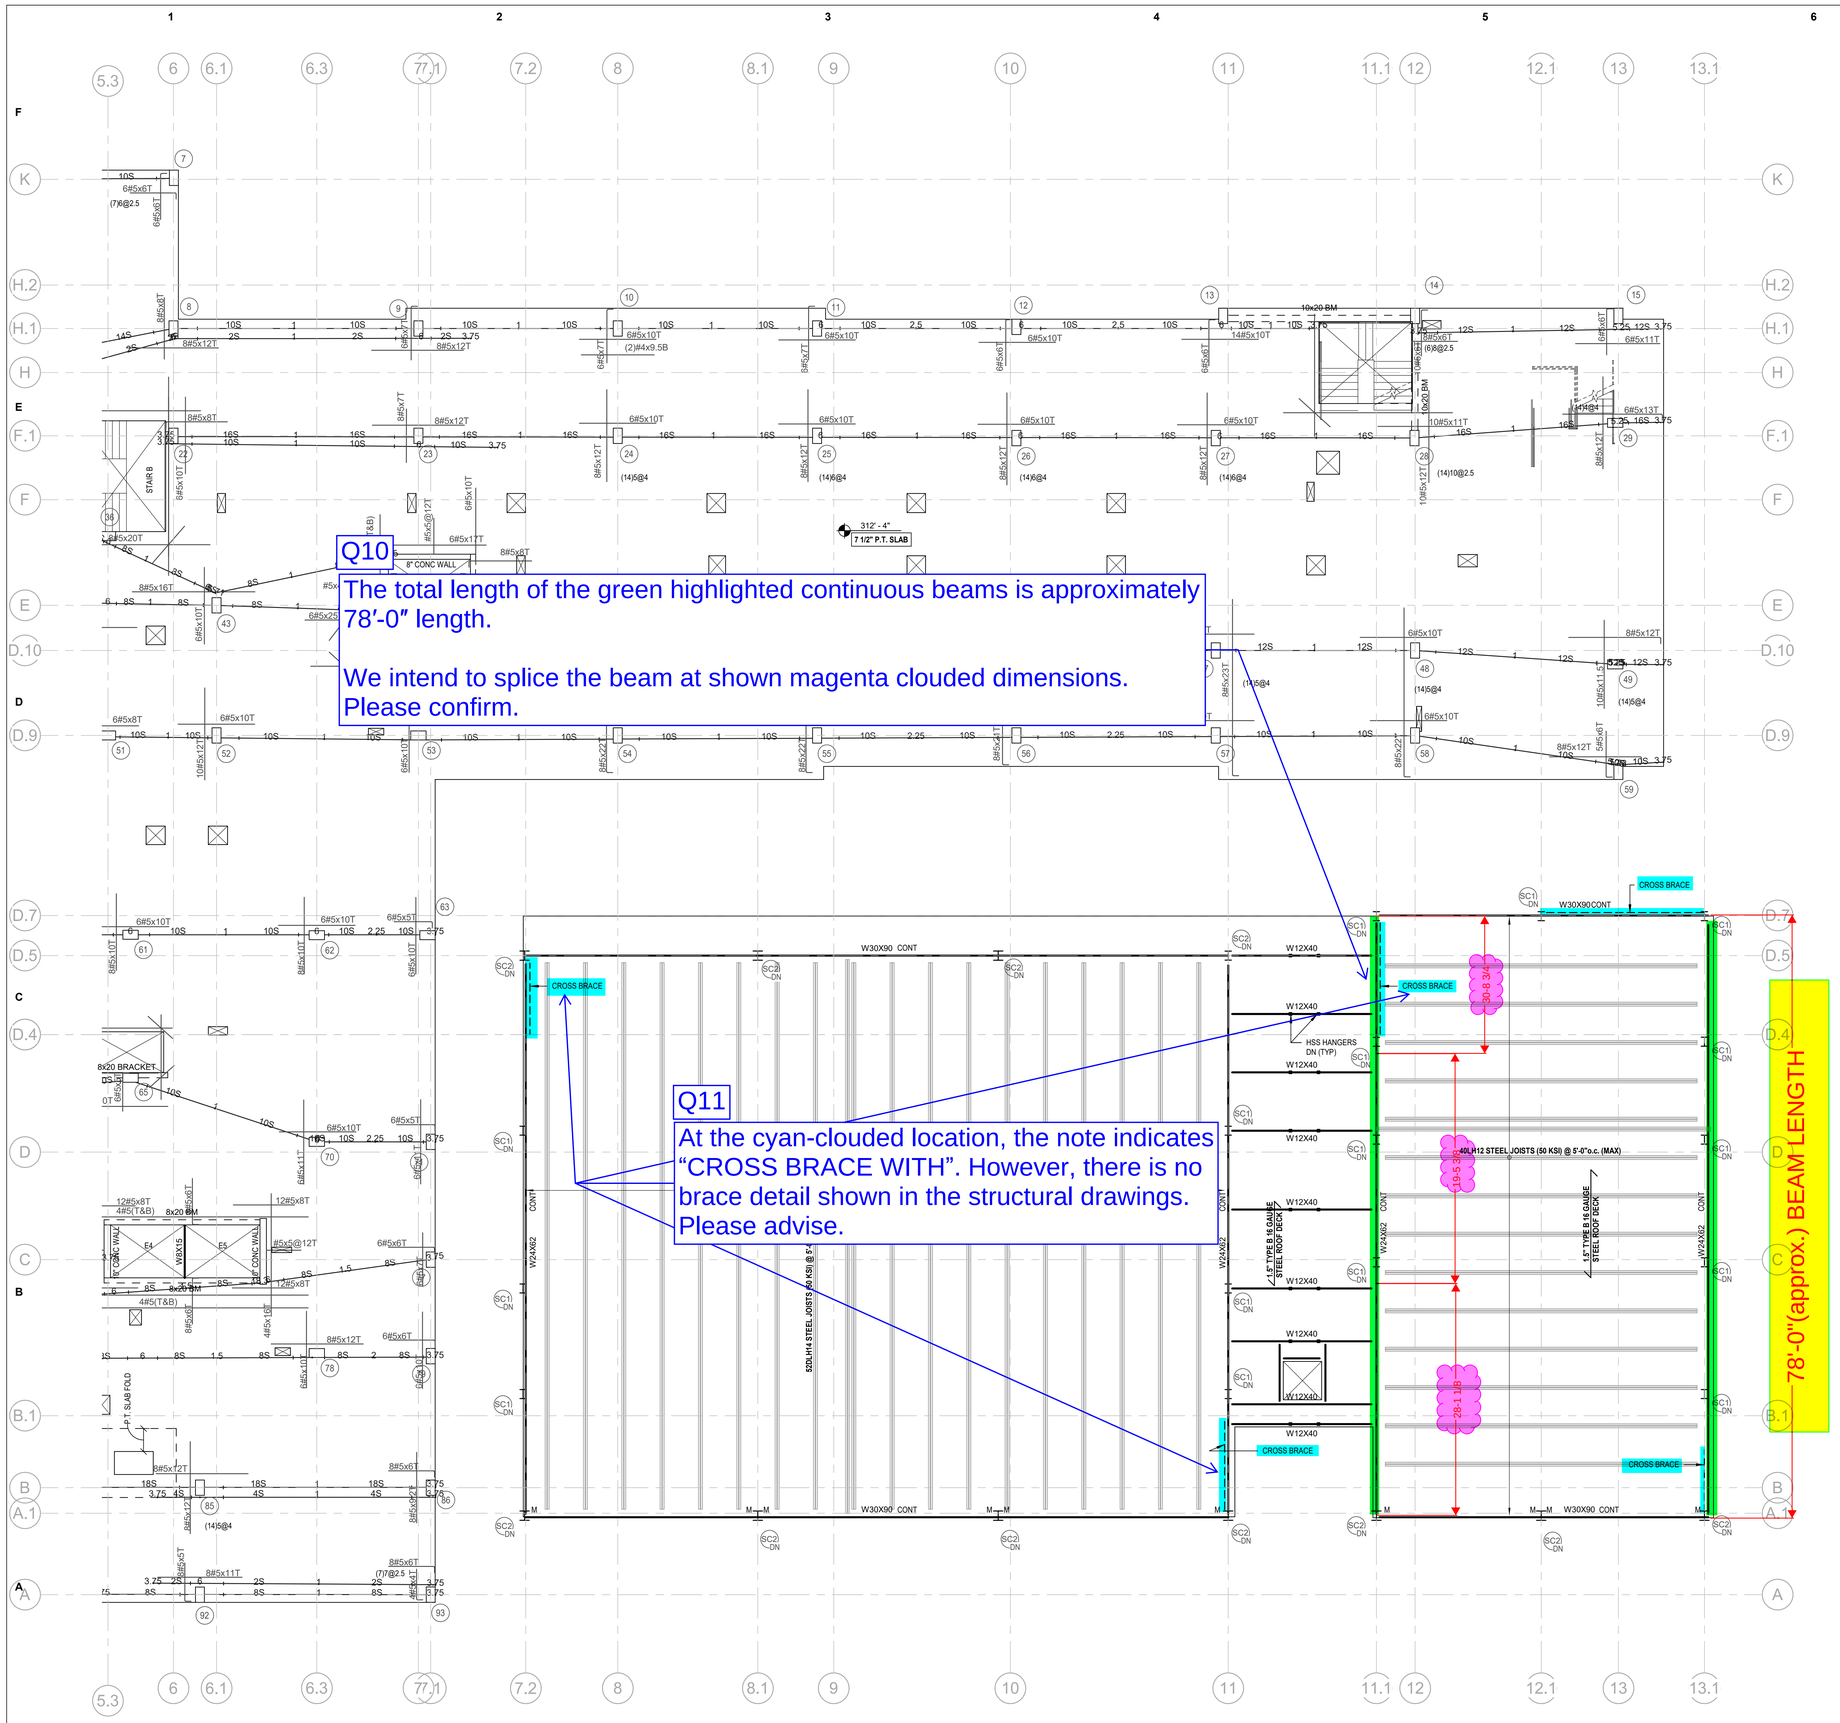

1 LEVEL 3 PLAN - PART II
1/8" = 1'-0"

SLAB NOTES

1. TOP OF SLAB ELEVATION SEE PLAN & ARCH DWGS.
2. FLOOR SLAB TO BE 7 1/2" THICK POST-TENSIONED CONCRETE SLAB REINF WITH #4@24"o.c. BOTTOM EACH WAY GENERAL REINFORCEMENT.
3. 28 DAY CONCRETE STRENGTH OF SLAB, f'c= 6000 psi (NWC). TYPICAL (U.N.O.)
4. DESIGN LIVE LOAD = 40 psf + 15 psf/ PARTITIONS (U.N.O.)
   100 psf AT STAIR ROOMS, LOBBY, CORRIDOR AND MECH ROOMS.
5. [(3)#5SR] DENOTES SHEAR HEAD REINFORCING EACH WAY, SEE TYPICAL DETAILS.
6. ALL REINF IS SHOWN ON PLAN. "T" DENOTES TOP BARS; "B" DENOTES BOTTOM BARS
7. 20S DENOTES NUMBER OF PT CABLES WITH 27 kips EFFECTIVE FORCE EACH.
8. "S" - INDICATES 1/2" DIA STRAND WITH 27KIPS EFFECTIVE POST TENSIONING FORCE
9. SEE PLAN FOR DIRECTION OF OUTERMOST LAYER OF REINFORCING. PROVIDED 3/4" CONCRETE COVER FOR TOP & BOTTOM BARS IN SLAB (U.N.O.)
10. ALL REINF STEEL (TOP & BOTTOM) IN THE SLAB EXPOSED TO WEATHER TO BE EPOXY COATED WITH 1" CONCRETE COVER FOR TOP BARS. (U.N.O.)
11. DENOTES SLOPING COLUMN, SEE COLUMN SCHEDULE.
    DENOTES ELEVATION OF P.T. CABLE C.G. FROM BOTTOM OF SLAB
12. SEE DRAWINGS S0408 FOR TYPICAL PT SLAB DETAILS.
13. SEE ARCHITECTURAL DRAWINGS FOR CONCRETE CURBS, PARAPET WALLS, EDGE OF SLAB DIMENSIONS ETC. AND 3-S0405 FOR REINFORCING DETAILS

OUTERMOST LAYER

Professional Certification
"I hereby certify that these documents were prepared or approved by me, and that I am a duly licensed professional engineer under the laws of the State of Maryland."
License Number: 19679
Expiration Date : 06-14-2026

FILLAT+ ARCHITECTURE
400 E. PRATT | SUITE 502 | BALTIMORE MD | 21202
Ph: 410.576.9310 | PFARC.COM

STRUCTURAL ENGINEER
TADJER-COHEN-EDELSON ASSOCIATES ,INC.
1109 SILVER SPRING ST., SUITE 510
SILVER SPRING, MD 20910
(301) 587-1820
12402000

MEP ENGINEER
ALLEN & SHARIFF ENGINEERING, LLC
7061 DEEPAGE DRIVE
COLUMBIA, MD 21045
(443) 545-7100

CIVIL ENGINEER
BOHLER
901 DULANEY VALLEY ROAD, SUITE 801
TOWSON, MD 21204
(410) 821-7900

INTERIOR DESIGNER
LOONEY & ASSOCIATES
20 N WACKER DR. SUITE 2010
CHICAGO, ILLINOIS 60606
(312) 329-0464

LANDSCAPE
EDSA
400 E. PRATT STREET, SUITE 502
BALTIMORE, MARYLAND 21202
(443)539-3350

TEHNOLOGY
MICHAEL RAISER ASSOCIATES, INC.
500 VALLEY ROAD SUITE 106
WAYNE, NJ 07470
(973)305-0011

FREDERICK CONFERENCE CENTER HOTEL

20 SOUTH CARROLL STREET
FREDERICK, MARYLAND, 21701

Copyright © 2025 Fillat Architecture, Inc. All rights reserved

IFC SET

LEVEL 3 PLAN - PART II

PROJECT NO.:	13013
SCALE:	1/8" = 1'-0"
DATE:	12.19.2025

REVISIONS:

1	PRE-GMP	06.09.25
2	IFC SET	12.19.25

S106B

12/19/2025 12:57:30 PM
